


Metro Gold Line

Foothill Extension Project

Monthly Project Status Report

February 2015

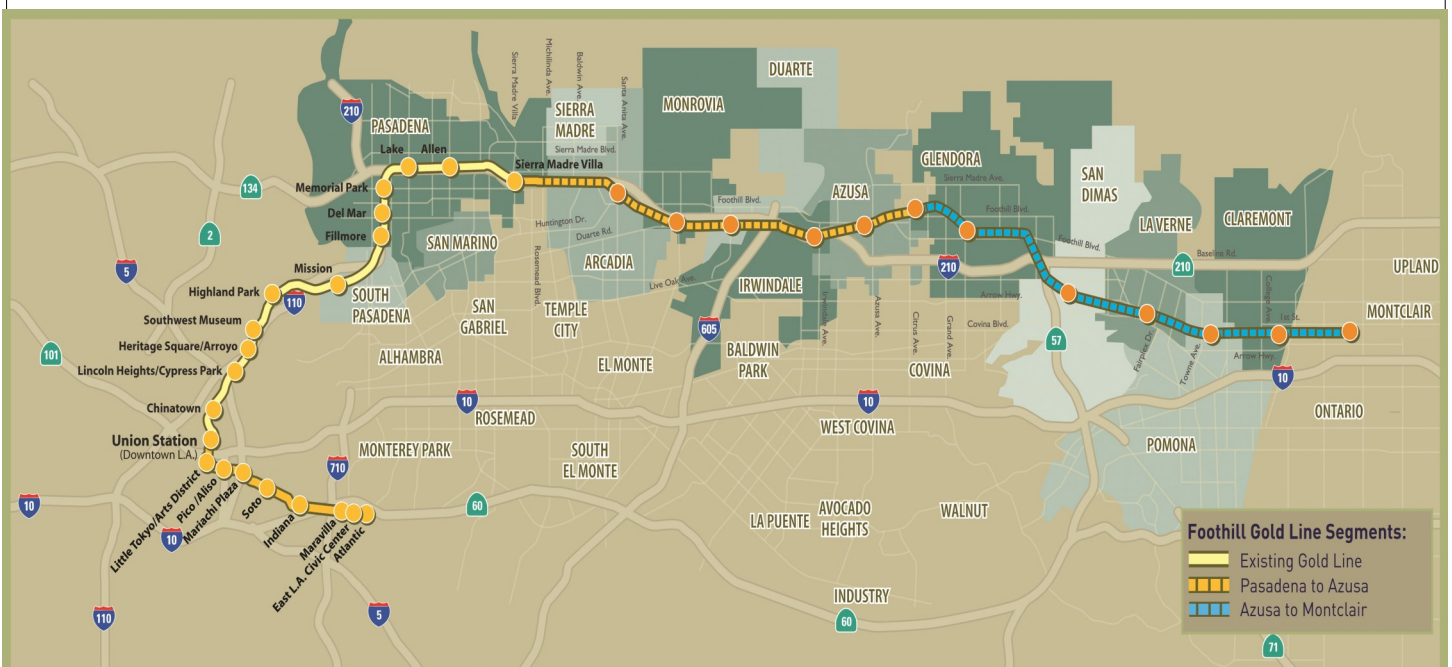

Foothill Gold Line

Connecting Los Angeles, the San Gabriel Valley and Inland Empire




TABLE OF CONTENTS

PHASE 2 FOOTHILL EXTENSION PROJECT STATUS

Project Description	3
Pasadena to Azusa Segment	4
Management Issues	4
Key Activities Completed This Period	5
Key Future Activities	6
Critical Path Schedule	7
Critical Path Float Trend	8
Alignment Contract Status	9
Alignment Construction Progress This Period	11
Facility Construction Progress This Period	12
Alignment Construction Progress Next Period	13
Facility Construction Progress Next Period	14
Alignment Construction Images	15
Alignment Change Management Log	17
Parking Facilities and Enhancements Contract Status	22
Parking Facilities and Enhancements Construction Images	24
Parking Facilities and Enhancements Change Management Log	26
Azusa to Montclair Segment	28
Financial Status	29

The Authority's mandate is to plan, design and construct a 37-mile light rail link between Downtown Los Angeles and Claremont. In addition, the San Bernardino Associated Governments (SANBAG) has requested that planning be extended one mile inside San Bernardino County to the City of Montclair and then possibly to Ontario Airport.

The Foothill Extension will be built in two segments to align effectively with projected cash flows and financial capacity constraints. The first segment is defined from the Sierra Madre Villa Station in Pasadena to the city of Azusa. Revenue service along this segment is planned for the year 2016. The second segment would include an extension from Azusa to the City of Montclair with revenue service projected for the year 2023 and the third segment, if applicable, will be comprised of an extension from Montclair to the Ontario Airport.

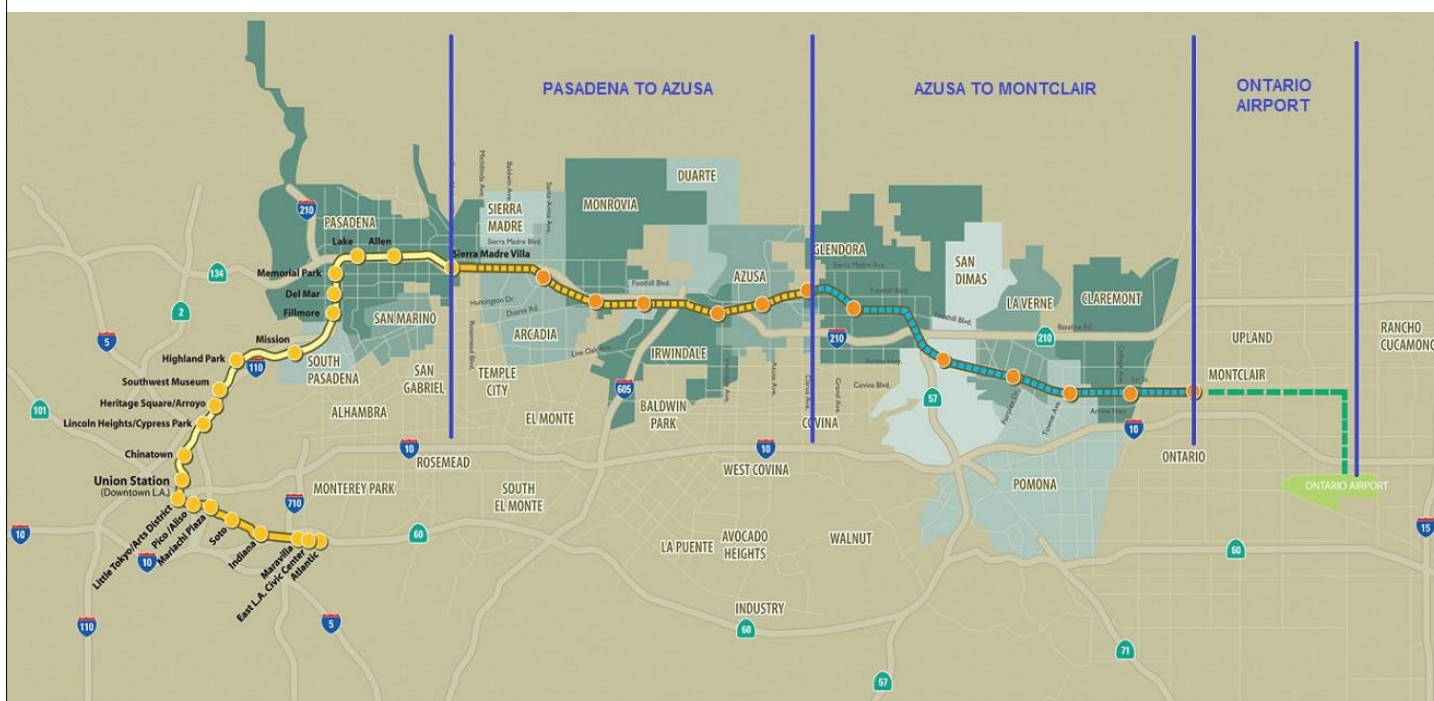

3



Pasadena to Azusa Segment

MANAGEMENT ISSUES

Metro Betterments

During the design process Metro staff have identified betterments that Metro staff would like to add to the project. Metro has provided a final disposition on all but a few items. Authority staff continues to work with Metro staff to resolve the remaining items.

TPSS Commissioning

The traction power substations (TPSS) provide equipment to transform utility power required for Light Rail Vehicle (LRV) propulsion, and then distribute that power to the LRVs via the overhead wires. Metro is responsible for purchasing the traction power substations. All TPSS have been delivered and set to date, however these deliveries were all behind schedule which proposed a potential to impact the project schedule. Authority staff coordinated with Metro and FTC to ensure minimal impact to the project, however the energization process will need to be finalized before schedule concerns are eliminated.



KEY ACTIVITIES COMPLETED THIS PERIOD

FTC reports the following SBE statistics for the month of November:

- Current SBE commitment: \$59,500,000
- SBE percent committed versus value of Project: 18.97%
- Overall Authority Project SBE goal: 16%

FTC reports the following approximate safety statistics to date:

- 1,876,115 total work hours performed by FTC, Mass Electric, and Subcontractors
- 13 recordable injuries reported to date
- 4 lost time injuries reported to date

Webcor reports the following DBE statistics for the month of November:

- Current DBE commitment: \$1,121,250
- DBE percent committed versus value of Project: 3.53%
- Overall Authority Project DBE goal: 2.3%

Webcor reports the following approximate safety statistics to date:

- 147,926 total work hours performed by Webcor and Subcontractors
- 1 recordable injuries reported to date
- 0 lost time injuries reported to date

The Baldwin and St. Joseph Traction Power Supply Substations were energized (4 remaining)

Continued placement of art and architectural elements at all stations

Continued track distressing throughout the alignment

Continued trackwork at the Gold Line Operations Campus (Campus)

Substantially completed OCS and Site Lighting Pole erection at the Campus and throughout the Alignment

Continued OCS wire runs in Segments 1, 2, 3, and 4

Continued installation of train control cases/bungalows and associated equipment

Continued installation of the communications system

Continued systems integration testing

Completed installation of Arcadia and Monrovia parking structure elevators

Continued installation of Azusa-Citrus parking structure elevators

Completed demolition of existing parking lot at Duarte parking lot site

Began second level deck pour of the Irwindale parking structure

Authority continued reviewing design submittals for Duarte, Azusa-Citrus and Irwindale structures



KEY FUTURE ACTIVITIES

Continue discussions with corridor cities regarding the project

Continue management of the Alignment contract, which will include oversight of construction activities and start-up activities

Continue to meet with Intermodal Parking Facilities and Enhancements Project contractor, Webcor Builders regarding design and construction of the Project

Complete construction of art and architectural elements at all stations

Complete OCS installation

Complete installation of train control system

Complete installation of communications system

Complete system integration tests

Finalize design for the following Parking Facilities: Azusa Citrus, Irwindale, and Duarte

Energize Los Robles, Soldano, Virginia, and Citrus Traction Power Supply Substations

Finalize the following property acquisitions:

- **Arcadia:**

1. Parcel 13010/1311 (Indiana St.) – To be vacated by the City of Arcadia.
2. Parcel 1401a (Huntington Dr. Aerial Easement) – To be conveyed by the City of Arcadia.
3. Parcel 1401b (Huntington Dr. Bridge Abutments) – To be conveyed by the City of Arcadia.
4. Parcel 1403 (99 N. Second Av.) – Setting Just Compensation 3/18/15.
5. Parcel 6009 (Huntington Dr. Bridge Abutments) – To be conveyed by the City of Arcadia.
6. Parcel 6010 (Huntington Dr. Bridge Abutments) – To be conveyed by the City of Arcadia.
7. Parcel 6011 (Huntington Dr. Bridge Abutments) – To be conveyed by the City of Arcadia.

- **Monrovia:**

1. Parcel 1601 (Encino Av.) – To be conveyed by the City of Monrovia.
2. Parcel 1903 (Monrovia Station) – To be conveyed by the City of Monrovia.
3. Parcel 21A12 (3M Parking Lot) – Waiting for legal description/as-builts.
4. Parcel 21A23 (Shamrock Trapezoid) – To be conveyed by the City of Monrovia.

- **Azusa:**

1. Parcel 3501 (1220 W. Foothill Blvd.) – Setting Just Compensation 3/18/15.




CRITICAL PATH SCHEDULE

Activity Name	OD	RD	AD	Start	Finish	Total Float																
							2012			2013			2014			2015			2016			
							Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	
REVENUE OPERATIONS DATE - CRITICAL PATH																						
RFP - LRV PROCUREMENT	375	0	557	18.Oct.10 08:00 A	26.Apr.12 15:00 A																	
LRV FABRICATION / DELIVER 15 VEHICLES	1353	307	912	17.Aug.12 07:00 A	18.Dec.15 15:00	244																
METRO - Pre-Revenue Operations - Phase 2A	60	60	0	19.Dec.15 07:00	16.Feb.16 15:00	244																
METRO - Project Schedule Contingency (2 Mo.)	44	44	0	17.Feb.16 07:00	31.Mar.16 15:00	244																
Phase 2A - Revenue Operations Date (ROD)	0	0	0		31.Mar.16 15:00*	244																
ALIGNMENT DELIVERY DATE - CRITICAL PATH																						
TPSS No.3 - INSTALLATION & TESTING	32	20	107	18.Sep.14 07:00 A	13.Mar.15 15:00	1																
SYSTEMS INTERGRATION TESTING - PHASE 1	185	130	49	09.Dec.14 07:00 A	28.Aug.15 15:00	1																
OCS - TESTING - SEGMENT 2	20	20	0	16.Mar.15 07:00	10.Apr.15 15:00	1																
OCS - TESTING - SEGMENT 4	20	20	0	13.Apr.15 07:00	08.May.15 15:00	1																
SYSTEMS INTERGRATION TESTING - PHASE 2	44	44	0	31.Aug.15 07:00	29.Oct.15 15:00	1																
C1135 - >>>SUBSTANTIAL COMPLETION - 1420 CD<<<	0	0	0		29.Oct.15 15:00*	2																
ALIGNMENT DELIVERY DATE - SECONDARY - CRITICAL PATH																						
DUARTE STATION - COMMUNICATIONS INSTL / TEST	44	10	109	16.Sep.14 07:00 A	27.Feb.15 15:00	1																



CRITICAL PATH FLOAT TREND

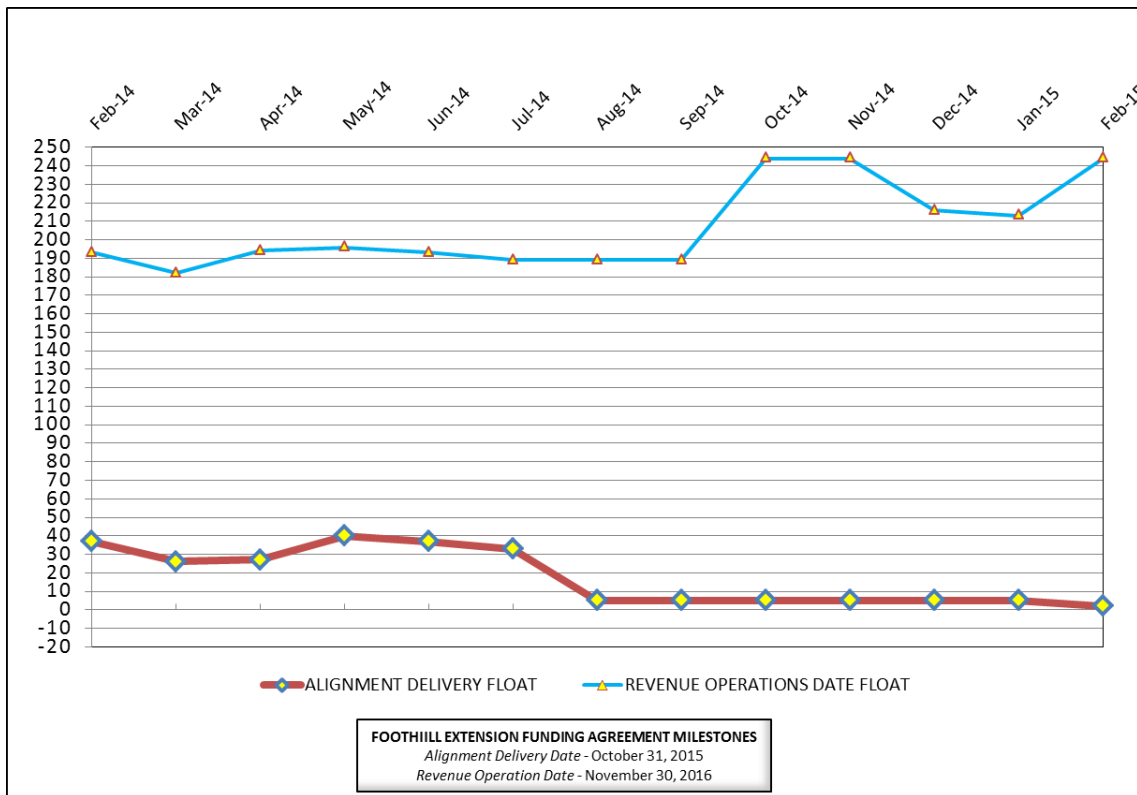

Revenue Operations Date Critical Path - (244 Calendar Days)

This period, Metro revised the procurement and installation schedule for the Rail Operations Center (ROC) upgrade. As a result, the critical path shifted from the ROC upgrade to the P3010 LRV procurement. At this time, Metro is forecasting the delivery of the 15th vehicle by December 2015. The critical path continues through Pre-Revenue Operations, which is expected to be completed by February 16, 2016. As a result, the float on this path improved one (1) month from the previous period. The Revenue Operations Date (ROD) is projected to be complete by March 31, 2016, which is eight (8) months ahead of the Funding Agreement Milestone date of November 30, 2016.

Alignment Delivery Date Critical Path - (2 Calendar Days / 1 Work Day)

This period, both the Traction Power Substation (TPSS) No.3 'Los Robles' installation/testing and the Duarte Station Communications installation/testing have slipped. As a result, both locations have become critical and are both on parallel critical paths. Upon the completion of TPSS No.3 'Los Robles', Segment 2 will be ready to begin testing the Overhead Contact System (OCS). The critical path continues through OCS testing in Segment 4, which will be followed by system integration testing. On the parallel path, after the Duarte Station communications LFAT testing is completed, the systems integration testing can begin. Upon the conclusion of systems integration testing, the alignment will be available for Metro to complete Pre-Revenue Operations.

Other elements of construction work, which are in progress and near critical are Segments 2 & 4 OCS installations; Irwindale Parking Structure, Irwindale Station mechanical/electrical/finish installations; Duarte parking lot; Citrus Station mechanical/electrical/finish installations; Citrus Parking Structure and the Maintenance & Operations Campus.

Project Float

The project float for the Revenue Operations Date is 244 days. The critical activities on this path are on schedule to meet the Target Revenue Operations Date of November 2016. The Alignment Delivery Date float value slipped 3 days this period. The Alignment Delivery Date is currently 2 days ahead the October 31, 2015 deadline.



Description: Alignment Design / Build

Status: February 15, 2015

Contract No.: C1135

Contractor: Foothill Transit Constructors (Kiewit-Parsons J.V.)

Progress Completed This Period

Design

- Submit 100% Design - Irwindale Ave. / First St.
- Submit - Preventative Maintenance Task Analysis Plan
- Submit AFC Design - Citrus Communications Book of Plans
- Submit AFC Design - Monrovia Comm. Book of Plans
- Submit - Spare Parts List
- Submit - Tree Survey Report

Construction

- See "Construction Progress This Period"

Activities Planned Next Period

Design

- Submit AFC Design - Alameda Communications Book of Plans
- Submit AFC Design - Duarte Communications Book of Plans
- Submit AFC Design - M&O Communications Book of Plans
- Submit AFC Design - Irwindale Communications Book of Plans
- Submit AFC Design - Parking Struc. Communications Book of Plans
- Submit AFC Design - Irwindale Ramp

Construction

- See "Construction Progress Next Period"

Areas of Concern

- **Irwindale Parking Communications** - The C1150 Design-Build Contractor is currently mitigating the shoring and utility delays, which impacted the start to the Irwindale pump station and MSE wall. The delays could potentially impact the C1135 Design-Build Contractor if the access to the parking facility is not granted by May 2015. The C1150 Design-Build Contractor has re-sequenced the Irwindale parking structure schedule and has plans to accelerate the concrete and elevator hoistway activities in order to provide access by the required date. At this time, the C1150 Design-Build Contractor is successful with the implementation and the execution of the mitigation plan. Currently, the parking facility is on target for access by May 2015.

Areas of Concern (Continued)


**Description:** Alignment Design / Build**Status:** February 15, 2015**Contract No.:** C1135**Contractor:** Foothill Transit Constructors (Kiewit-Parsons J.V.)**Cost Summary:**

	Million(s)
CONTRACT	
Contract Award Value:	485.9
Executed Change Orders:	17.8
Current Contract Value:	503.7
Potential Change Orders:	1.9
Current Forecast:	505.5
Earned Value/Actual Cost	440.4
AUTHORIZATION FOR EXPENDITURE	
Budget	514.5
Commitment	503.7
Balance	9.0

Cost Assessment:

This period the Contract forecast increased \$346 Thousand. The major increase was due to the following: CO 135 - Virginia TPSS Access for Delivery, and CO 136 - Rail Profile Grinding, PCO 094 - Add Pavers Duarte Sta. West Ramp, PCO 105 - M&O Fire Alarm System, and PCO 106 - 1st/Santa Clara Noise Mitigations. The overall increase to the cost forecast was offset by a decreases due to the cancelation PCO 095.01 - M&O Paint Poles & Fixtures and reductions in the final negotiated price of CO 133 - Irwindale Ramp Signs.

The Design-Build Contractor has earned 440.4 Million and is currently 90.0% complete. The progress is currently 7.8% behind the early planned curve, which is due to OCS installation progress in Segments 2, 4 and M&O. In addition train control installation progress at Segment 2, and 4 is also behind the planned progress curve.

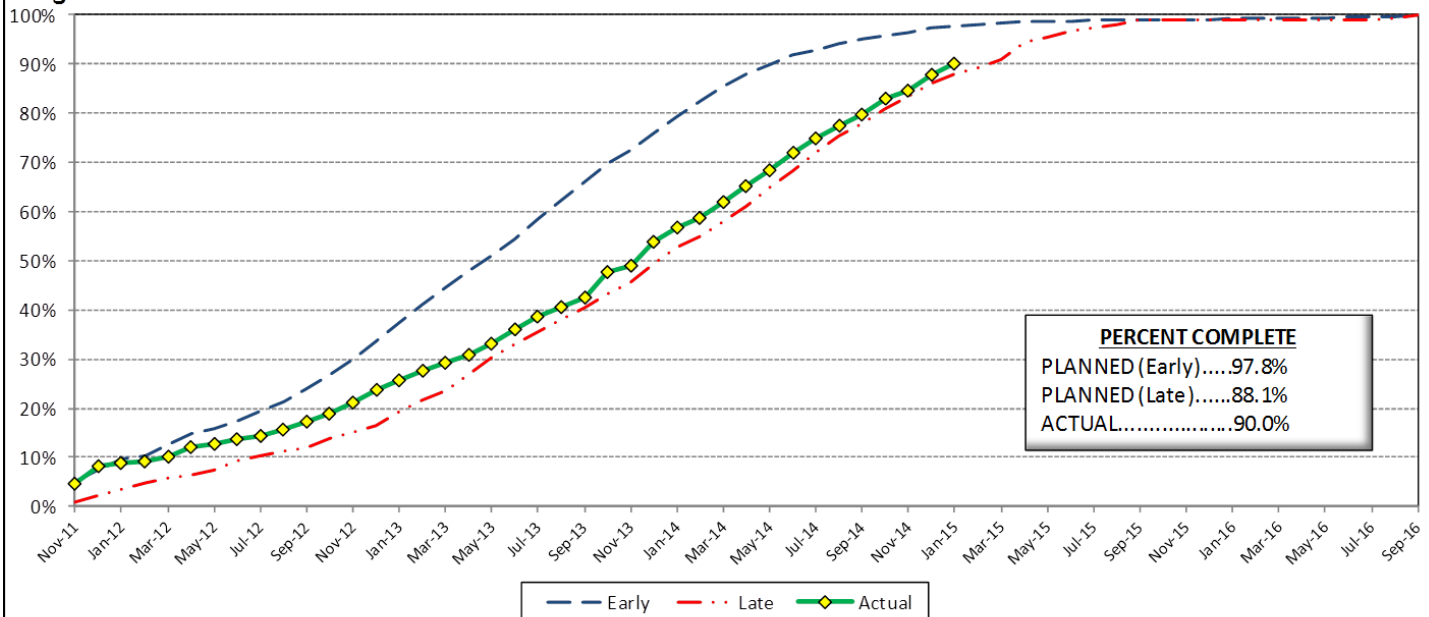Progress Curve**Schedule Summary:**

Contract Award:	07/27/11
Interim Notice to Proceed (INTP) :	11/03/11
Original Contract Duration:	1,780 Calendar Days
Current Contract Duration:	1,780 Calendar Days
Elapsed Time from NTP:	1,200 Calendar Days

Contract Milestones

Milestones	Description	Original Contract	Current Contract	Forecast	Variance
1	Substantial Completion	09/23/15	09/23/15	10/29/15	(36)
2	Punchlist Complete	06/19/16	06/19/16	07/25/16	(36)
3	Final Completion	09/17/16	09/17/16	10/23/16	(36)
4	Access - IFS Br.	12/15/12	12/15/12	12/15/2012 A	0
5	Test Track Complete	03/27/15	03/27/15	04/22/15	(26)
6	Colorado Br. Demo Complete	02/01/12	02/01/12	6/15/2012 A	(135)


Schedule Assessment:

With the progress continuing to trend at the rate of the late progress curve, activities in all Segments continue to approach near critical. The Design-Build Contractor continues to meet the requisite use of resources in order to meet the critical elements of the schedule. At this time, the primary activities which are critical or near critical by Segment are as follows: Segment 1 - Train Control Installation & TPSS commissioning, Segment 2 - OCS Installation, Segment 3 - Duarte Station Communications LFAT Testing, Segment 4 - OCS Installation, and Irwindale Station mechanical/electrical & finishes. Maintenance & Operations Facility - train control installation & testing, OCS Installation, Main Building Finishes, Car Wash Building.

The Test Track Completion is forecast to be available on April 22, 2015, which is 26 days behind the target date.



ALIGNMENT CONSTRUCTION PROGRESS THIS PERIOD

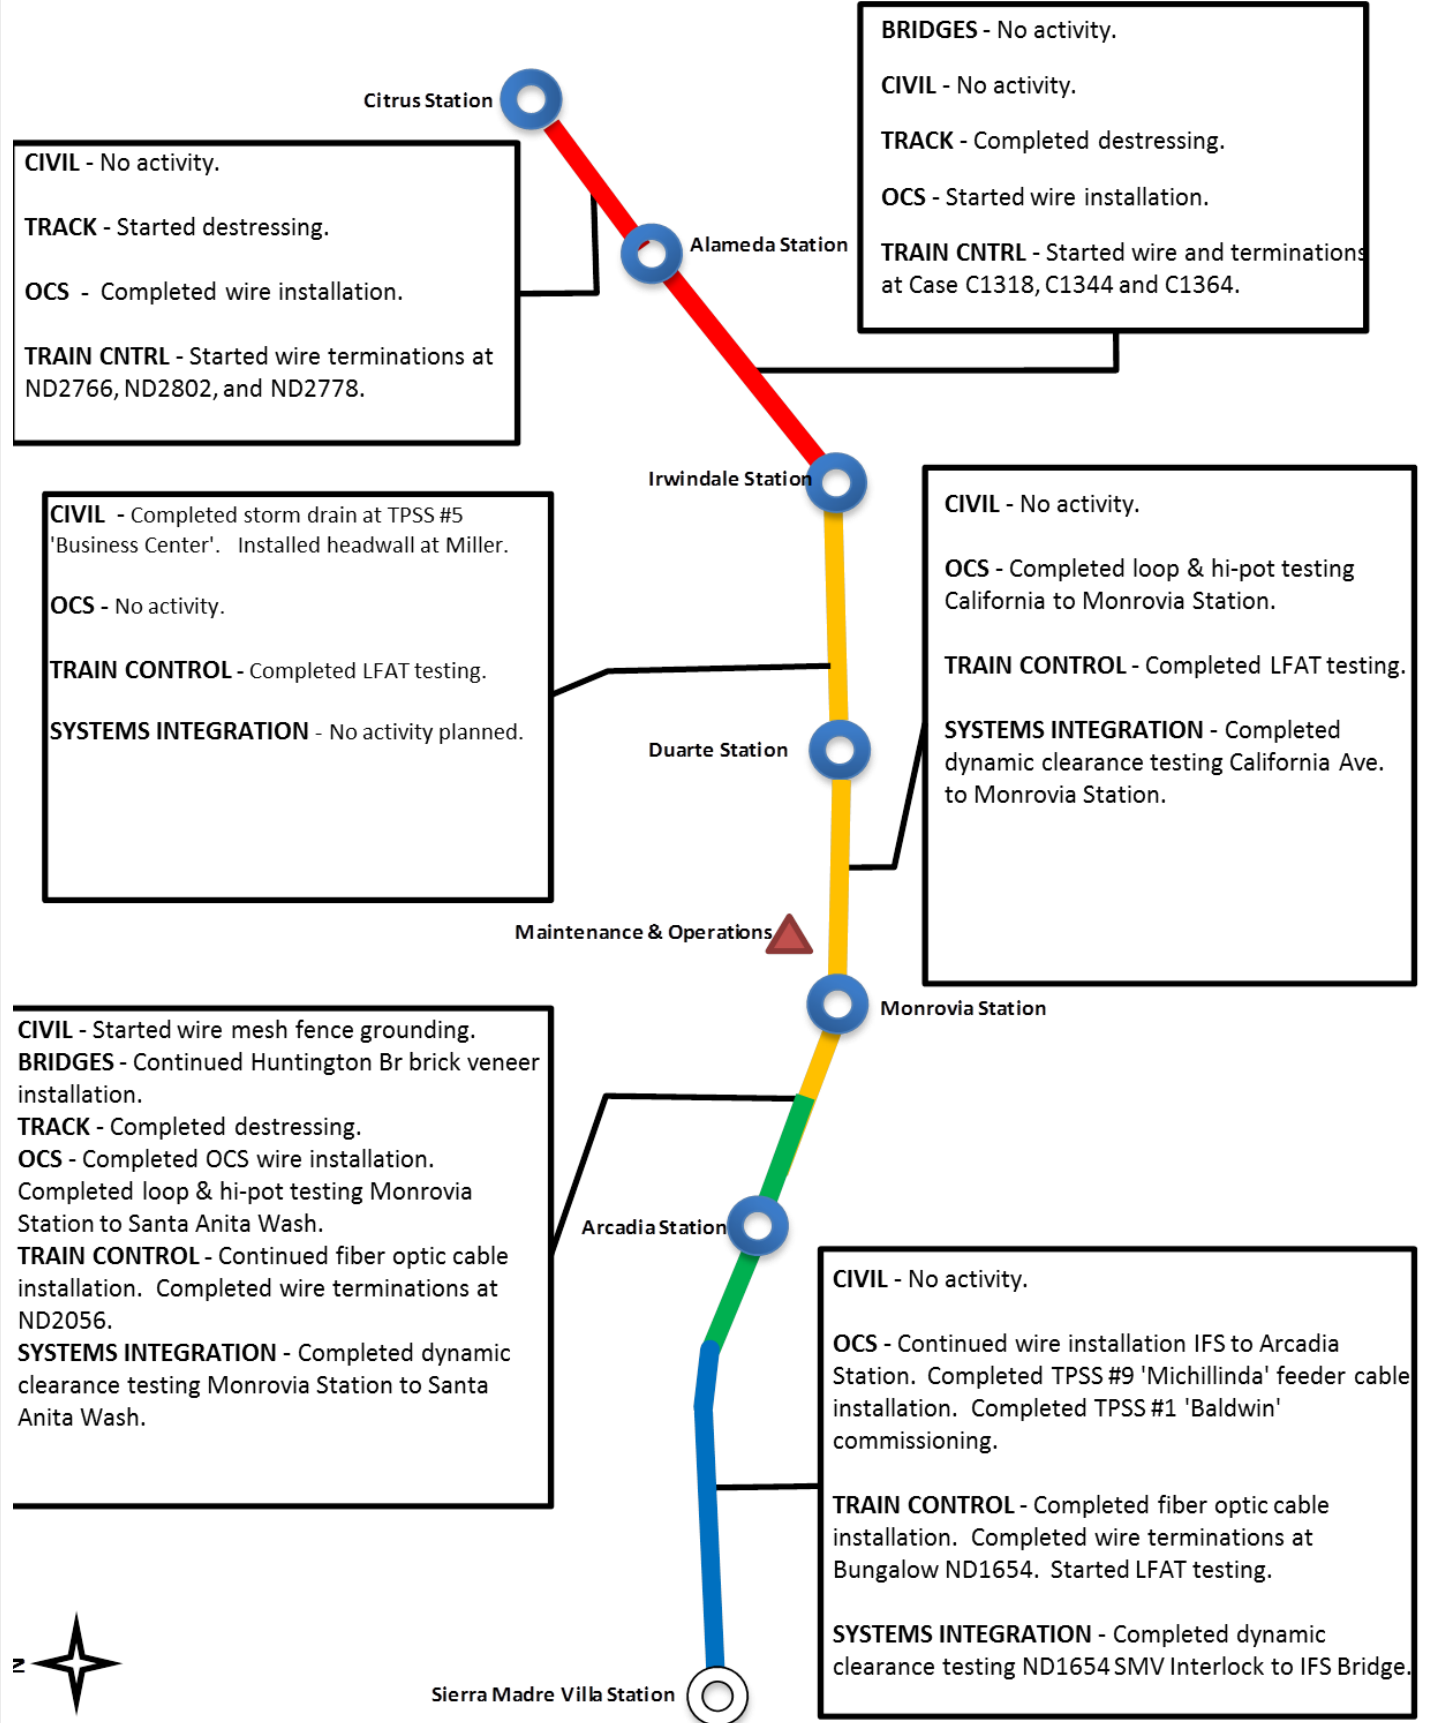



FACILITY CONSTRUCTION PROGRESS THIS PERIOD

Citrus Ave Station

STATION - Continue communications bungalow wire terminations.

PARKING - Started installation of stair No.2 and elevator No.2 hoist way structural steel. Completed barrier rail concrete. Completed installation of CMU walls for elevator and electrical rooms. Started Level 2 plumbing. Started sewer installation.

STATION - Completed canopy metal roofing installation. Continued electrical /communications bungalow wire installation & terminations. Continued platform paver installation.

PARKING - No activity planned.

Alameda Station

STATION - Started platform paver installation. Continued canopy metal roofing installation. Continued electrical wire installation & terminations.

PARKING - Completed Level 1 vertical columns/shear walls and slab on grade. Started level 2 deck.

Irwindale Station

CIVIL - Completed installation of storm water detention system. Continue Wall 'A' and 'C' fence installations. Started Wall 'D' fence installation. Started curbs and AC paving.

STRUCTURES - *M&O Building* - continued interior doors & glazing. Completed drywall installation. Continued exterior metal panels. Completed car hoist installation. Completed Blow Down and Wheel Truing Steel installation. Continue elevators. Start acoustical ceiling tile installation. Started bathroom tile installation and plumbing finishes. *Car Wash* - Continued installation of car wash equipment. Completed roof installation. *Cleaning Platform* - Continued communications installation. Started drywall, doors, and tile. *Material Storage* - Completed roll-up doors. *MOW Building* - Started communications installation. *Fire Tank* - Completed Start tank bolted assembly.

OCS - Continue OCS wire installations.

TRAIN CONTROL - Completed wire terminations at South bungalows. Completed track circuits, yard signals and Xing gates.

STATION - Continued installation communications equipment and terminations. Started steel metal railing installation. Installed blue light station. Installed ADA ramp. Completed artwork installation.

PARKING - Installed construction fencing, started demolition of existing paving and tree removal.

Duarte Station

STATION - Completed walkway and ramp lighting. Completed metal railing installation.

PARKING - Continued communications equipment and wire installation. Continued installation of elevator cabs.

Maintenance & Operations

Monrovia Station

STATION - Continued communications wire terminations. Completed metal railing installation. Started artwork installation.


PARKING - Continued communications wiring and equipment installations. Completed installation of elevator cabs.

Arcadia Station





ALIGNMENT CONSTRUCTION PROGRESS NEXT PERIOD

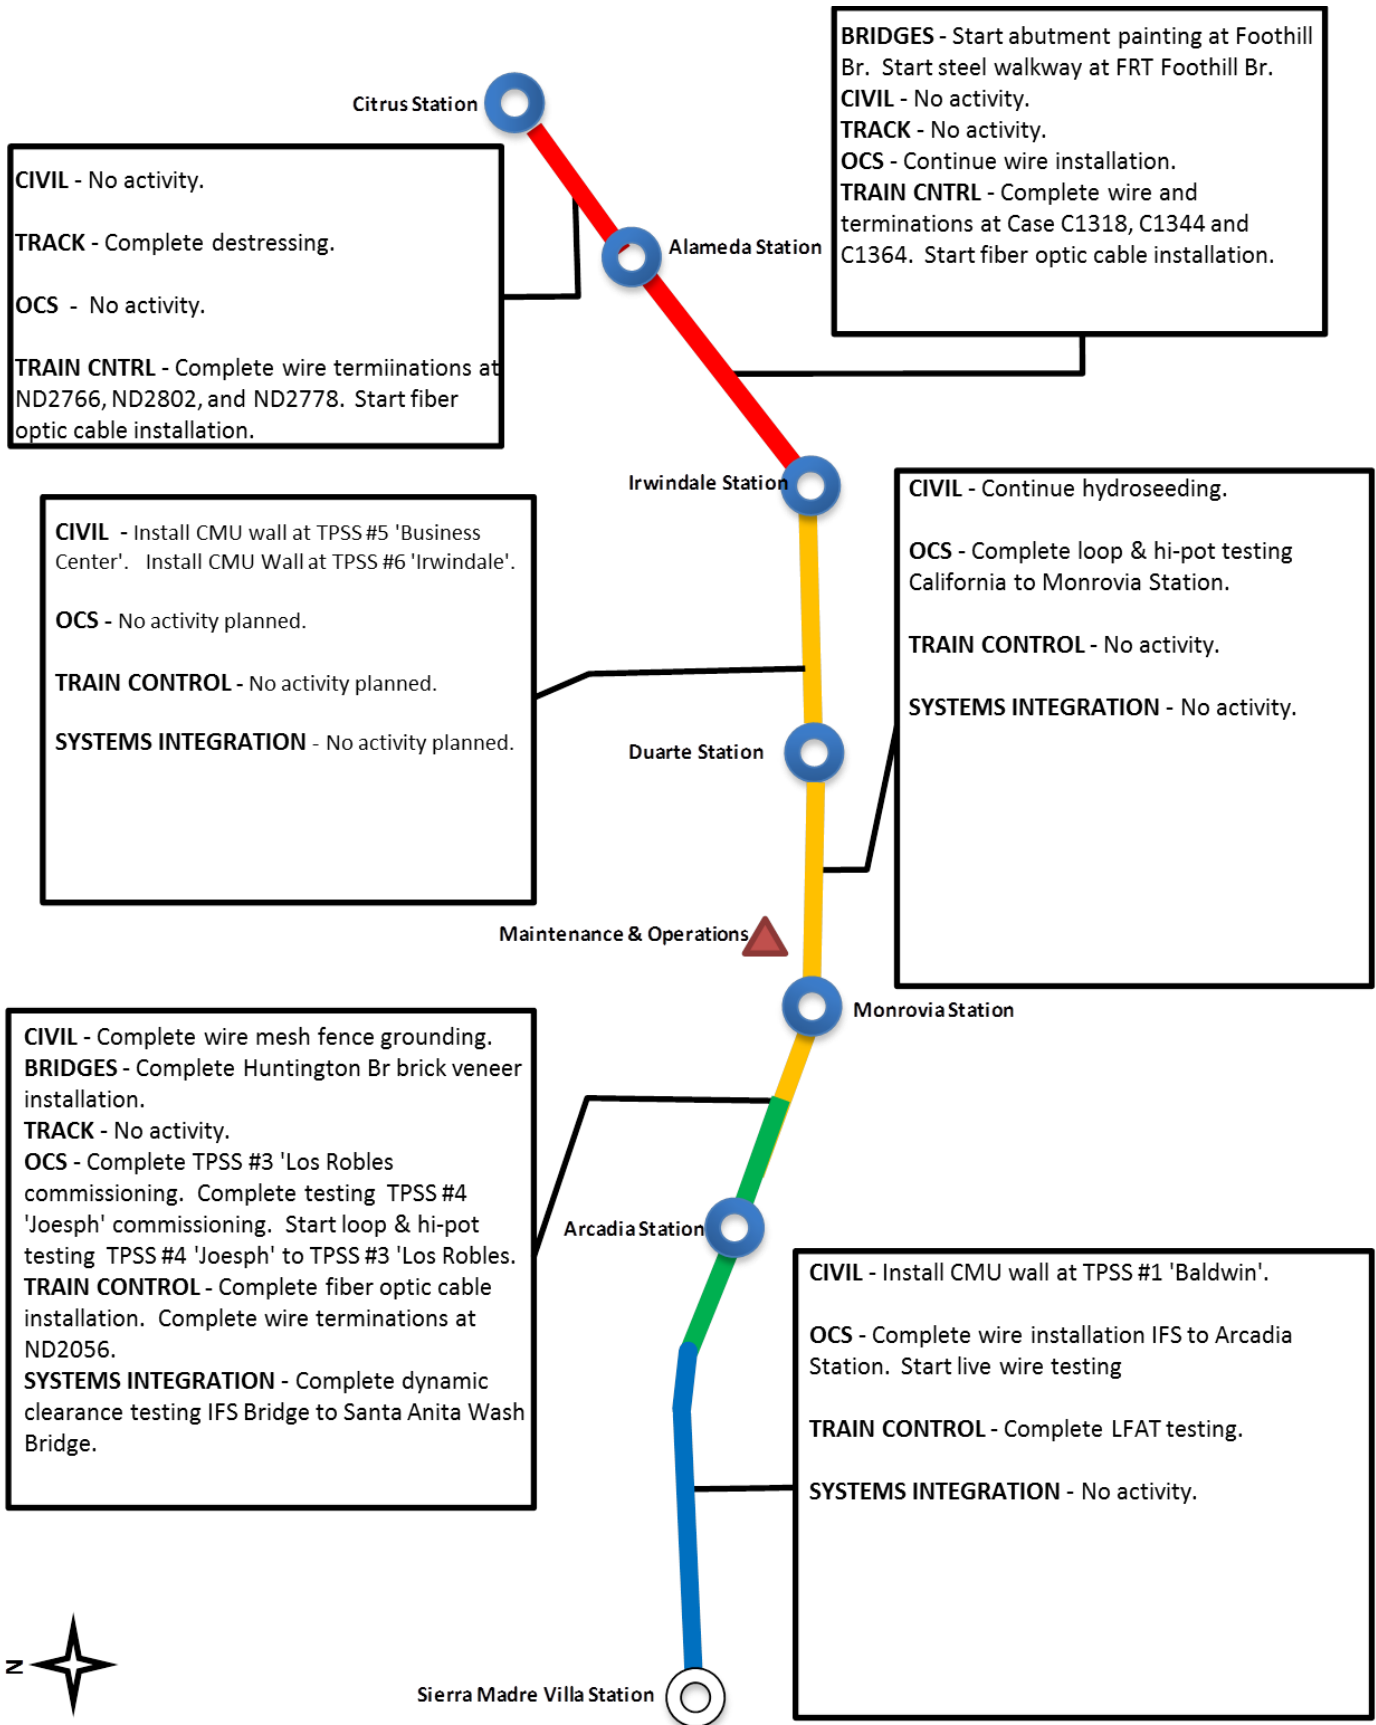



FACILITY CONSTRUCTION PROGRESS NEXT PERIOD

Citrus Ave Station

STATION - Continue communications bungalow wire terminations. Start metal roofing installation.

PARKING - Complete installation of stair No.2 and elevator No.2 hoist way structural steel. Start elevator No.1 and No.2 glazing installation. Start fire protection installation. Complete electrical rough-in. Start electrical equipment installation. Complete plumbing installation. Continue sewer installation. Start pedestrian walkway lighting.

STATION - Continue electrical /communications bungalow wire installation & terminations. Complete platform paver installation. Start metal platform railing installation.

PARKING - No activity planned.

Alameda Station

STATION - Continue platform paver installation. Complete canopy metal roofing installation. Continue wire installation & terminations.

PARKING - Complete Level 2 columns/shear walls and level 2 deck.

Irwindale Station

CIVIL - Complete steel picket fence installations at Wall 'A', 'C', 'D' and start Wall 'B' and 3M fence installations.

STRUCTURES - *M&O Building* - Complete interior doors & glazing. Complete exterior metal panels. Complete elevators. Continue acoustical ceiling tile installation. Complete bathroom tile installation and plumbing finishes. *Car Wash* - Complete installation of car wash equipment. *Cleaning Platform* - Complete communications installation. Complete tile, and bathroom finishes. *MOW Building* - Complete communications installation. Fire Tank - Install roof and start MEP testing.

OCS - Complete OCS wire installations. Start OCS testing.

TRAIN CONTROL - Continue LFAT testing.

STATION - Complete installation communications equipment and terminations. Complete metal railing installation. Start Communications LFAT testing.

PARKING - Start site grading. Start installation of underground conduits. Start light pole bases. Start curbs.

Duarte Station

STATION - Start painting metal railings. Start Communications LFAT testing.

PARKING - Complete communications equipment and wire installation. Complete installation of cabs. Start installation of signs and start paint markings.

Maintenance & Operations

Monrovia Station

STATION - Continue communications wire terminations. Start painting metal railing. Complete artwork installation. Start painting structure exterior.

PARKING - Complete communications wiring and equipment installations.

Arcadia Station





ALIGNMENT CONSTRUCTION IMAGES

Segment 1: Sierra Madre Villa - Emergency Egress
Stair Installation



Segment 2: 1st/Santa Clara - Gate Arm Installation
and Adjustment

Segment 3: Monrovia Station - Guardrail Painting





ALIGNMENT CONSTRUCTION IMAGES (CONTINUED)



Segment 4: Irwindale Station Progress

Segment 4: Citrus to Barranca - Track Surfacing



Operations Campus: Solar Panel Installation on the MOW Canopy



Change Management Log

Date: 3/4/2015

Page: 1 of 5

Project: C1135 Alignment - FTC Contract #: C1135

Original Contract Amount:	\$485,867,000				
Approved Change Orders:	\$18,968,786	3.90%	Pending Change Orders:	\$0	0.00%
Current Contract Total:	\$504,835,786		Pending Contract Total:	\$504,835,786	3.90%

Change Orders

Number	Change Management	Title	Initiated Date	Approved Date	Outstanding Days	Time Extension	Amount
EXECUTED Change Orders							
001.00	000.00	Interim NTP	11/3/2011	11/3/2011	0		\$0
002.00	013.00	Colorado Bridge Haz Mat	5/17/2012	5/18/2012	1		\$121,382
002.01	013.01	Colorado Bridge HazMat - Final	9/5/2012	9/7/2012	2		\$13,164
003.00	001.00	Sound Wall Deletion - Duarte Road	7/12/2012	7/18/2012	6		(\$74,707)
004.00	018.00	Revise Block Design - CBD Calc	8/23/2012	8/29/2012	6		\$3,986
004.01	018.01	Revise Block Design - CBD Calc - 2	9/5/2013	9/11/2013	6		\$0
005.00	023.00	Wayside Signal Aspect Revision	9/6/2012	9/7/2012	1		\$26,072
005.01	023.01	Wayside Signal "Call On" Function	10/30/2013	11/1/2013	2		\$75,169
006.00	040.00	Arcadia Frieze, Bench-Artist Design	9/6/2012	9/10/2012	4		\$13,683
006.01	040.01	Arcadia Frieze, Bench-Construction	3/7/2013	3/12/2013	5		\$155,894
007.00	019.02	Soils Testing Abutments & Fdns	9/14/2012	9/18/2012	4		\$44,993
008.00	041.00	Unknown Utilities RFCN 005 006 008	9/14/2012	9/18/2012	4		\$132,450
009.00	038.00	Illuminate City Names @ Stations	9/18/2012	9/24/2012	6		\$184,657
010.00	046.00	SGRB - Lead Based Paint Remediation	9/21/2012	9/24/2012	3		\$244,536
011.00	004.00	Station Architectural Changes	10/11/2012	10/12/2012	1		\$443,950
012.00	003.01	Systems and Testing for Added TPSS	12/13/2012	12/14/2012	1		\$1,443,193
013.00	005.02	IDIQ Comm Contract (Rev 2)	12/14/2012	1/22/2013	39		\$698,259
014.00	060.00	Sewer Encasement Changes in Azusa	12/18/2012	1/24/2013	37		\$141,354
015.00	037.02	M&O - Materials Storage Revisions	12/26/2012	1/15/2013	20		\$62,862
015.01	037.03	M&O Storage Shelving Revisions	9/16/2013	9/19/2013	3		\$20,380
016.00	002.00	Relocation of Access Road to 3M Fac	12/26/2012	1/16/2013	21		\$53,814
017.00	025.00	3 Electrical Casings for ALW	2/27/2013	3/1/2013	2		\$219,033
018.00	073.00	Hazardous Abatement at Bridges	1/15/2013	2/6/2013	22		\$1,081,803
019.00	054.00	City of Hope Conduits	1/11/2013	1/22/2013	11		\$34,313
020.00	059.00	Citrus TPSS Transformer Pad Changes	2/6/2013	2/7/2013	1		\$34,536
021.00	075.00	Demo & Replace Palm Dr. Roadway	2/7/2013	2/14/2013	7		\$90,365
022.00	077.00	M&O Differing Site Conditions; Pt 1	2/13/2013	2/15/2013	2		\$66,360
022.01	093.00	M and O DSC T and M Work Part 2	3/8/2013	3/12/2013	4		\$66,625
022.02	103.00	M and O DSC Part 3	3/27/2013	3/28/2013	1		\$35,211
022.03	115.00	DSC at M and O Part 4	5/3/2013	5/7/2013	4		\$5,706
023.00	089.00	Contaminated Soil Abatement	2/26/2013	2/27/2013	1		\$422,068
024.00	068.00	Monrovia Sound Wall Panel Change	2/26/2013	2/28/2013	2		(\$24,150)
025.00	052.00	Santa Anita Trail Detour	3/8/2013	3/12/2013	4		\$27,691
026.00	070.00	Block Type Change at M&O Building	3/26/2013	3/26/2013	0		\$35,016
027.00	065.00	M&O IT Changes-Duct Banks/Conduits	3/26/2013	3/26/2013	0		\$88,650
027.01	065.01	M&O IT Changes - Power to WAP	9/4/2013	9/6/2013	2		\$73,049
027.02	065.02	M&O IT Changes - Remaining Work	7/16/2014	7/17/2014	1		\$155,991
028.00	039.01	Delete Layover Building	4/11/2013	4/12/2013	1		(\$313,832)
029.00	095.00	8in Sanitary Sewer Line- Alameda Av	4/23/2013	4/25/2013	2		\$226,089
029.01	095.01	Alameda Sewer Line Revised Scope	11/22/2013	11/26/2013	4		(\$37,425)
030.00	102.00	M&O-Disconnect Switches, Insulators	4/23/2013	4/25/2013	2		\$67,817
031.00	110.00	Rmv Abandoned Utility Line @ Dalton	4/23/2013	4/25/2013	2		\$1,562
032.00	104.00	Highland Ave Abandoned CMP sleeves	5/1/2013	5/3/2013	2		\$15,005
033.00	114.00	Remove contaminated wood culvert	5/3/2013	5/7/2013	4		\$4,714
034.00	128.00	M&O Backup Power/Generator Changes	5/13/2013	5/21/2013	8		\$121,340



Change Management Log

Date: 3/4/2015

Page: 2 of 5

Project: C1135 Alignment - FTC Contract #: C1135

Change Orders

Number	Change Management	Title	Initiated Date	Approved Date	Outstanding Days	Time Extension	Amount
EXECUTED Change Orders							
035.00	083.00	M&O Vehicle Sanding System Changes	5/21/2013	5/24/2013	3		\$27,463
036.00	006.00	IFS Related Contract Changes	6/7/2013	6/11/2013	4		(\$263,111)
037.00	137.00	CTS Redesign	7/12/2013	7/16/2013	4		\$58,214
038.00	138.00	Segment 4 Safety Manager	7/12/2013	7/16/2013	4		\$157,274
038.01	138.01	Segment 4 Safety manager - Part 2	11/19/2013	11/21/2013	2		\$72,963
038.02	138.02	Segment 4 Safety Manager - Part 3	4/3/2014	4/7/2014	4		\$82,271
039.00	085.00	M&O Drainage System Enhancements	7/19/2013	8/13/2013	25		\$251,579
040.00	067.00	Station Paver Changes	7/23/2013	8/13/2013	21		\$728,340
040.01	067.01	Rebar Changes for Station Pavers	10/28/2013	10/31/2013	3		\$10,586
041.00	112.00	12" Pasadena Waterline Potholes	8/12/2013	8/16/2013	4		\$19,735
042.00	150.00	Demo Abandoned Water Lines @ Dalton	8/12/2013	8/16/2013	4		\$5,937
043.00	007.01	Emer. Backup for Guideway Lighting	8/16/2013	10/1/2013	46		\$359,158
044.00	172.00	Contaminated Wood Culvert Sta. 1202	8/27/2013	8/28/2013	1		\$7,712
045.00	139.00	BLS Changes	8/28/2013	9/4/2013	7		\$110,801
046.00	165.00	Azusa-Alameda Station; 2nd Portal	8/28/2013	9/4/2013	7		\$77,175
047.00	145.00	St. Joseph drainage enhancements	9/4/2013	9/6/2013	2		\$17,592
048.00	149.00	M&O - Lights at NW Corner Park	9/4/2013	9/6/2013	2		\$29,351
049.00	174.00	TPSS #5 Cal-Am Power Conflict	9/4/2013	9/6/2013	2		\$127,260
050.00	171.00	Relocate Access Stair to Foothill	9/4/2013	9/6/2013	2		\$20,276
051.00	173.00	Dalton 8" Water Line Work	9/5/2013	9/12/2013	7		\$35,316
052.00	071.00	Duarte Rd Screen Wall Change	9/5/2013	9/17/2013	12		(\$133,864)
053.00	176.00	Remove Contaminatd Wood-Buena Vista	9/10/2013	9/12/2013	2		\$5,543
054.00	147.00	DECCO Bypass	9/10/2013	9/12/2013	2		\$18,519
055.00	166.00	Foothill Blvd. Water/SD Relocation	9/20/2013	9/20/2013	0		\$127,074
056.00	186.00	Contaminated Wood @ San Gabriel Ave	9/23/2013	9/24/2013	1		\$4,291
057.00	194.00	California/Duarte Water Line Work	10/28/2013	10/31/2013	3		\$220,743
058.00	189.00	Four Utility Changes	10/28/2013	10/31/2013	3		\$14,157
059.00	180.00	Remove/Dispose of ACM E of Highland	10/30/2013	11/1/2013	2		\$29,311
060.00	179.00	CTS Upgrade to OC-192	10/30/2013	11/1/2013	2		\$112,543
061.00	213.00	Irwindale On-ramp Stockpile	11/8/2013	11/21/2013	13		\$200,185
062.00	053.00	Delete Totten Tubes Scope of Work	11/8/2013	11/21/2013	13		(\$143,801)
063.00	146.00	Home Depot Striping and Signing	11/15/2013	11/21/2013	6		\$21,003
064.00	204.00	Unknown Duct Bank @ San Gabriel Ave	11/15/2013	11/21/2013	6		\$1,265
065.00	140.00	M&O-Overhead Work Platform Changes	12/5/2013	12/16/2013	11		\$317,656
066.00	217.00	Buried SD & Headwall, STA 1306+50	12/6/2013	12/17/2013	11		\$1,020
067.00	219.00	Contaminated Soil, Monrovia Station	12/12/2013	12/17/2013	5		\$17,503
068.00	220.00	DSC at Sawpit Wash Abutments	12/12/2013	12/17/2013	5		\$12,668
069.00	188.00	Costco Emergency Gate-Path to POS	1/21/2014	1/22/2014	1		\$19,882
070.00	214.00	M&O - Generator Load Bank	1/21/2014	1/22/2014	1		\$38,092
071.00	224.00	Alameda South Water Line Tie-in	1/30/2014	1/31/2014	1		\$6,330
072.00	202.00	Aesthetic Lighting Provisions-SGRB	2/3/2014	2/4/2014	1		\$27,055
073.00	160.00	Move Mountain Interlocking Bungalow	2/11/2014	2/13/2014	2		\$68,596
074.00	200.00	M&O Parts Carousel Warranty & PM	2/11/2014	2/13/2014	2		\$68,906
075.00	235.00	Remove Contaminated Wood Ties	2/14/2014	2/18/2014	4		\$4,571
076.00	234.00	Accelerate Work at California Ave	2/14/2014	2/18/2014	4		\$5,663
077.00	247.00	Line Stop in California	2/18/2014	2/20/2014	2		\$14,524
078.00	201.00	Added Sound Wall, SW of IFS	2/27/2014	2/28/2014	1		\$18,201
079.00	238.00	M&O-MOW Canopy Structural Eval	2/27/2014	2/28/2014	1		\$7,147
079.01	238.01	M&O - MOW Canopy Solar	8/20/2014	8/26/2014	6		\$714,659
080.00	232.00	Car Moving Tractor-Coupler Upgrade	2/27/2014	2/28/2014	1		\$177,145



Change Management Log

Date: 3/4/2015

Page: 3 of 5

Project: C1135 Alignment - FTC Contract #: C1135

Change Orders

Number	Change Management	Title	Initiated Date	Approved Date	Outstanding Days	Time Extension	Amount
EXECUTED Change Orders							
081.00	242.00	Car Moving Tractor Options/Features	2/27/2014	2/28/2014	1		\$69,099
082.00	091.00	Rockvale Water Line Mitigation	3/4/2014	3/5/2014	1		\$163,750
082.01	091.01	Rockvale Water Line-EIC credit	4/11/2014	4/14/2014	3		(\$5,391)
083.00	251.00	Cut and Move Rail to Segment 1	3/4/2014	3/5/2014	1		\$249,934
084.00	218.00	Delete Equipment at ROC	3/26/2014	3/27/2014	1		(\$91,708)
085.00	239.00	Install Sound Wall Door @ STA. 1169	3/26/2014	3/27/2014	1		\$12,737
086.00	250.00	Change Top Row of Block Wall 1124.1	3/26/2014	3/27/2014	1		\$3,688
087.00	229.00	Irwindale TPSS-Adjust Eqpt. Layout	4/3/2014	4/7/2014	4		\$17,878
088.00	262.00	Provisional Sum Adjustment	4/3/2014	4/7/2014	4		\$0
088.01	262.01	Provisional Sum Adjustment - 2	9/19/2014	9/25/2014	6		\$0
088.02	262.02	Provisional Sum Adjustment - 3	11/12/2014	11/14/2014	2		\$0
089.00	261.00	Longer DF Bolts - SGRB	4/3/2014	4/7/2014	4		\$17,331
090.00	169.02	M&O Trimming Table Changes (rev. 2)	4/11/2014	4/14/2014	3		\$54,083
091.00	181.00	Alameda Utility Changes	4/11/2014	4/14/2014	3		(\$9,599)
092.00	241.00	Business Center TPSS Crane Changes	4/23/2014	4/28/2014	5		\$13,655
093.00	276.00	Myrtle Early Completion Incentive	4/23/2014	4/28/2014	5		\$160,000
094.00	254.00	Drainage East of Pasadena Ave.	4/23/2014	4/28/2014	5		\$6,569
095.00	275.00	Remove Rail Ties at 1st/Santa Clara	4/23/2014	4/28/2014	5		\$2,270
096.00	274.00	Buried Concrete @ Huntington Bridge	4/23/2014	4/28/2014	5		\$2,819
097.00	269.00	Asbestos Pipe at Duarte and Myrtle	4/23/2014	4/28/2014	5		\$6,583
098.00	278.00	Abandoned Gas Line at California	5/6/2014	5/7/2014	1		\$8,170
099.00	170.00	M&O Car Wash Betterments	5/6/2014	5/7/2014	1		\$166,144
100.00	223.00	M&O-Volume Control for PA Speakers	5/6/2014	5/7/2014	1		\$38,105
101.00	283.00	Track Work Around at Mountain Ave	5/6/2014	5/7/2014	1		\$29,996
102.00	284.00	Install 115# Buffer Rails in Seg. 1	5/6/2014	5/7/2014	1		\$29,442
103.00	230.00	Azusa-Citrus Ped Crossing Operation	5/6/2014	5/7/2014	1		\$84,183
104.00	231.00	Red Signal Violation Indication	6/3/2014	6/3/2014	0		\$335,134
105.00	253.00	Remove Stem Wall along Duarte Rd.	6/11/2014	6/12/2014	1		\$37,527
106.00	271.00	DVR Changes	7/16/2014	7/17/2014	1		\$181,301
107.00	260.00	M&O Supplemental Fire Water System	7/16/2014	8/4/2014	19		\$1,642,824
108.00	163.00	1st/Santa Clara Grade X-ing Changes	7/25/2014	7/30/2014	5		\$156,177
109.00	164.00	M&O Body Shop Changes	7/25/2014	8/4/2014	10		\$488,598
110.00	256.00	Monrovia North Bunglow LCP Changes	7/25/2014	7/30/2014	5		\$125,313
111.00	237.00	M&O-Signaling System Changes	7/29/2014	8/4/2014	6		\$1,133,746
112.00	252.00	Irwindale Security Kiosk Provisions	8/4/2014	8/6/2014	2		\$178,044
112.01	252.01	Irwindale Security Kiosk - Part 2	2/9/2015	2/11/2015	2		\$47,168
113.00	281.00	M&O - Accent Colors	8/4/2014	8/6/2014	2		\$26,928
114.00	305.00	Lead Paint, Foothill Median Barrier	8/18/2014	8/20/2014	2		\$5,690
115.00	270.00	TES Load Flow Simulation	8/19/2014	8/21/2014	2		\$22,399
116.00	203.00	Mayflower Driveway/Wall Credit	8/20/2014	8/26/2014	6		(\$19,138)
117.00	307.00	Contaminated Wood Ties-Santa Anita	8/20/2014	8/26/2014	6		\$3,226
118.00	082.01	M&O / 3M Fence Revisions (rev 1)	9/17/2014	9/25/2014	8		\$886,650
119.00	314.00	Mountain Early Completion Incentive	9/17/2014	9/24/2014	7		\$80,000
120.00	301.00	Santa Anita Avenue Bridge Artwork	9/17/2014	9/25/2014	8		\$57,224
121.00	313.00	Additional Traffic Signal Testing D	9/19/2014	9/25/2014	6		\$7,875
122.00	320.00	Remove Asbestos Pipe at Virginia	11/12/2014	11/14/2014	2		\$9,485
123.00	303.00	Additional Anti-Graffiti Coating	12/8/2014	12/8/2014	0		\$63,727
124.00	326.00	Santa Anita Avenue Bridge Lighting	12/8/2014	12/8/2014	0		\$208,633
124.01	326.01	Santa Anita Bridge Lighting-Part 2	1/16/2015	1/19/2015	3		\$5,744
125.00	335.00	M&O - Interior Wall Revisions	12/18/2014	12/19/2014	1		\$43,786



Change Management Log

Date: 3/4/2015

Page: 4 of 5

Project: C1135 Alignment - FTC Contract #: C1135

Change Orders

Number	Change Management	Title	Initiated Date	Approved Date	Outstanding Days	Time Extension	Amount
EXECUTED Change Orders							
126.00	304.00	M&O Lobby Aesthetic Changes	12/18/2014	12/19/2014	1		\$128,047
127.00	292.00	M&O - Guard House Changes	12/19/2014	12/19/2014	0		\$65,463
128.00	339.00	Mountain Ped. Crossing Changes	1/8/2015	1/12/2015	4		\$96,159
129.00	340.00	Business Center TPSS Drainage	1/16/2015	1/19/2015	3		\$249,959
130.00	255.00	Virginia TPSS Access Road	1/8/2015	1/12/2015	4		\$39,718
131.00	291.00	Eliminate 'Train Coming' Signs	1/8/2015	1/12/2015	4		\$9,325
132.00	322.00	Replace Existing OCS Pole at SMV	1/16/2015	1/19/2015	3		\$27,010
133.00	187.01	Irwindale Ramp Signs	1/20/2015	1/26/2015	6		\$125,015
134.00	346.00	Delay in Setting of Yard Substation	1/20/2015	1/26/2015	6		\$15,181
135.00	344.00	Virginia TPSS-Access for Delivery	1/30/2015	2/2/2015	3		\$67,019
136.00	328.00	Rail Profile Grinding	2/9/2015	2/18/2015	9		\$524,000
137.00	065.03	M&O Main Building Comm. Room Floors	2/17/2015	2/17/2015	0		\$4,402
138.00	353.00	1st/Santa Clara Noise Mitigations	2/17/2015	2/17/2015	0		\$13,889
139.00	323.00	Add Pavers to Duarte Station W Ramp	2/18/2015	2/18/2015	0		\$31,982
140.00	338.00	M&O-Wheel Truing Machine Car Puller	2/19/2015	2/19/2015	0		\$83,112
141.00	258.00	M&O Tactile Guidance Changes	2/23/2015	2/26/2015	3		\$203,945
142.00	352.00	M&O - Fire Alarm System	2/23/2015	2/26/2015	3		\$238,983
143.00	351.00	Sierra Madre Track Rehab	2/23/2015	2/26/2015	3		\$18,107
144.00	349.00	Remove water line east of Highland	2/23/2015	2/26/2015	3		\$4,648
145.00	360.00	M&O Facility - Yard Control Console	3/2/2015	3/3/2015	1		\$23,158
146.00	359.00	Generators for Testing-SRGB to IRW	3/2/2015	3/3/2015	1		\$6,758
Subtotal:							\$18,968,786

Subtotal: \$18,968,786

Total: \$18,968,786

Open PCOs

PCO Number	Title
OPEN	
022.04	M&O IT Changes - Furniture Interface
029.00	Del. Irwindale/Gladstone Mitigation
075.00	Comm. Changes Parking Structures
075.01	Add 2 ETEs to Duarte Parking Lot
080.00	Delete Evergreen / Myrtle Mitigation
084.00	M&O Service Vehicle Pathways
085.00	Joseph TPSS Power Feed Credit
087.00	ETEL/PTEL Faceplate Betterment
091.00	UP Tunnel Analysis & Modifications
092.00	Abandoned California Water Lines
096.00	Station Identifier Changes
098.00	M&O Facility - NW Corner Changes
100.00	Change Wayside Operational Signage
101.00	Peck Road Ramp
103.00	Tactile Guidance Tile at Stations
104.00	Striping/Signs at Station Ped Xings
107.00	Add APS @ 2 intersections in Duarte
108.00	M&O - Move East Lobby Wall

Open RFCs

RFC Number	Title
OPEN	
075.00	Grade X-ing Train Signal Changes CS
078.00	Addl Fence To Close Gaps at Alignmn
080.00	Irwindale Signal Case and Push But
093.00	Blk Wall Finish In the MO Fac CSP



Change Management Log

Date: 3/4/2015

Page: 5 of 5

Project: C1135 Alignment - FTC Contract #: C1135

Open PCOs

PCO Number	Title
OPEN	
109.00	M&O Early Completion Milestone

Open RFC Notices

Number	Title
037.00	DSC at Santa Anita Wash Abutment 1
044.00	DSC Utility at Azusa Avenue
086.00	Ground Grid Damaged at Citrus TPSS
088.00	Change to Exit Gate Procedure
098.00	Housekeeping Pads for Electrical Eq
099.00	Dispose of Haz Mat at Angelino Ave
100.00	MO Yard Signage Changes
102.00	Foothill Yard MOW Track Fouling Iss



Description: Intermodal Parking Facilities & Enhancements **Status:** February 15, 2015

Contract No.: C1150

Contractor: Webcor Builders

Progress Completed This Period

Design

- Submit AFC Design - Duarte Parking Lot
- Submit AFC Design - Duarte Parking Enhancements
- Submit AFC Design - Azusa-Alameda Enhancements
- Submit AFC Design - Irwindale Parking Structure (full set)

Activities Planned Next Period

Design

- Submit AFC Design - Irwindale Enhancements (full set)
- Submit AFC Design - Signage

Areas of Concern

- **IRWINDALE PARKING STRUCTURE RECOVERY** - The Design-Build Contractor has started to accelerate the Irwindale parking structure and has made a significant improvement by implementing a 6-day work week schedule. The Design-Build Contractor is currently on pace to complete the concrete structure and provide access to the C1135 - Alignment Design-Build Contractor before May 2015.

Areas of Concern (Continued)

DUARTE PARKING LOT PROCUREMENT - The light pole procurement was incorporated into the Design-Build Contractor's schedule, and the projected duration for delivery is estimated to be four (4) months. As a result, there is a potential 1.5 month delay to the Substantial Completion milestone. The Authority will monitor procurement progress and will discuss potential alternatives to expedite the delivery of the light poles to minimize potential impacts to the Substantial Completion milestone.


**Description:** Intermodal Parking Facilities & Enhancements **Status:** February 15, 2015**Contract No.:** C1150**Contractor:** Webcor Builders**Cost Summary:**

	Million(s)
CONTRACT	
Contract Award Value:	48.8
Executed Change Orders:	0.9
Current Contract Value:	49.7
Potential Change Orders:	0.3
Current Forecast:	50.0
Earned Value/Actual Cost	36.1
AUTHORIZATION FOR EXPENDITURE	
Budget	50.3
Commitment	49.7
Balance	0.3

Cost Assessment:

This period, the current cost forecast is \$50.0 Million and remains unchanged from the previous period. The current forecast is within the authorized budget.

Although a 90 day time extension was granted, the Design-Build Contractor remains behind the revised plan due to schedule delays at the Irwindale site. In order to recover for an on schedule completion of June 2015, the Design-Build Contractor will need to progress 12% over the next period.

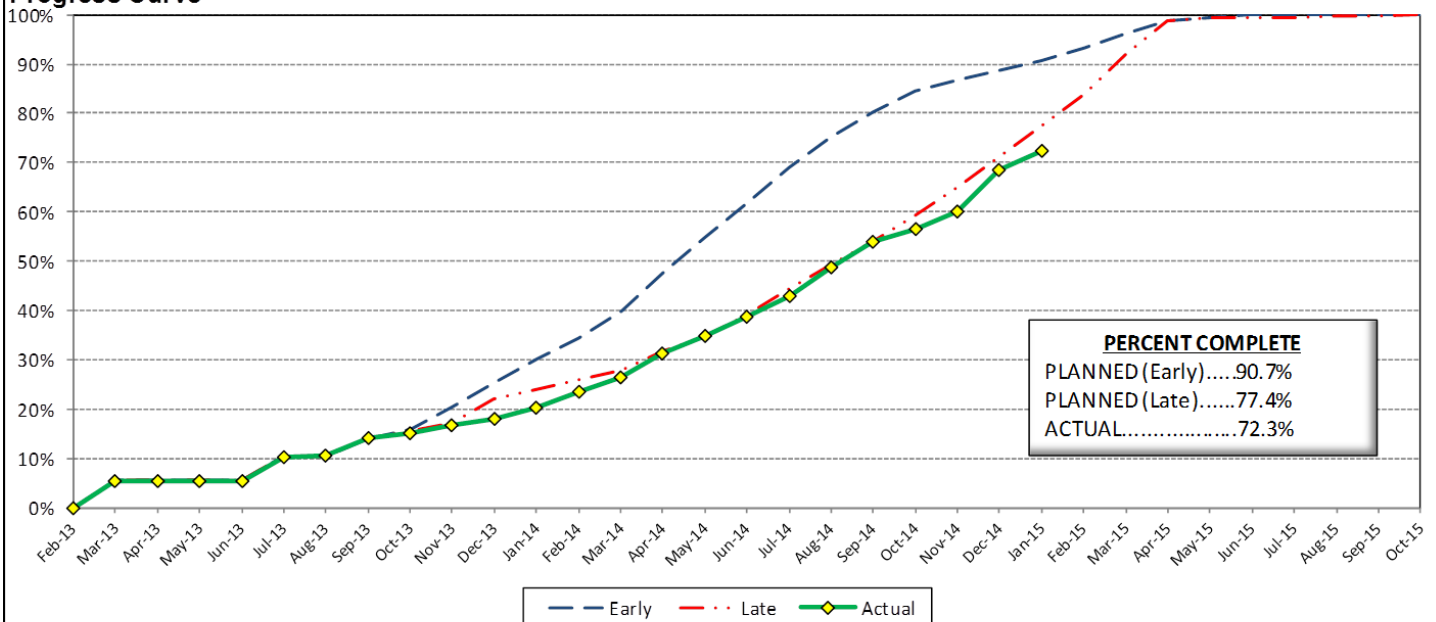Progress Curve**Schedule Summary:**

Contract Award:	02/27/13
Notice to Proceed (NTP) :	03/20/13
Original Contract Duration:	845 Calendar Days
Current Contract Duration:	935 Calendar Days
Elapsed Time from NTP:	697 Calendar Days

Contract Milestones

Milestones	Description	Original Contract	Current Contract	Forecast	Variance
1	Substantial Completion	03/15/15	06/13/15	07/09/15	(26)
2	Punchlist Complete	05/29/15	08/27/15	09/22/15	(26)
3	Final Completion	07/13/15	10/11/15	11/06/15	(26)
4	TPSS Work	03/01/14	03/01/14	3/31/2014 A	(30)

Schedule Assessment:

Although the Design-Build Contractor appears to be successful with the implementation of the Irwindale site schedule mitigation effort, the Design-Build Contractor is currently reporting light pole procurement delays at the Duarte and Alameda site, which are currently impacting the Substantial Completion milestone. In order to maintain on schedule progress, the level 2 columns & shear walls at the Irwindale site, and the elevator and stair No.2 structural steel installation at the Azusa-Citrus site will need to be completed by the next reporting period.



PARKING FACILITY CONSTRUCTION IMAGES



Arcadia Parking Structure Site Overview



Monrovia Parking Structure Site Overview



PARKING FACILITY CONSTRUCTION IMAGES

Duarte Parking Lot Demolition



Irwindale Parking Structure Site Overview

Azusa-Citrus Parking Structure Site Overview





Change Management Log

Date: 3/4/2015

Page: 1 of 2

Project: C1150 Parking - Webcor Contract #: C1150

Original Contract Amount:	\$48,750,000				
Approved Change Orders:	\$907,617	1.86%	Pending Change Orders:	\$16,295	0.03%
Current Contract Total:	\$49,657,617		Pending Contract Total:	\$49,673,912	1.90%

Change Orders

Number	Change Management	Title	Initiated Date	Approved Date	Outstanding Days	Time Extension	Amount
EXECUTED Change Orders							
001.00	001.00	Monrovia Parking Alternative Layout	6/25/2013	7/11/2013	16		\$21,382
001.01	001.01	Monrovia Alternative - Cancellation	9/17/2013	10/7/2013	20		(\$12,006)
002.00	003.00	Clock Tower Procurement	7/3/2013	7/11/2013	8		\$107,246
003.00	002.00	Relocate Elevator @ Azusa-Citrus PF	12/18/2013	1/8/2014	21		\$159,899
004.00	013.00	Irwindale Structure Relocation	1/23/2014	8/28/2014	217	90	(\$65,564)
005.00	018.00	Monrovia Demo Unforeseen Conditions	3/18/2014	3/26/2014	8		\$17,013
006.00	010.00	Arcadia Transit Plaza Betterments	3/14/2014	3/26/2014	12		\$35,466
007.00	009.01	Irwindale Intersection Betterments	3/25/2014	3/26/2014	1		\$19,985
008.00	017.00	Irwindale Intersection Water Line	3/25/2014	4/14/2014	20		\$7,748
009.00	020.00	Unforeseen Underground Demo-Arcadia	6/13/2014	7/9/2014	26		\$6,313
010.00	011.00	Soldano TPSS Added ROW Fence	7/24/2014	7/28/2014	4		\$8,481
011.00	024.00	SCE Power Feed to DB2 Arcadia TPSS	7/24/2014	7/28/2014	4		\$17,199
012.00	025.00	Additional Sidewalk at Arcadia	7/24/2014	7/28/2014	4		\$3,342
013.00	006.00	St. Joseph Drainage Enhancements	7/31/2014	7/31/2014	0		\$139,488
014.00	012.00	Additional Conduit Provisions	8/13/2014	9/3/2014	21		\$57,262
015.00	030.00	Unforeseen Conditions at Michillinda	8/22/2014	8/28/2014	6		\$1,643
016.00	019.00	Parking Facility Artwork	8/27/2014	8/28/2014	1		\$75,850
017.00	034.00	Michillinda Conduit Demo & Pull Box	11/12/2014	11/20/2014	8		\$31,506
018.00	016.00	Monrovia Canopies & Banding Color	12/19/2014	12/29/2014	10		\$247,577
019.00	035.00	Irwindale CCTV Pole	12/29/2014	1/5/2015	7		\$6,220
020.00	039.00	Engineering Costs for Arcadia Clock	12/17/2014	12/29/2014	12		\$5,292
021.00	008.00	Azusa-Citrus Plaza Pavers	1/5/2015	1/13/2015	8		\$7,350
022.00	038.00	Temporary Power for Irrigation at M	1/7/2015	1/13/2015	6		\$1,465
023.00	037.00	Additional Slurry for City of Arcad	1/7/2015	1/13/2015	6		\$7,460
Subtotal:							\$907,617
Subtotal:							\$907,617

PENDING Change Orders

025.00	029.00	Metro-Requestd Elevator Vent Detail	2/12/2015		20		\$11,553
026.00	041.00	Azusa Citrus Grand Pylon Power	2/13/2015		19		\$4,742
Subtotal:							\$16,295
Subtotal:							\$16,295
Total:							\$923,912

Open PCOs

PCO Number	Title
OPEN	
013.00	Primrose Avenue cul-de-sac Deletion
014.00	Delete Azusa-Alameda Enhancements
017.00	Michillinda Pull Box Replacement
018.00	Irwindale Kiosk Foundation

Open RFCs

RFC Number	Title
OPEN	
007.00	Added PME Switch & 2 Spare Conduits
011.00	Comm. Duct Bank Interface with DB2
012.00	SCE Capacitor Bank at Michillinda T
013.00	ETEL Enclosures
016.00	Irwindale Added FH for LACFD Code C



Change Management Log

Date: 3/4/2015

Page: 2 of 2

Project: C1150 Parking - Webcor Contract #: C1150

Open PCOs

PCO Number	Title
OPEN	
019.00	Michillinda TPSS Architectural Mods

Open RFCs

RFC Number	Title
OPEN	
017.00	Elevator Holding Tanks

Open RFC Notices

Number	Title
016.00	Irwindale Added FH for LACFD Code C
023.00	Generator for Monrovia Elevators
024.00	Relocate Monrovia Jobsite Trailers
025.00	CCTV Scope at Duarte Surface Lot



AZUSA TO MONTCLAIR SEGMENT

ACTIVITIES COMPLETED THIS PERIOD

Authority and City staff continued to hold coordination meetings to discuss the project. A draft of the Master Cooperative Agreement (MCA) was distributed to all cities for review in September 2014, after which all the cities met to discuss the terms of the MCA. The cities were scheduled to provide comments on the MCA to the Authority by November, and then by January but neither of those deadline were met. The cities provided comments in early February 2105, and the cities and Authority met on February 18th to discuss these comments. The MCA is expected to be agreed upon by all parties by April 30, 2015. The Authority and cities are working together to meet this deadline.

The Authority also continued to hold meetings with the Station Design Art Review (SDAR) committees from each city. Last November, the Authority conducted a tour of the Gold Line Phase 1 artwork and the Phase 2A Arcadia Transit Plaza for all SDAR members. Each Station Artist is developing concepts for the Station Artwork based on research of the cultural, historical and natural characteristics of their Station Area. These concepts will be presented at the upcoming Community Open Houses.

This period, Authority staff worked on the following technical elements of the project:

- Continued advancement of the plan and profile drawings
- Continued right-of-way survey and drawings
- Began surveying work
- Began geotechnical work
- Began Pomona parking facility conceptual design

KEY FUTURE ACTIVITIES

The advanced conceptual engineering process is an 18-month process. Upon completion, the Azusa to Montclair segment will be ready for a design-build procurement. Upcoming activities include continuing to attend coordination meetings with each corridor city, finalizing the city MCAs, development of the ROW drawing work, refinement of the alignment, completing the SDAR, and completing the geotechnical investigations.

Federal Transit Administration (FTA)

The Metro Board of Directors excluded the Gold Line from seeking federal New Starts funding. The Authority will work together with Metro along with the Congressional delegation to seek funding to construct the extension following completion of the environmental review.



PHASE 2 FOOTHILL EXTENSION FINANCIAL STATUS

Project Operating Budget Summary in Millions of Dollars

February 28, 2015

	(a)	(b)	(c=a-b)	(d)
FINANCIAL PLAN	Current Budget	Funding Committed to Project	Uncommitted Funds	Revenues Received
SCAG	1.0	0.9	0.1	0.9
Interest Income	2.0	2.0	-	2.0
Bridge Replacement	13.9	13.9	-	13.9
Phase I Carryover	4.0	4.0	-	4.0
Maintenance and Operations Facility	-	-	-	-
Cities	11.0	-	11.0	-
Measure R - Pasadena to Azusa	810.5	777.0	33.5	479.9
Measure R - Azusa to Montclair	-	-	-	-
SANBAG	55.2	1.5	53.7	1.5
Federal TCSP	2.9	2.9	-	2.8
Federal Bus Intermodal Plan	9.0	9.0	-	4.6
Federal New Starts 2004 MTA Passthrough	4.0	4.0	-	4.0
Federal New Starts 2005 MTA Passthrough	0.5	0.5	-	0.5
Federal New Starts 2006 Corridor Study	2.5	2.5	-	2.5
Federal/Other	1,033.5	-	1,033.5	-
Total Revenues	1,950.0	818.2	1,131.8	516.6
	(a)	(b)	(c)	(d=a-b)
	Current Budget	Current Obligation	Current Expenditures	Current Available Balance
EXPENSES				
Program Management and Administration	108.9	99.0	96.4	9.9
Master Cooperative Agreements	11.0	3.3	2.7	7.7
Real Estate including ROW Acq	21.0	21.0	19.7	-
Special Programs	0.3	-	-	0.3
Procurement/Vehicles	60.0	-	-	60.0
Maintenance and Operations Facility Land	22.0	22.0	22.0	-
Construction - IFS	19.8	19.8	19.8	-
Construction - Pasadena to Azusa segment	328.9	328.9	300.0	-
Construction - Azusa to Montclair segment	1,181.0	-	-	1,181.0
Construction - M&O	47.0	44.0	35.1	2.0
Construction - Parking Structures	44.2	44.2	36.1	-
MTA Project Costs	64.0	64.0	14.3	-
Contingency	27.4	-	-	27.4
Project Reserve	14.5	-	-	14.5
Total Project	1,950.0	646.2	546.1	1,303.8
