

Phase 2 Exposition Metro Line Project

Monthly Project Status Report

July 2015





TABLE OF CONTENTS

PHASE 2 EXPO LINE PROJECT STATUS

TABLE OF CONTENTS	2
Phase 2 Exposition Metro Line Construction Authority Project Description	3
Phase 2 Exposition Metro Line Construction Authority Culver City to Santa Monica Segment.....	4
Project Management Issues	4
Key Activities Completed This Period	5
Key Future Activities	6
Phase 2 Exposition Metro Line Construction Authority Schedule Status	7
Critical Path Schedule.....	7
Schedule Narrative	9
Phase 2 Exposition Metro Line Construction Authority Financial Status.....	10
Project Cost Status and Analysis	10
Expo Baseline Activities	11
Metro Baseline Activities - Vehicles	12
Non-Baseline Activities.....	13
Phase 2 Exposition Metro Line Construction Authority Contract Status	14
Expo Phase 2 Design-Build Contract Status.....	14
Expo Phase 2 VBU Design-Build Contract Status	15
Expo Phase 2 OMF Contract Status.....	16
Expo Phase 2 Bikeway Contract Status	17



Phase 2 Exposition Metro Line Construction Authority Project Description

The Expo Phase 2 Project is located in the Westside of Los Angeles, extending approximately seven miles from the Expo Phase 1 terminus at Culver City Station to Santa Monica. The Phase 2 alignment begins at the terminus of Expo Phase 1 and utilizes the existing Exposition Right-of-Way (ROW), then diverges from the Exposition ROW and enters onto Colorado Avenue east of 17th Street. The alignment follows the center of Colorado Avenue to the proposed terminus in downtown Santa Monica in the vicinity of the intersection of 4th Street and Colorado Avenue.



Figure 1: Exposition Metro Line Construction Authority Phase 2 Alignment



Phase 2 Exposition Metro Line Construction Authority Culver City to Santa Monica Segment

Project Management Issues

Mainline Schedule

The latest Skanska/Rados Joint Venture (SRJV) progress schedule shows Substantial Completion at the beginning of December, which is approximately four (4) months beyond the contractual Substantial Completion date. The latest progress schedule includes a conservative 30 day review cycle for final approval of test results and a 20 day rain allowance. The delay is due to several factors, which include delayed site turnover to the track installation subcontractor, delayed ductbank installation, and vibration mitigation design and construction. The contractor and the Authority are working on a mitigation plan to minimize these delays. This latest schedule is still within the schedule contingency allocation, and should therefore not impact the overall revenue operations date. The Authority anticipates having the system substantially complete for turnover to Metro to begin Phase 2 testing and Pre-Revenue operations in October 2015.

City of Santa Monica

Terminus property condemnation has been filed with the court. A legal issues trial date has been set for November 2015.

Operations and Maintenance Facility (OMF)

The current project schedule shows Substantial Completion of the OMF in December 2015, which is over six (6) months later than the current Substantial Completion date of May 2015. The project's slip is due to damage to the train control laterals, delays with the track work installation in the wash facility, delays in the main and secondary building construction and delays to the procurement of long-lead electrical equipment. The OMF contractor is looking at recovery options. The Authority anticipates having the facility turned over to Metro in October 2015.

MSE Wall Settlement

An approximate 300 foot area of earthwork fill East of Centinela Ave. settled at a rate greater than anticipated. SRJV has contracted with a firm to perform pressure grouting in this area to stabilize the settlement. Inspection of the wall panels have shown the panels are performing as required. No delays to testing or turnover are anticipated.



Key Activities Completed This Period

Phase 2 Design-Build contractor, Skanska/Rados (SRJV)

- SRJV advanced remaining design elements. Staff worked with SRJV to resolve open issues.
- SRJV continued construction activities:
 - advanced OCS poles and wire;
 - advanced station platforms and C/S rooms;
 - advanced support poles for canopies/artwork and pavers at stations;
 - advanced soundwalls
 - advanced TPSS site work (TPSS6 and TPSS7);
 - advanced street improvements including street lighting and traffic signal installation; and
 - continued train control installation.
- SRJV advanced construction submittals and requests for information; Authority staff reviewed and collaborated to resolve previously rejected submittals.
- SCE, DWP, and communications providers continued to relocate facilities and provide new service.
- Continued Local Field Acceptance Testing (LFATs) and Systems Integration Testing (SITs) for systems and train control.
- CPUC acceptance of Overland Grade Crossing.

Venice Boulevard Underpass Design-Build contractor

- The Expo Phase 2 Contractor (SRJV) completed the remaining roadway construction work and continues final inspection with AHJ's and completion of punch list work.

Operations and Maintenance Facility, Kiewit Building Group (KBG)

- Track and Site Work:
 - continued coordination and installation of dry and wet utilities;
 - completed rail installation;
 - set SCE switchgear.
 - continued OCS pole and portal erection
- Main and Secondary Building:
 - completed main building roofing and interior drywall;
 - continued MEP installation;
 - continued installation of glazing.
- Wash Building & Cleaning Platform:
 - install roof at wash building;
 - hang precast panels.

Bikeway

- Soil mitigation completed, final DTSC review approval received.
- Grading, drainage, electrical conduit, bike light installation and paving in process.



Key Future Activities

Phase 2 Design-Build contractor, Skanska/Rados (SRJV)

- SRJV advance remaining design elements. Metro, Authority, and third party staff will continue to work with SRJV to resolve comments and open issues.
- SRJV will continue the following construction activities:
 - advance stations;
 - advance OCS wire installation;
 - install guideway lighting;
 - advance canopy poles and station paver installation;
 - advance street improvements;
 - SCE, DWP, and communication providers to finalize relocations and continue providing service to the remaining low voltage meters;
 - Continue LFATs and SITs for systems and train control.
 - Field review and CPUC acceptance of remaining grade crossings.

Venice Boulevard Underpass

- Finalize roadway and Culver City Plaza design and obtain third party approval.
- Expo Phase 2 Contractor (SRJV) will work on the roadway construction work punch list items.

Operations and Maintenance Facility contractor, Kiewit Building Group

- Continue Construction Safety Certification.
- Set interior equipment.
- Continue track installation.
- Continue start-up and activation meetings.
- Continue OCS wire and systems installation.
- Commence precast panel installation on wash building and cleaning platform
- Commence construction of guard shack;
- Commence installation of site lighting and parking areas;
- Energize train control bungalows and start LFATs.

Bikeway

- Complete construction, signing and striping.

General


- Continue coordination with the COLA, CSM, Metro, and Caltrans.
- Facilitate Fire Life Safety Committee meetings.
- Continue FEIR mitigation measures.

**EXPOSITION METRO LINE
CONSTRUCTION AUTHORITY**
Monthly Phase 2 Project Status Report
Period Ending – July 31, 2015




Phase 2 Exposition Metro Line Construction Authority Schedule Status

**Critical Path Schedule,
Period Ending July 31, 2015**

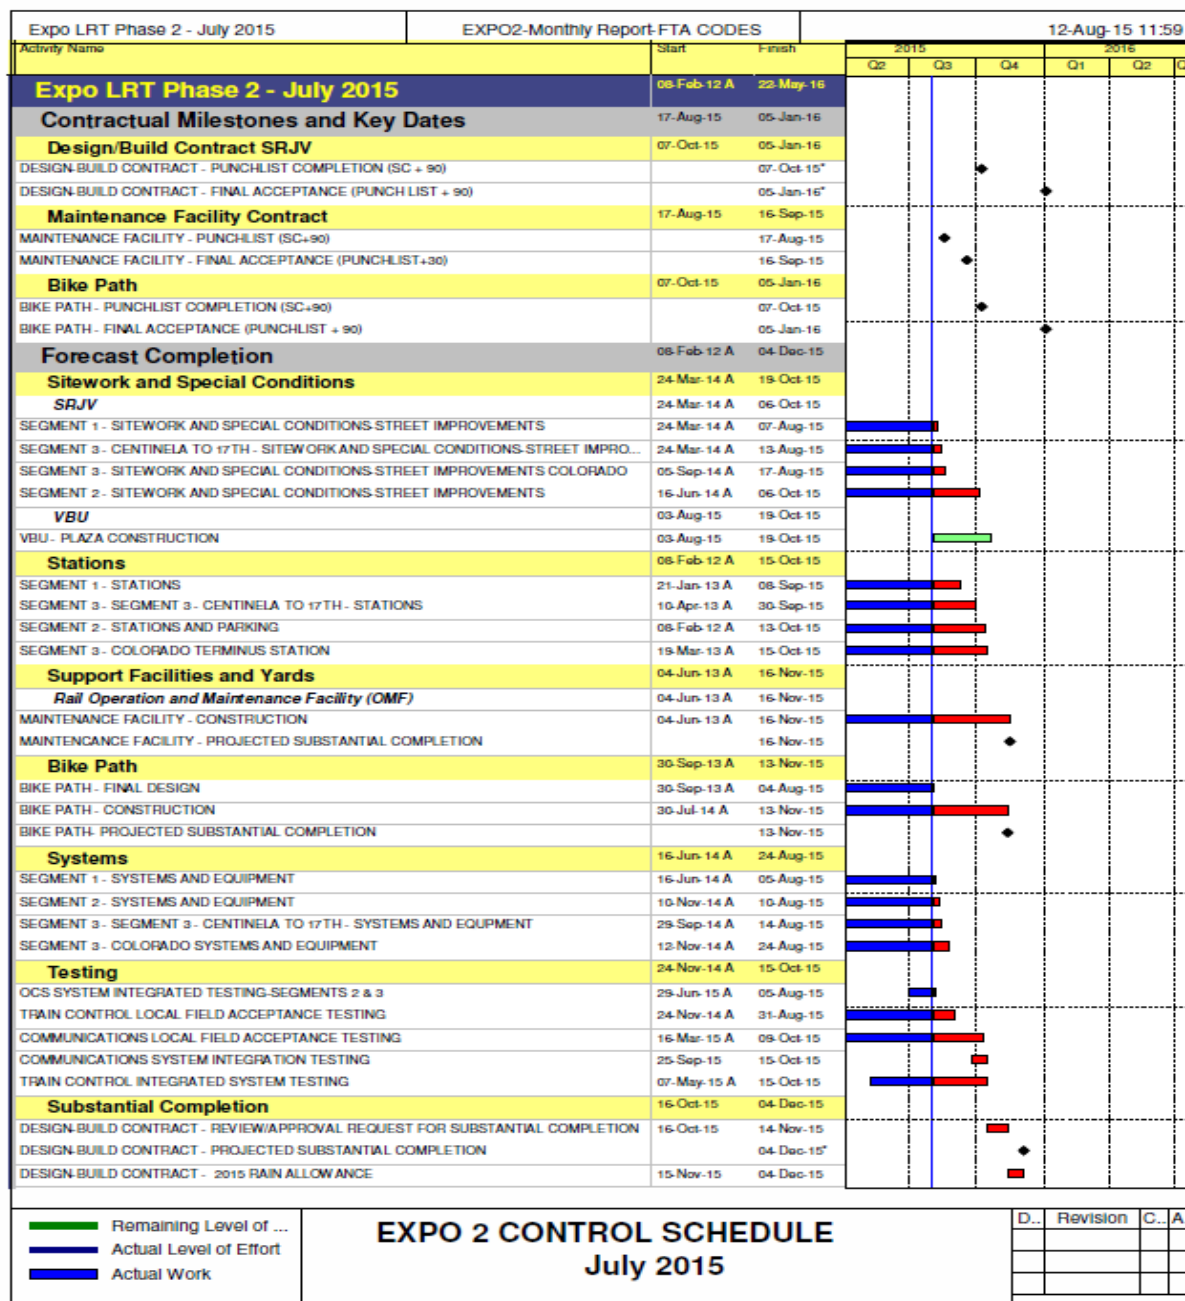



Critical Path Schedule Continued

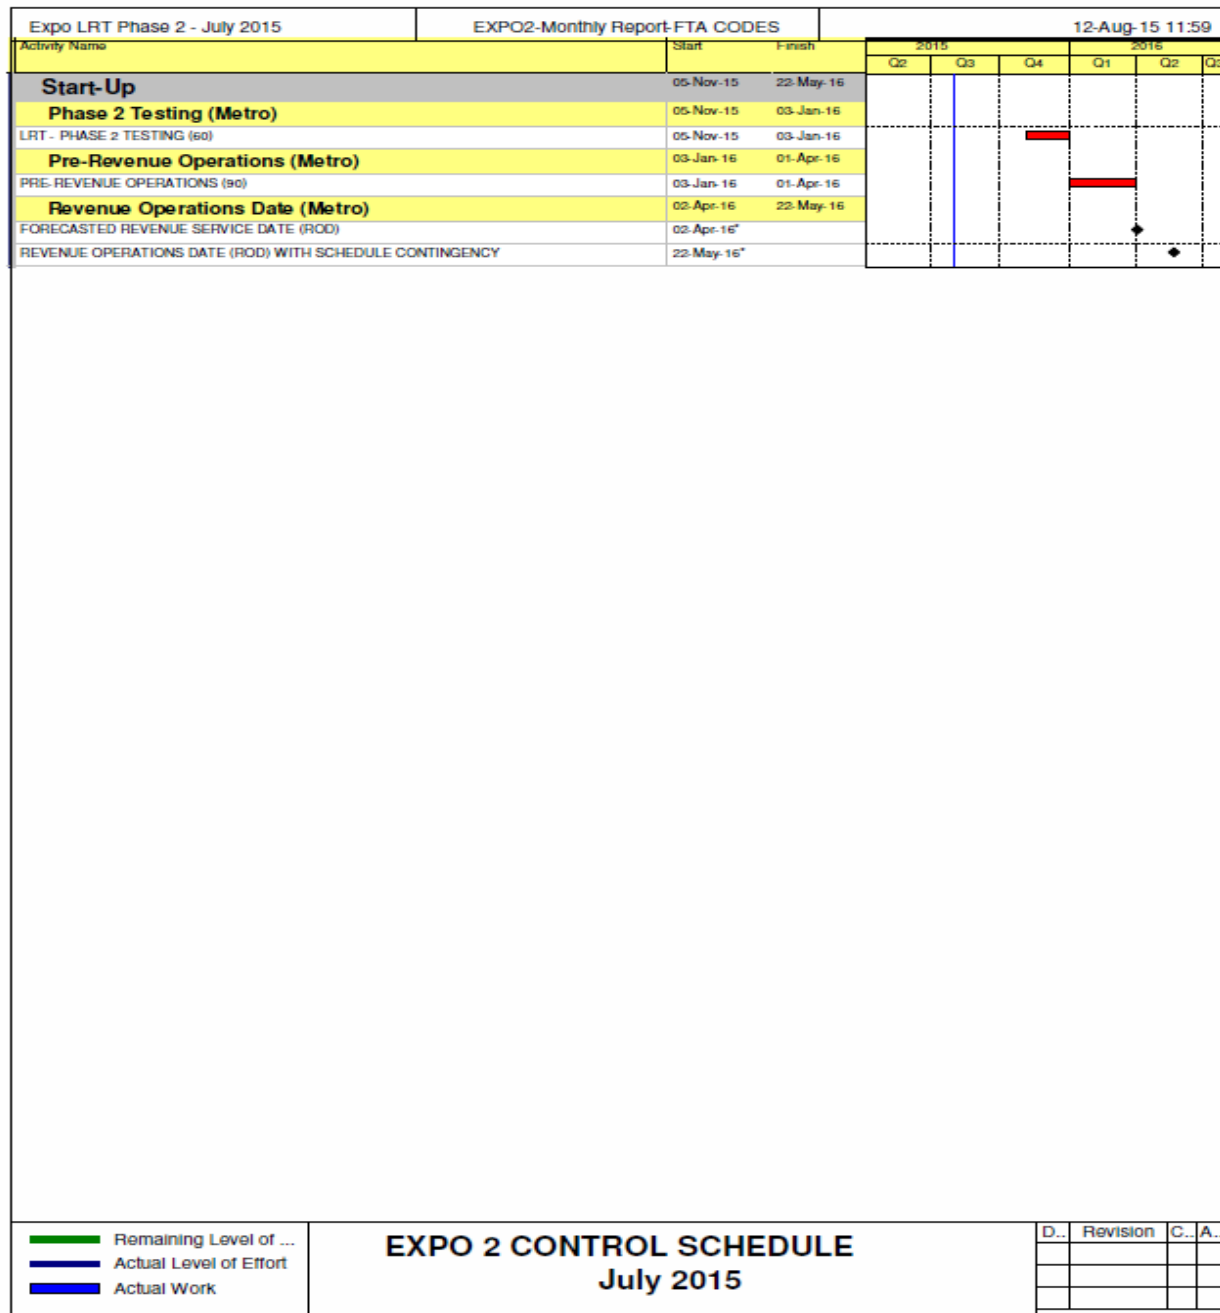



Schedule Narrative

Critical and Near-Critical Path Analysis

The Critical Path runs through the completion of the train control LFATs, followed by the dynamic train control testing from Centinela to the Terminus. The completion of the installation of the communications systems, followed by testing, is also on the Critical Path.

The coordination with third party utility owners is ongoing in order to provide power service to the project and support the systems testing phase which started in November 2014.

Project Float/ Schedule Contingency

On January 5, 2012, the Board of Directors authorized the Authority to include schedule contingency in accordance with Metro's Project Contingency procedure which resulted in a Revenue Operations Date of November 5, 2016. At the January 9, 2014 Board Meeting half of the contingency was released. If all the remaining Schedule Contingency were needed, the projected Revenue Operation Date would be May 22, 2016.

	Original Duration (days)	Days Released	Current Duration (days)
Schedule Contingency	334	167	167



Phase 2 Exposition Metro Line Construction Authority Financial Status

Project Cost Status and Analysis Expo/Metro Baseline

COST REPORT BY ELEMENT

UNITS IN MILLIONS

Element	Description	Original Budget	Current Budget	Commitments	Expenditures	Current Forecast	Forecast Variance Over/<Under>
C	CONSTRUCTION	766.3	759.8	688.0	609.5	759.8	-
R	RIGHT-OF-WAY	265.0	257.6	115.4	113.7	257.6	-
V	VEHICLES	202.1	202.1	202.1	77.7	202.1	-
P	PROFESSIONAL SERVICES	148.2	149.7	120.2	104.5	149.7	-
SC	SPECIAL CONDITIONS	63.6	81.9	66.5	58.3	81.9	-
PR	PROJECT RESERVE	66.0	60.1	-	-	60.1	-
TOTAL		1,511.2	1,511.2	1,192.2	963.6	1,511.2	-

NOTE: Expenditures are Paid-to-Date through 6/30/15

Original Budget and Current Budget:

The Life of Project Budget for the Phase 2 Exposition Metro Line Project was adopted in March 2011 for a value of \$1.511 billion.

Current Forecast:

The total project forecast at completion remains the same as the current budget of \$1.511 billion.



Project Operating Budget Summary in Millions of Dollars



Expo

Sources & Uses of Funds - Phase 2

Status as of July 31, 2015

Metro / Expo Baseline Activities

Sources of Funds (millions)

A

B

C = A - B

Source	Budget	Funding Committed	Uncommitted
Prop A 35%	\$ 224.0	\$ 170.3	\$ 53.7
Prop C 25%	\$ 5.8	\$ 2.6	\$ 3.2
Measure R	\$ 908.9	\$ 631.3	\$ 277.6
Prop 1B Bonds - PTMISEA	\$ 48.9	\$ 15.2	\$ 33.7
Prop 1B Bonds - SLPP	\$ 28.3	\$ 28.3	\$ -
Regional Improvement Program (State)	\$ 47.8	\$ 47.8	\$ 0.0
Local Agency Contribution	\$ 45.3	\$ 45.3	\$ 0.0
	\$ 1,309.1	\$ 940.8	\$ 368.3
Total Sources:	\$ 1,309.1	\$ 940.8	\$ 368.3

Uses of Funds by Element (millions)

A

B

C

D = A - B

Element	Budget	Committed	Paid	Uncommitted
Design-Build Corridor	\$ 594.5	\$ 558.8	\$ 501.6	\$ 35.8
Other Construction Elements	\$ 165.4	\$ 129.3	\$ 107.9	\$ 36.1
Right-of-Way	\$ 257.6	\$ 115.4	\$ 113.7	\$ 142.2
Professional Services	\$ 149.7	\$ 120.2	\$ 104.5	\$ 29.5
Special Conditions	\$ 81.9	\$ 66.5	\$ 58.3	\$ 15.4
Project Reserve	\$ 60.1	\$ -	\$ -	\$ 60.1
Total Uses:	\$ 1,309.1	\$ 990.1	\$ 885.9	\$ 319.0

Paid-to-Date through 6/30/15



Project Operating Budget Summary in Millions of Dollars



Expo

Sources & Uses of Funds - Phase 2

Status as of July 31, 2015

Metro / Expo Baseline Activities - Vehicles

Sources of Funds (millions)

A

B

C = A - B

Source	Budget	Funding Committed	Uncommitted
RSTP (Federal) for LRVs	\$ 7.7	\$ 7.7	\$ -
CMAQ (Federal) for LRVs	\$ 41.3	\$ 41.3	\$ -
Reg. Imp. Prog. (Federal) for LRVs	\$ 153.1	\$ 153.1	\$ -
	\$ 202.1	\$ 202.1	\$ -
Total Sources:	\$ 202.1	\$ 202.1	\$ -

Uses of Funds by Element (millions)

A

B

C

D = A - B

Element	Budget	Committed	Paid	Uncommitted
Vehicles	\$ 202.1	\$ 202.1	\$ 77.7	\$ -
Total Uses:	\$ 202.1	\$ 202.1	\$ 77.7	\$ -

Paid-to-Date through 6/30/15



Project Operating Budget Summary in Millions of Dollars



Expo

Sources & Uses of Funds - Phase 2

Status as of July 31, 2015

Non - Baseline Activities

Sources of Funds (millions)

A B C = A - B

Source	Budget	Funding Committed	Uncommitted
Project Revenue: City of LA Betterment	\$ 5.4	\$ 5.4	\$ -
Project Revenue: Metro	\$ 3.9	\$ 3.9	\$ -
Project Revenue: City of Santa Monica Betterment	\$ 20.6	\$ 20.6	\$ -
Total Sources:	\$ 29.9	\$ 29.9	\$ -

Uses of Funds by Element (millions)

A B C D = A - B

Element	Budget	Committed	Paid	Uncommitted
Design-Build Betterments				
COLA - Sepulveda Blvd Bridge & Aerial Station (Diff.)	\$ 5.3	\$ 5.3	\$ 4.1	\$ -
COLA - Greenway Project Culvert	\$ 0.1	\$ 0.1	\$ 0.1	\$ -
Metro - Various Betterments (Metro Board Approved 4/17/14)	\$ 3.9	\$ 2.1	\$ 1.5	\$ 1.8
City of Santa Monica Water System Betterments	\$ 1.6	\$ 1.6	\$ 1.5	\$ 0.0
City of Santa Monica PCC Funding Agreement	\$ 0.5	\$ 0.4	\$ -	\$ 0.1
City of Santa Monica Storm Drain Laterals	\$ 0.3	\$ 0.3	\$ 0.2	\$ -
26th Street & 17th Street Station Betterments P.E.	\$ 0.4	\$ 0.4	\$ 0.4	\$ -
26th Street & 17th Street Station Betterments Construction	\$ 7.7	\$ 6.4	\$ 5.5	\$ 1.3
4th Street Terminus Station P.E.	\$ 0.5	\$ 0.4	\$ 0.4	\$ 0.1
4th Street Terminus Station Construction	\$ 8.0	\$ 7.3	\$ 6.2	\$ 0.7
CSM Cont. Release - Jacob Guard Rails, Pavers & Landscaping	\$ 1.8	\$ 1.4	\$ -	\$ 0.4
Total Uses:	\$ 29.9	\$ 25.6	\$ 19.8	\$ 4.3

Paid-to-Date through 6/30/15



Expo Phase 2 Design-Build Contract Status

Expo Phase 2 Contractor: Skanska/Rados	Contract No.: XP8902-002 Status as of: 31-Jul-15																													
Progress/Work Completed: See Page 6 Areas of Concern: See Pages 4 and 5	Major Activities (In Progress): See Page 5 and 6 Major Activities Next Period: See Page 6																													
		Original Contract Dates	Time Extension	Current Contract	Forecast	Variance CDs																								
	Substantial Completion	07/10/15	0	07/10/15	07/10/15	0																								
	Contract Completion	01/08/16	0	01/08/16	01/08/16	0																								
<u>Schedule Summary:</u> Date of Award: 05/13/11 Limited Notice to Proceed: 05/19/11 Original Contract Duration: 1700 Current Contract Duration: 1700 Elapsed Time from NTP: 1,535	<u>Cost Summary:</u> <table><tr><td></td><td colspan="2">\$ In 000's</td></tr><tr><td></td><td>Baseline Project</td><td>Betterments/ Modifications</td></tr><tr><td>1. Award Value:</td><td>541,651.27</td><td>5,278.94</td></tr><tr><td>2. Executed Modifications:</td><td></td><td>53,087.10</td></tr><tr><td>3. Approved Change Orders:</td><td>4709.84</td><td></td></tr><tr><td>4. Current Contract Value (1 + 2 + 3):</td><td>546,361.10</td><td>58,366.03</td></tr><tr><td>5. Pending Changes:</td><td>170.22</td><td>2,813.82</td></tr><tr><td>6. Incurred Cost:</td><td>506,155.18</td><td>55,136.96</td></tr></table>							\$ In 000's			Baseline Project	Betterments/ Modifications	1. Award Value:	541,651.27	5,278.94	2. Executed Modifications:		53,087.10	3. Approved Change Orders:	4709.84		4. Current Contract Value (1 + 2 + 3):	546,361.10	58,366.03	5. Pending Changes:	170.22	2,813.82	6. Incurred Cost:	506,155.18	55,136.96
	\$ In 000's																													
	Baseline Project	Betterments/ Modifications																												
1. Award Value:	541,651.27	5,278.94																												
2. Executed Modifications:		53,087.10																												
3. Approved Change Orders:	4709.84																													
4. Current Contract Value (1 + 2 + 3):	546,361.10	58,366.03																												
5. Pending Changes:	170.22	2,813.82																												
6. Incurred Cost:	506,155.18	55,136.96																												



Expo Phase 2 VBU Design-Build Contract Status

Expo Phase 2 Contractor: Balfour Beatty Infrastructure, Inc.	Contract No.: XP8901-828 Status as of: 31-Jul-15																																					
Progress/Work Completed: See Page 6 Areas of Concern: See Pages 4 and 5	Major Activities (In Progress): See Page 5 and 6 Major Activities Next Period: See Page 6																																					
		Original Contract Dates	Time Extension	Current Contract	Forecast	Variance CDs																																
	Substantial Completion	07/12/13	262	03/31/14	03/31/14	0																																
<u>Schedule Summary:</u> Date of Award: 08/04/11 Limited Notice to Proceed: 09/01/11 Original Contract Duration: 680 Current Contract Duration: 796 Elapsed Time from NTP: 1,430	<u>Cost Summary:</u> <table><tr><td></td><td></td><td colspan="2">\$ In 000's</td></tr><tr><td></td><td></td><td>Baseline Project</td><td>Betterments/ Modifications</td></tr><tr><td>1. Award Value:</td><td></td><td>15,675.00</td><td></td></tr><tr><td>2. Executed Modifications:</td><td></td><td>(1,640.84)</td><td>1,277.00</td></tr><tr><td>3. Approved Change Orders:</td><td></td><td>1,184.57</td><td>-</td></tr><tr><td>4. Current Contract Value (1 + 2 + 3):</td><td></td><td>15,218.73</td><td>1,277.00</td></tr><tr><td>5. Pending Changes:</td><td></td><td>-</td><td></td></tr><tr><td>6. Incurred Cost:</td><td></td><td>14,943.83</td><td>1,551.90</td></tr></table>								\$ In 000's				Baseline Project	Betterments/ Modifications	1. Award Value:		15,675.00		2. Executed Modifications:		(1,640.84)	1,277.00	3. Approved Change Orders:		1,184.57	-	4. Current Contract Value (1 + 2 + 3):		15,218.73	1,277.00	5. Pending Changes:		-		6. Incurred Cost:		14,943.83	1,551.90
		\$ In 000's																																				
		Baseline Project	Betterments/ Modifications																																			
1. Award Value:		15,675.00																																				
2. Executed Modifications:		(1,640.84)	1,277.00																																			
3. Approved Change Orders:		1,184.57	-																																			
4. Current Contract Value (1 + 2 + 3):		15,218.73	1,277.00																																			
5. Pending Changes:		-																																				
6. Incurred Cost:		14,943.83	1,551.90																																			

Expo Phase 2			Contract No.: XP8902-016					
Contractor: Kiewitt Building Group								
O&M Facility			Status as of: 31-Jul-15					
Progress/Work Completed: See Page 6 Areas of Concern: See Pages 4 and 5			Major Activities (In Progress): See Page 5 and 6 Major Activities Next Period: See Page 6					
				Original Contract Dates	Time Extension	Current Contract	Forecast	Variance CDs
			Substantial Completion	11/25/14	176	05/20/15	05/20/15	0
Schedule Summary:			Cost Summary:				\$ In 000's	
							Baseline Project	Betterments/ Modifications
			1. Award Value:				99,930.56	
Date of Award:	05/03/13		2. Executed Modifications:					(180.80)
Limited Notice to Proceed:	06/03/13		3. Approved Change Orders:				2,691.53	-
Original Contract Duration:	540		4. Current Contract Value (1 + 2 + 3):				102,622.09	(180.80)
Current Contract Duration:	540		5. Pending Changes:				262.84	98.62
Elapsed Time from NTP:	789		6. Incurred Cost:				82,816.74	(72.55)

[illegible]
