

Phase 2 Exposition Metro Line Project

Monthly Project Status Report

November 2015





TABLE OF CONTENTS

PHASE 2 EXPO LINE PROJECT STATUS

TABLE OF CONTENTS 2

Phase 2 Exposition Metro Line Construction Authority Project Description 3

Phase 2 Exposition Metro Line Construction Authority Culver City to Santa Monica Segment..... 4

Project Management Issues 4

Key Activities Completed This Period 5

Key Future Activities 6

Phase 2 Exposition Metro Line Construction Authority Schedule Status 7

Critical Path Schedule..... 7

Schedule Narrative 8

Phase 2 Exposition Metro Line Construction Authority Financial Status..... 9

Project Cost Status and Analysis..... 9

Expo Baseline Activities 10

Metro Baseline Activities - Vehicles..... 11

Non-Baseline Activities..... 12

Phase 2 Exposition Metro Line Construction Authority Contract Status 13

Expo Phase 2 Design-Build Contract Status..... 13

Expo Phase 2 VBU Design-Build Contract Status 14

Expo Phase 2 OMF Contract Status..... 15

Expo Phase 2 Bikeway Contract Status 16



Phase 2 Exposition Metro Line Construction Authority Project Description

The Expo Phase 2 Project is located in the Westside of Los Angeles, extending approximately seven miles from the Expo Phase 1 terminus at Culver City Station to Santa Monica. The Phase 2 alignment begins at the terminus of Expo Phase 1 and utilizes the existing Exposition Right-of-Way (ROW), then diverges from the Exposition ROW and enters onto Colorado Avenue east of 17th Street. The alignment follows the center of Colorado Avenue to the proposed terminus in downtown Santa Monica in the vicinity of the intersection of 4th Street and Colorado Avenue.



Figure 1: Exposition Metro Line Construction Authority Phase 2 Alignment



Phase 2 Exposition Metro Line Construction Authority Culver City to Santa Monica Segment

Project Management Issues

Mainline Schedule

The latest Skanska/Rados Joint Venture (SRJV) progress schedule shows Substantial Completion at the end of December, which is approximately five (5) months beyond the contractual Substantial Completion date. The delay is due to several factors, which include delayed site turnover to the track installation subcontractor, delayed ductbank installation, and vibration mitigation design and construction. The contractor and the Authority are working on a mitigation plan to minimize these delays. This latest schedule includes a conservative 30 day review cycle for final approval of test results and a 20 day rain allowance and is still within the schedule contingency allocation, and should therefore not impact the overall revenue operations date. The Authority submitted the application for turnover to Metro to begin Phase 2 testing and Pre-Revenue operations on November 25, 2015.

City of Santa Monica

Terminus property condemnation has been filed with the court. A trial date was set by the court for the fall of 2016.

Operations and Maintenance Facility (OMF)

The current project schedule shows Substantial Completion of the OMF in December 2015, which is over six (6) months later than the current Substantial Completion date of May 2015. The project's slip is due to damage to the train control laterals, delays with the track work installation in the wash facility, the main and secondary building construction and the procurement of long-lead electrical equipment. The OMF contractor is looking at recovery options. The Authority anticipates having the facility turned over to Metro in December 2015.



Key Activities Completed This Period

Phase 2 Design-Build contractor, Skanska/Rados (SRJV)

- Continued street improvements
- Continued to obtain street improvement “Finals” from COLA and CSM
- Completed soil stabilization grouting from Carmelita to Centinela and resumed roadway improvements at this section of the alignment
- Completed communications device installation at stations
- Continued electrical and communications finishes (labeling, etc.) at station electrical and C/S rooms
- Continued irrigation, landscaping, signage and fencing
- Completed Phase 1 Train Control dynamic testing
- Continued communication systems testing
- Punchlist preparation and safety certification in progress

Venice Boulevard Underpass Design-Build contractor

- The Expo Phase 2 Contractor (SRJV) completed the remaining roadway construction work and continues final inspection with AHJ’s and completion of punch list work.

Operations and Maintenance Facility, Kiewit Building Group (KBG)

- Continued to install finishes and shop equipment at the buildings
- Continued interior and exterior finishes at the Guard Shack
- Continued the installation of site finishes
- Continued the startup process for building systems
- Started building systems testing and training
- Started shop equipment testing and training
- Continued equipment installation and wiring at the main data room
- Continued Train Control testing
- Commenced signage installation
- Commenced punchlist preparation
- Commenced safety certification

Bikeway

- Final DTSC review approval received.
- Signing and striping nearing completion.
- Start punch list walks



Key Future Activities

Phase 2 Design-Build contractor, Skanska/Rados (SRJV)

- SRJV advance remaining design elements. Metro, Authority, and third party staff will continue to work with SRJV to resolve comments and open issues.
- SRJV will continue the following construction activities:
 - complete stations;
 - test guideway lighting;
 - advance landscaping
 - SCE, DWP, and communication providers to finalize relocations and continue providing service to the remaining low voltage meters;
 - Continue LFATs and SITs for systems and train control.

Venice Boulevard Underpass

- Commence roadway and Culver City Plaza construction.
- Expo Phase 2 Contractor (SRJV) will work on the roadway construction work punch list items.

Operations and Maintenance Facility contractor, Kiewit Building Group

- Continue Construction Safety Certification.
- Set interior equipment.
- Continue start-up and activation meetings.
- Continue systems installation.
- Continue construction of guard shack;
- Continue installation of site lighting, parking areas and site walls;
- Continue LFATs and commence SITs.
- Commence punchlist preparation.

Bikeway

- Complete construction, signing and striping.
- Bikeway from Carmelina to Centinela intersection


General

- Continue coordination with the COLA, CSM, Metro, and Caltrans.
- Facilitate Fire Life Safety Committee meetings.
- Continue FEIR mitigation measures.



Phase 2 Exposition Metro Line Construction Authority Schedule Status

**Critical Path Schedule,
Period Ending November 30, 2015**

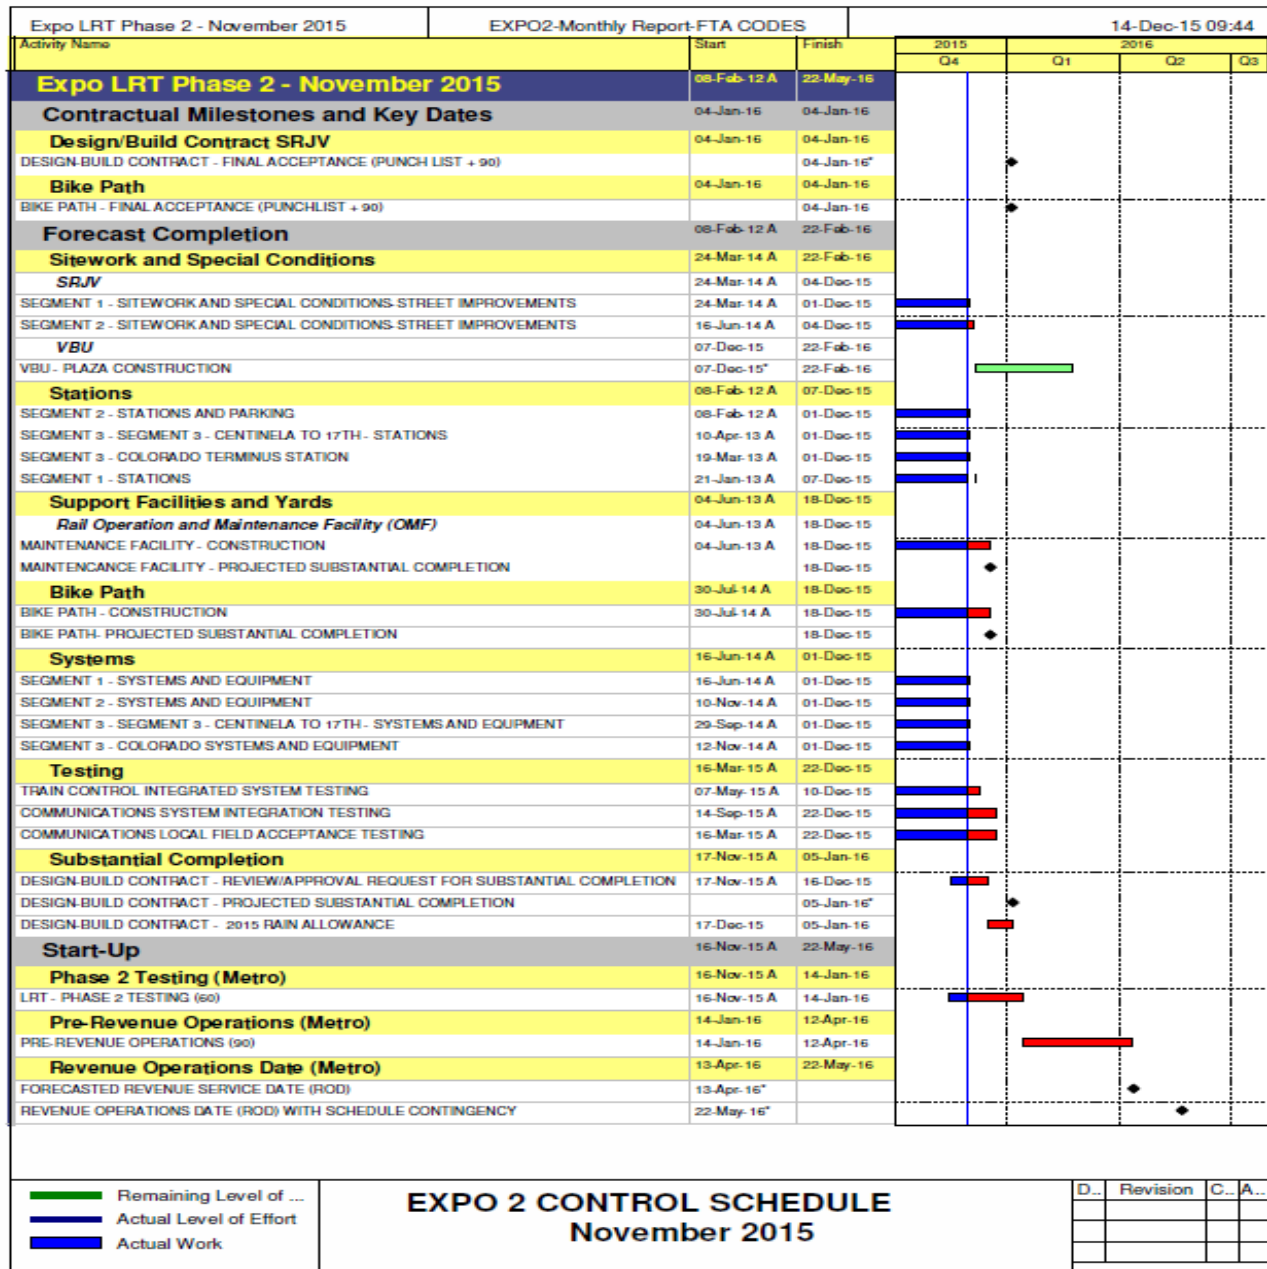



Schedule Narrative

Critical and Near-Critical Path Analysis

The critical path runs through completing the Metro Phase 2 Testing. At the OMF, the Critical Path runs through completing the train control, communications and building systems testing.

Project Float/ Schedule Contingency

On January 5, 2012, the Board of Directors authorized the Authority to include schedule contingency in accordance with Metro's Project Contingency procedure which resulted in a Revenue Operations Date of November 5, 2016. At the January 9, 2014 Board Meeting half of the contingency was released. If all the remaining Schedule Contingency were needed, the projected Revenue Operation Date would be May 22, 2016.

	Original Duration (days)	Days Released	Current Duration (days)
Schedule Contingency	334	167	167



Phase 2 Exposition Metro Line Construction Authority Financial Status

**Project Cost Status and Analysis
Expo/Metro Baseline**

COST REPORT BY ELEMENT

UNITS IN MILLIONS

Element	Description	Original Budget	Current Budget	Commitments	Expenditures	Current Forecast	Forecast Variance Over/<Under>
C	CONSTRUCTION	766.3	759.8	692.2	647.5	759.8	-
R	RIGHT-OF-WAY	265.0	257.6	115.3	113.7	257.6	-
V	VEHICLES	202.1	202.1	202.1	80.1	202.1	-
P	PROFESSIONAL SERVICES	148.2	149.7	124.2	112.3	149.7	-
SC	SPECIAL CONDITIONS	63.6	81.9	66.7	59.6	81.9	-
PR	PROJECT RESERVE	66.0	60.1	-	-	60.1	-
TOTAL		1,511.2	1,511.2	1,200.5	1,013.2	1,511.2	-

NOTE: Expenditures are Paid-to-Date through 10/31/15

Original Budget and Current Budget:

The Life of Project Budget for the Phase 2 Exposition Metro Line Project was adopted in March 2011 for a value of \$1.511 billion.

Current Forecast:

The total project forecast at completion remains the same as the current budget of \$1.511 billion.



Project Operating Budget Summary in Millions of Dollars



Expo

*Sources & Uses of Funds - Phase 2
 Status as of November 30, 2015*

Metro / Expo Baseline Activities

Sources of Funds (millions)	A	B	C = A - B	
Source	Budget	Funding Committed	Uncommitted	
Prop A 35%	\$ 208.6	\$ 208.6	\$ -	
Prop C 25%	\$ 5.8	\$ 2.6	\$ 3.2	
Measure R	\$ 908.8	\$ 908.8	\$ -	
Prop 1B Bonds - PTMISEA	\$ 64.4	\$ 64.4	\$ -	
Prop 1B Bonds - SLPP	\$ 28.3	\$ 28.3	\$ -	
Regional Improvement Program (State)	\$ 47.8	\$ 47.8	\$ 0.0	
Local Agency Contribution	\$ 45.3	\$ 45.3	\$ 0.0	
	\$ 1,309.1	\$ 1,305.8	\$ 3.3	
Total Sources:	\$ 1,309.1	\$ 1,305.8	\$ 3.3	

Uses of Funds by Element (millions)	A	B	C	D = A - B
Element	Budget	Committed	Paid	Uncommitted
Design-Build Corridor	\$ 594.5	\$ 560.4	\$ 521.1	\$ 34.2
Other Construction Elements	\$ 165.4	\$ 131.8	\$ 126.5	\$ 33.5
Right-of-Way	\$ 257.6	\$ 115.3	\$ 113.7	\$ 142.3
Professional Services	\$ 149.7	\$ 124.2	\$ 112.3	\$ 25.5
Special Conditions	\$ 81.9	\$ 66.7	\$ 59.6	\$ 15.1
Project Reserve	\$ 60.1	\$ -	\$ -	\$ 60.1
Total Uses:	\$ 1,309.1	\$ 998.4	\$ 933.1	\$ 310.7

Paid-to-Date through 10/31/15



Project Operating Budget Summary in Millions of Dollars



Sources & Uses of Funds - Phase 2
 Status as of November 30, 2015

Metro / Expo Baseline Activities - Vehicles

Sources of Funds (millions)	A	B	C = A - B	
Source	Budget	Funding Committed	Uncommitted	
RSTP (Federal) for LRVs	\$ 7.7	\$ 7.7	\$	-
CMAQ (Federal) for LRVs	\$ 41.3	\$ 41.3	\$	-
Reg. Imp. Prog. (Federal) for LRVs	\$ 153.1	\$ 153.1	\$	-
	\$ 202.1	\$ 202.1	\$	-
Total Sources:	\$ 202.1	\$ 202.1	\$	-

Uses of Funds by Element (millions)	A	B	C	D = A - B
Element	Budget	Committed	Paid	Uncommitted
Vehicles	\$ 202.1	\$ 202.1	\$ 80.1	\$ -
Total Uses:	\$ 202.1	\$ 202.1	\$ 80.1	\$ -

Paid-to-Date through 10/31/15



Project Operating Budget Summary in Millions of Dollars



*Sources & Uses of Funds - Phase 2
Status as of November 30, 2015*

Non - Baseline Activities

Sources of Funds (millions)	A	B	C = A - B	
Source	Budget	Funding Committed	Uncommitted	
Project Revenue: City of LA Betterment	\$ 5.4	\$ 5.4	\$ -	
Project Revenue: Metro	\$ 3.9	\$ 3.9	\$ -	
Project Revenue: City of Santa Monica Betterment	\$ 20.2	\$ 20.2	\$ -	
Total Sources:	\$ 29.5	\$ 29.5	\$ -	

Uses of Funds by Element (millions)	A	B	C	D = A - B
Element	Budget	Committed	Paid	Uncommitted
Design-Build Betterments				
COLA - Sepulveda Blvd Bridge & Aerial Station (Diff.)	\$ 5.3	\$ 5.3	\$ 5.1	\$ -
COLA - Greenway Project Culvert	\$ 0.1	\$ 0.1	\$ 0.1	\$ -
Metro - Various Betterments (Metro Board Approved 4/17/14)	\$ 3.9	\$ 2.8	\$ 2.0	\$ 1.1
City of Santa Monica Water System Betterments	\$ 1.6	\$ 1.6	\$ 1.5	\$ -
City of Santa Monica PCC Funding Agreement	\$ 0.5	\$ 0.5	\$ -	\$ -
City of Santa Monica Storm Drain Laterals	\$ 0.3	\$ 0.3	\$ 0.2	\$ -
26th Street & 17th Street Station Betterments P.E	\$ 0.4	\$ 0.4	\$ 0.4	\$ -
26th Street & 17th Street Station Betterments Construction	\$ 7.3	\$ 6.8	\$ 5.6	\$ 0.5
4th Street Terminus Station P.E	\$ 0.5	\$ 0.4	\$ 0.4	\$ 0.1
4th Street Terminus Station Construction	\$ 8.0	\$ 7.7	\$ 5.4	\$ 0.3
CSM Cont. Release - Jacob Guard Rails, Pavers & Landscaping	\$ 1.8	\$ 1.7	\$ -	\$ 0.1
Total Uses:	\$ 29.5	\$ 27.5	\$ 20.6	\$ 2.0

Paid-to-Date through 10/31/15



Expo Phase 2 Design-Build Contract Status

<p>Expo Phase 2 Contractor: Skanska/Rados</p>	<p>Contract No.: XP8902-002</p> <p>Status as of: 30-Nov-15</p>																																		
<p>Progress/Work Completed: See Page 6</p> <p>Areas of Concern: See Pages 4 and 5</p>	<p>Major Activities (In Progress): See Page 5 and 6</p> <p>Major Activities Next Period: See Page 6</p> <table border="1" data-bbox="636 1138 1505 1444"> <thead> <tr> <th></th> <th>Original Contract Dates</th> <th>Time Extension</th> <th>Current Contract</th> <th>Forecast</th> <th>Variance CDs</th> </tr> </thead> <tbody> <tr> <td>Substantial Completion</td> <td>07/10/15</td> <td>0</td> <td>07/10/15</td> <td>07/10/15</td> <td>0</td> </tr> <tr> <td>Contract Completion</td> <td>01/08/16</td> <td>0</td> <td>01/08/16</td> <td>01/08/16</td> <td>0</td> </tr> <tr> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> </tr> <tr> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> </tr> </tbody> </table>						Original Contract Dates	Time Extension	Current Contract	Forecast	Variance CDs	Substantial Completion	07/10/15	0	07/10/15	07/10/15	0	Contract Completion	01/08/16	0	01/08/16	01/08/16	0												
	Original Contract Dates	Time Extension	Current Contract	Forecast	Variance CDs																														
Substantial Completion	07/10/15	0	07/10/15	07/10/15	0																														
Contract Completion	01/08/16	0	01/08/16	01/08/16	0																														
<p><u>Schedule Summary:</u></p> <p>Date of Award: 05/13/11</p> <p>Limited Notice to Proceed: 05/19/11</p> <p>Original Contract Duration: 1700</p> <p>Current Contract Duration: 1700</p> <p>Elapsed Time from NTP: 1,657</p>	<p><u>Cost Summary:</u></p> <table border="1" data-bbox="636 1453 1505 1873"> <thead> <tr> <th rowspan="2"></th> <th colspan="2">\$ In 000's</th> </tr> <tr> <th>Baseline Project</th> <th>Betterments/ Modifications</th> </tr> </thead> <tbody> <tr> <td>1. Award Value:</td> <td>541,651.27</td> <td>5,278.94</td> </tr> <tr> <td>2. Executed Modifications:</td> <td></td> <td>55,409.63</td> </tr> <tr> <td>3. Approved Change Orders:</td> <td>5619.22</td> <td></td> </tr> <tr> <td>4. Current Contract Value (1 + 2 + 3):</td> <td>547,270.48</td> <td>60,688.57</td> </tr> <tr> <td>5. Pending Changes:</td> <td>80.38</td> <td>1,487.41</td> </tr> <tr> <td>6. Incurred Cost:</td> <td>527,761.60</td> <td>57,947.99</td> </tr> </tbody> </table>						\$ In 000's		Baseline Project	Betterments/ Modifications	1. Award Value:	541,651.27	5,278.94	2. Executed Modifications:		55,409.63	3. Approved Change Orders:	5619.22		4. Current Contract Value (1 + 2 + 3):	547,270.48	60,688.57	5. Pending Changes:	80.38	1,487.41	6. Incurred Cost:	527,761.60	57,947.99							
	\$ In 000's																																		
	Baseline Project	Betterments/ Modifications																																	
1. Award Value:	541,651.27	5,278.94																																	
2. Executed Modifications:		55,409.63																																	
3. Approved Change Orders:	5619.22																																		
4. Current Contract Value (1 + 2 + 3):	547,270.48	60,688.57																																	
5. Pending Changes:	80.38	1,487.41																																	
6. Incurred Cost:	527,761.60	57,947.99																																	



Expo Phase 2 VBU Design-Build Contract Status

<p>Expo Phase 2 Contractor: Balfour Beatty Infrastructure, Inc.</p>	<p>Contract No.: XP8901-828 Status as of: 30-Nov-15</p>																																				
<p>Progress/Work Completed: See Page 6</p> <p>Areas of Concern: See Pages 4 and 5</p>	<p>Major Activities (In Progress): See Page 5 and 6</p> <p>Major Activities Next Period: See Page 6</p>																																				
		<p>Original Contract Dates</p>	<p>Time Extension</p>	<p>Current Contract</p>	<p>Forecast</p>	<p>Variance CDs</p>																															
	<p>Substantial Completion</p>	<p>07/12/13</p>	<p>262</p>	<p>03/31/14</p>	<p>03/31/14</p>	<p>0</p>																															
<p>Schedule Summary:</p> <p>Date of Award: 08/04/11</p> <p>Limited Notice to Proceed: 09/01/11</p> <p>Original Contract Duration: 680</p> <p>Current Contract Duration: 796</p> <p>Elapsed Time from NTP: 1,552</p>	<p>Cost Summary:</p> <table border="1"> <thead> <tr> <th colspan="2"></th> <th colspan="2" style="text-align: center;">\$ In 000's</th> </tr> <tr> <th colspan="2"></th> <th style="text-align: center;">Baseline Project</th> <th style="text-align: center;">Betterments/ Modifications</th> </tr> </thead> <tbody> <tr> <td>1. Award Value:</td> <td></td> <td style="text-align: right;">15,675.00</td> <td></td> </tr> <tr> <td>2. Executed Modifications:</td> <td></td> <td style="text-align: right;">(1,640.84)</td> <td style="text-align: right;">1,277.00</td> </tr> <tr> <td>3. Approved Change Orders:</td> <td></td> <td style="text-align: right;">1,184.57</td> <td style="text-align: center;">-</td> </tr> <tr> <td>4. Current Contract Value (1 + 2 + 3):</td> <td></td> <td style="text-align: right;">15,218.73</td> <td style="text-align: right;">1,277.00</td> </tr> <tr> <td>5. Pending Changes:</td> <td></td> <td style="text-align: center;">-</td> <td></td> </tr> <tr> <td>6. Incurred Cost:</td> <td></td> <td style="text-align: right;">14,943.83</td> <td style="text-align: right;">1,551.90</td> </tr> </tbody> </table>							\$ In 000's				Baseline Project	Betterments/ Modifications	1. Award Value:		15,675.00		2. Executed Modifications:		(1,640.84)	1,277.00	3. Approved Change Orders:		1,184.57	-	4. Current Contract Value (1 + 2 + 3):		15,218.73	1,277.00	5. Pending Changes:		-		6. Incurred Cost:		14,943.83	1,551.90
		\$ In 000's																																			
		Baseline Project	Betterments/ Modifications																																		
1. Award Value:		15,675.00																																			
2. Executed Modifications:		(1,640.84)	1,277.00																																		
3. Approved Change Orders:		1,184.57	-																																		
4. Current Contract Value (1 + 2 + 3):		15,218.73	1,277.00																																		
5. Pending Changes:		-																																			
6. Incurred Cost:		14,943.83	1,551.90																																		



Expo Phase 2 OMF Contract Status

<p>Expo Phase 2 Contractor: Kiewitt Building Group O&M Facility</p>	<p>Contract No.: XP8902-016 Status as of: 30-Nov-15</p>																									
<p>Progress/Work Completed: See Page 6</p> <p>Areas of Concern: See Pages 4 and 5</p>	<p>Major Activities (In Progress): See Page 5 and 6</p> <p>Major Activities Next Period: See Page 6</p>																									
		<p>Original Contract Dates</p>	<p>Time Extension</p>	<p>Current Contract</p>	<p>Forecast</p>	<p>Variance CDs</p>																				
<p>Substantial Completion</p>	<p>11/25/14</p>	<p>176</p>	<p>05/20/15</p>	<p>05/20/15</p>	<p>0</p>																					
<p><u>Schedule Summary:</u></p> <p>Date of Award: 05/03/13</p> <p>Limited Notice to Proceed: 06/03/13</p> <p>Original Contract Duration: 540</p> <p>Current Contract Duration: 540</p> <p>Elapsed Time from NTP: 911</p>	<p><u>Cost Summary:</u></p> <p style="text-align: right;">\$ In 000's</p> <table border="1" style="width: 100%; border-collapse: collapse;"> <thead> <tr> <th style="width: 70%;"></th> <th style="width: 15%; text-align: center;">Baseline Project</th> <th style="width: 15%; text-align: center;">Betterments/ Modifications</th> </tr> </thead> <tbody> <tr> <td>1. Award Value:</td> <td style="text-align: right;">99,930.56</td> <td></td> </tr> <tr> <td>2. Executed Modifications:</td> <td></td> <td style="text-align: right;">35.85</td> </tr> <tr> <td>3. Approved Change Orders:</td> <td style="text-align: right;">3,657.41</td> <td style="text-align: center;">-</td> </tr> <tr> <td>4. Current Contract Value (1 + 2 + 3):</td> <td style="text-align: right;">103,587.97</td> <td style="text-align: right;">35.85</td> </tr> <tr> <td>5. Pending Changes:</td> <td style="text-align: right;">236.47</td> <td style="text-align: right;">98.56</td> </tr> <tr> <td>6. Incurred Cost:</td> <td style="text-align: right;">101,154.76</td> <td style="text-align: right;">35.85</td> </tr> </tbody> </table>						Baseline Project	Betterments/ Modifications	1. Award Value:	99,930.56		2. Executed Modifications:		35.85	3. Approved Change Orders:	3,657.41	-	4. Current Contract Value (1 + 2 + 3):	103,587.97	35.85	5. Pending Changes:	236.47	98.56	6. Incurred Cost:	101,154.76	35.85
	Baseline Project	Betterments/ Modifications																								
1. Award Value:	99,930.56																									
2. Executed Modifications:		35.85																								
3. Approved Change Orders:	3,657.41	-																								
4. Current Contract Value (1 + 2 + 3):	103,587.97	35.85																								
5. Pending Changes:	236.47	98.56																								
6. Incurred Cost:	101,154.76	35.85																								



Expo Phase 2 Bikeway Contract Status

<p>Expo Phase 2 Contractor: Skanska/Rados Bikeway Project</p>	<p>Contract No.: XP8903-01 Status as of: 30-Nov-15</p>																																				
<p>Progress/Work Completed: See Page 6</p> <p>Areas of Concern: See Pages 4 and 5</p>	<p>Major Activities (In Progress): See Page 5 and 6</p> <p>Major Activities Next Period: See Page 6</p>																																				
		<p>Original Contract Dates</p>	<p>Time Extension</p>	<p>Current Contract</p>	<p>Forecast</p>	<p>Variance CDs</p>																															
	<p>Substantial Completion</p>	<p>07/10/15</p>	<p>0</p>	<p>07/10/15</p>	<p>07/10/15</p>	<p>0</p>																															
<p><u>Schedule Summary:</u></p> <p>Date of Award: 01/27/12</p> <p>Limited Notice to Proceed: 08/28/13</p> <p>Original Contract Duration: 681</p> <p>Current Contract Duration: 681</p> <p>Elapsed Time from NTP: 825</p>	<p><u>Cost Summary:</u></p> <table border="1" data-bbox="1187 1398 1520 1801"> <thead> <tr> <th colspan="2"></th> <th colspan="2" style="text-align: center;">\$ In 000's</th> </tr> <tr> <th colspan="2"></th> <th style="text-align: center;">Baseline Project</th> <th style="text-align: center;">Betterments/ Modifications</th> </tr> </thead> <tbody> <tr> <td>1. Award Value:</td> <td></td> <td style="text-align: right;">11,041.06</td> <td></td> </tr> <tr> <td>2. Executed Modifications:</td> <td></td> <td style="text-align: right;">1,469.80</td> <td></td> </tr> <tr> <td>3. Approved Change Orders:</td> <td></td> <td style="text-align: right;">424.90</td> <td style="text-align: center;">-</td> </tr> <tr> <td>4. Current Contract Value (1 + 2 + 3):</td> <td></td> <td style="text-align: right;">12,935.76</td> <td style="text-align: center;">-</td> </tr> <tr> <td>5. Pending Changes:</td> <td></td> <td style="text-align: center;">-</td> <td></td> </tr> <tr> <td>6. Incurred Cost:</td> <td></td> <td style="text-align: right;">11,655.20</td> <td style="text-align: center;">-</td> </tr> </tbody> </table>							\$ In 000's				Baseline Project	Betterments/ Modifications	1. Award Value:		11,041.06		2. Executed Modifications:		1,469.80		3. Approved Change Orders:		424.90	-	4. Current Contract Value (1 + 2 + 3):		12,935.76	-	5. Pending Changes:		-		6. Incurred Cost:		11,655.20	-
		\$ In 000's																																			
		Baseline Project	Betterments/ Modifications																																		
1. Award Value:		11,041.06																																			
2. Executed Modifications:		1,469.80																																			
3. Approved Change Orders:		424.90	-																																		
4. Current Contract Value (1 + 2 + 3):		12,935.76	-																																		
5. Pending Changes:		-																																			
6. Incurred Cost:		11,655.20	-																																		
