

# We will get going in just a moment



# Thank you for joining us!



This conversation will be recorded and shared afterwards online and via email



You can submit your questions using the Q&A feature.

# Next stop: more subway.

**PURPLE (D LINE) EXTENSION TRANSIT PROJECT**  
Section 1



**Fairfax Street Decking Removal**  
Wilshire Blvd. Full Closures



July 26, 2022

# Wilshire/Fairfax Station Rendering




# Fairfax Decking Removal - Sequence

**Phase 3 - Fairfax Ave. to San Diego Way**  
Weekends 10 - 13

**Phase 1 - Fairfax Ave. to Ogden Dr.**  
Weekends 1 - 7


**Phase 2 - Fairfax Intersection**  
Weekends 8 & 9

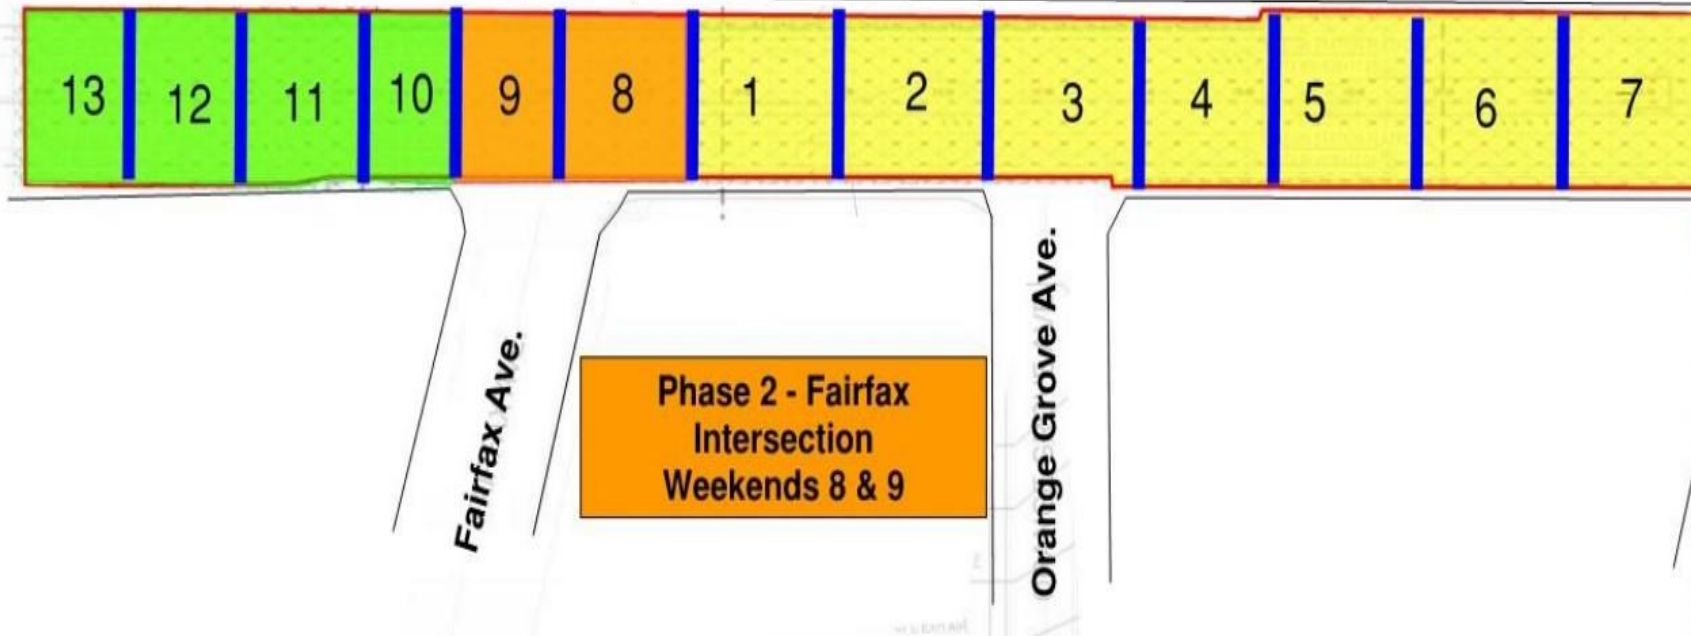

Weekend	Dates
1	September 9 – September 12
2	September 16 – September 19
3	September 23 – September 26
4	September 30 – October 3
5	October 7 – October 10
6	October 14 – October 17
7	October 21 – October 24
8	October 28 – October 31
9	November 4 – November 7
Veteran's Day (No work)	November 11 – November 14
10	November 18 – November 21
Thanksgiving (No work)	November 25 – November 28
11	December 2 – December 5
12	December 9 – December 12
13	December 16 – December 19


# Fairfax Decking Removal – Phase 1

- Work will begin at 9pm on Friday night and continue through 6am on Monday morning. As a contingency, the design-builder has requested approval to extend work hours as late as 12 noon on Monday. The extension will only be used in the event of an emergency.
- Decking Removal will begin at the Wilshire/Fairfax Station over the weekend of September 9 to September 12.
- Phase 1, the area immediately east of Fairfax Av, will be the first section restored.
- A full closure on Wilshire BI will be in place over the duration of this work. Eastbound traffic will be detoured at Fairfax Av, and westbound traffic will be detoured at La Brea Av

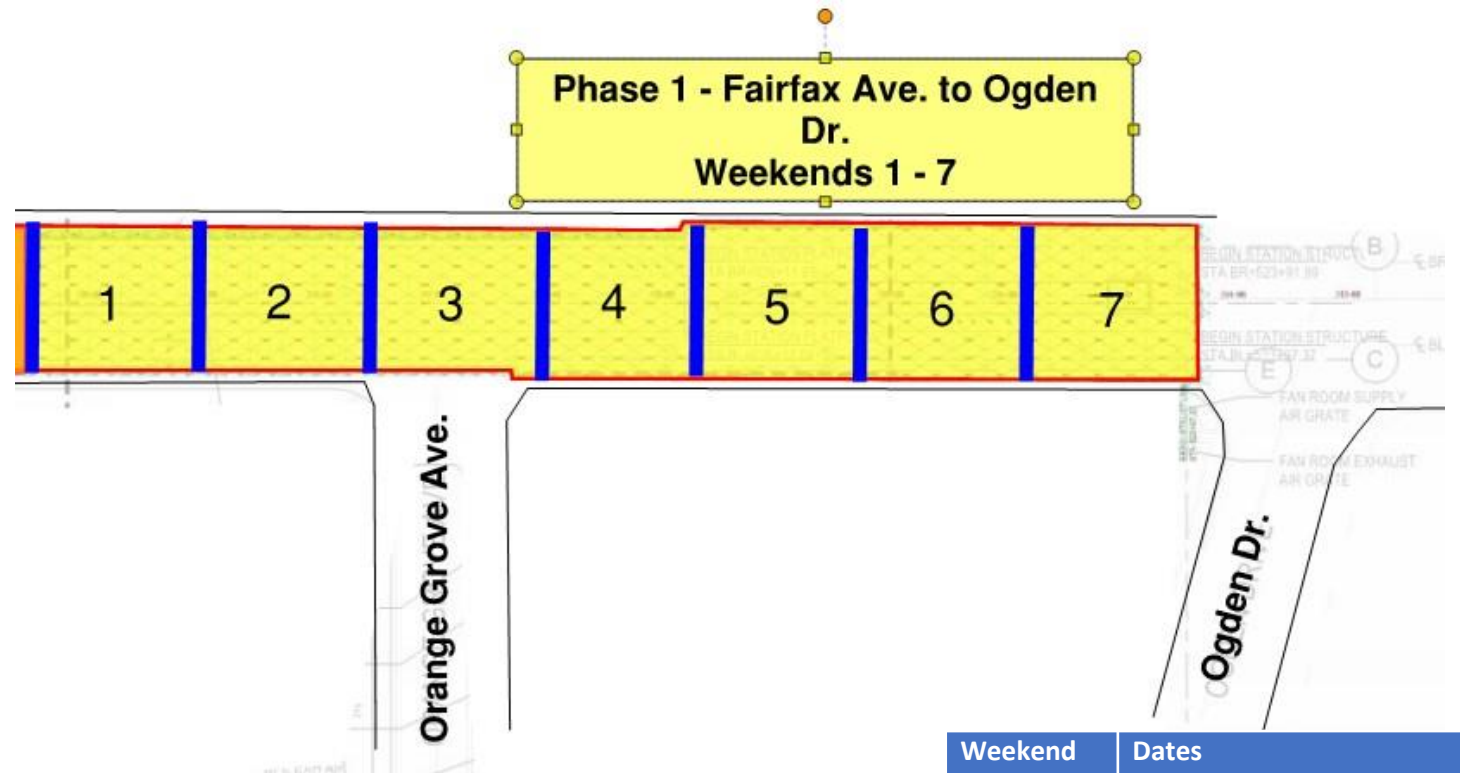

Weekend	Dates
1	September 9 – September 12
2	September 16 – September 19
3	September 23 – September 26
4	September 30 – October 3
5	October 7 – October 10
6	October 14 – October 17
7	October 21 – October 24


# Fairfax Decking Removal – Phase 1 Detour Map

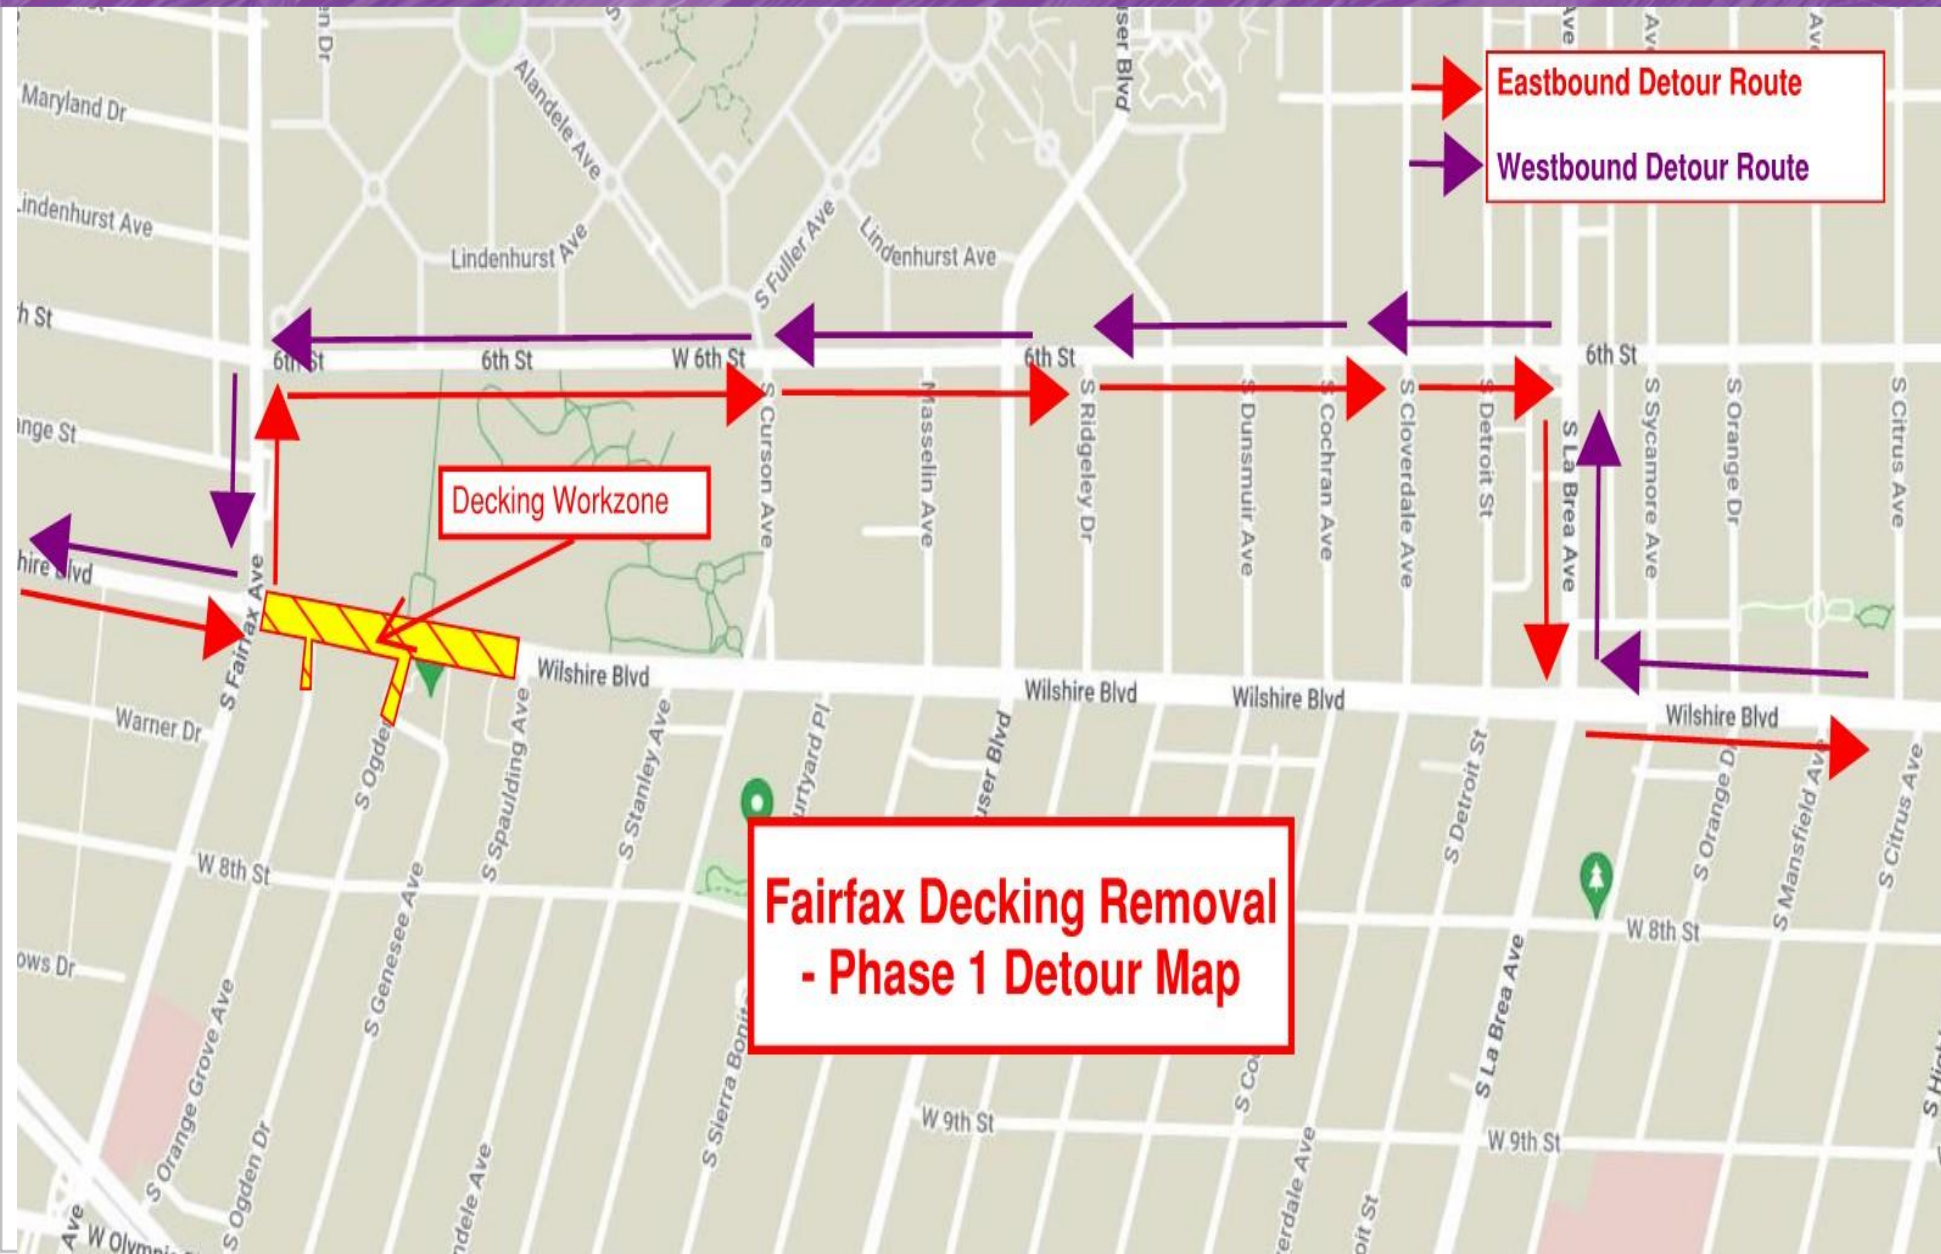


- Eastbound Wilshire > Northbound Fairfax Av > Eastbound 6<sup>th</sup> St > Southbound La Brea Av > Eastbound Wilshire
- Westbound Wilshire > Westbound 6<sup>th</sup> St > Southbound Fairfax Av > Westbound Wilshire

# Fairfax Decking Removal – Phase 2

- Work will begin at 9pm on Friday night and continue through 6am on Monday morning. As a contingency, the Design-Builder has requested approval to extend work hours as late as 12 noon on Monday. The extension will only be used in the event of an emergency.
- Following Phase 1 Decking Removal, STS will begin working within the Wilshire/Fairfax Intersection.
- This work will take two weekends to complete, October 28 – October 31, and November 4 to November 7
- Full closures will be in place on Wilshire Bl and Fairfax Av. All traffic will be detoured around the workzone.
- Southbound Fairfax Av traffic will be detoured at 6<sup>th</sup> St
- Northbound Fairfax Av traffic will be detoured at Olympic Bl
- Eastbound Wilshire Bl traffic will be detoured at La Cienega Bl and San Vicente Bl
- Westbound Wilshire Bl traffic will be detoured at La Brea Av

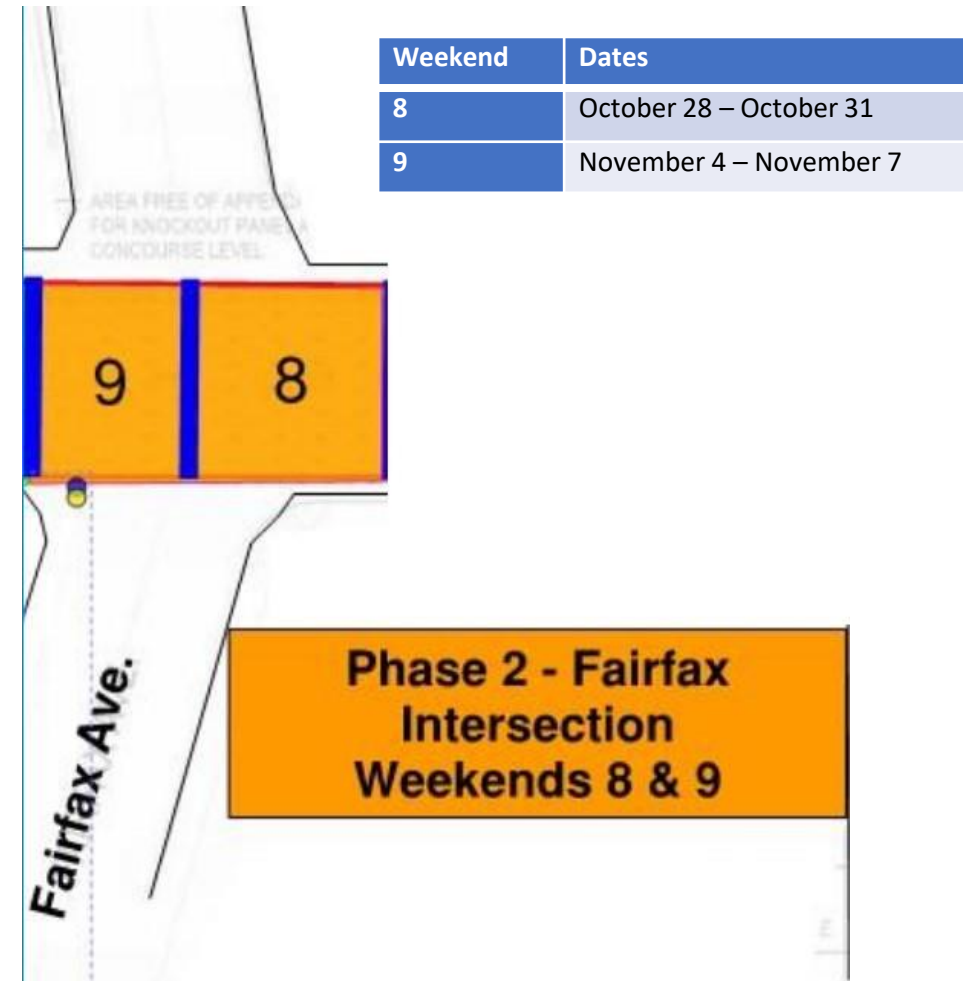

# Fairfax Decking Removal – Phase 2 Detour Map

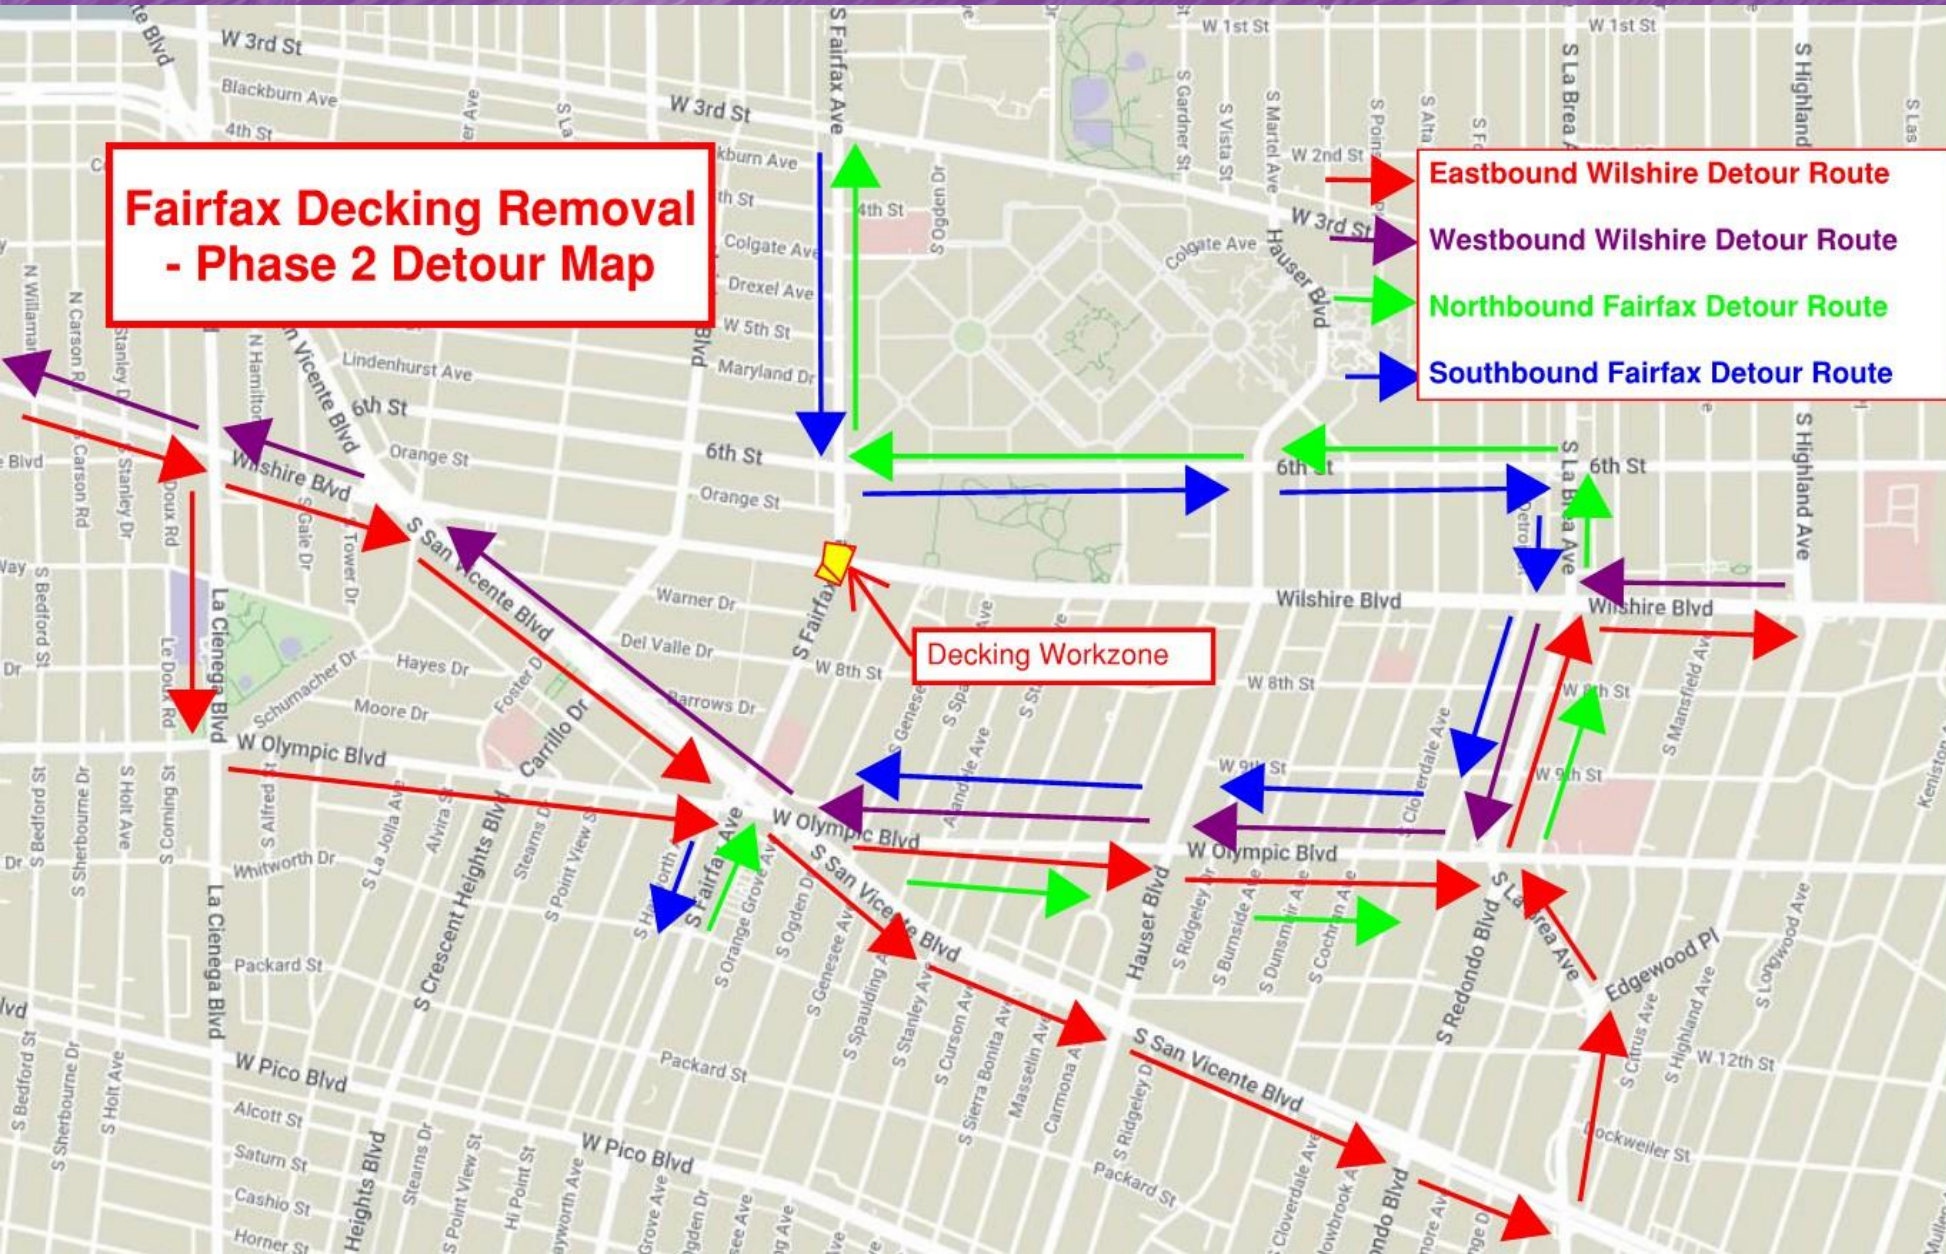

**Fairfax Decking Removal  
- Phase 2 Detour Map**

- Eastbound Wilshire Detour Route
- Westbound Wilshire Detour Route
- Northbound Fairfax Detour Route
- Southbound Fairfax Detour Route

**Decking Workzone**

- Eastbound Wilshire > Southbound La Cienega Bl > Westbound Olympic Bl > Northbound La Brea Av > Eastbound Wilshire
- Eastbound Wilshire > Southbound San Vicente Bl > Northbound La Brea Av > Eastbound Wilshire
- Westbound Wilshire > Southbound La Brea Av > Westbound Olympic Bl > Northbound San Vicente Bl > Westbound Wilshire
- Northbound Fairfax Av > Eastbound Olympic Bl > Northbound La Brea Av > Westbound 6<sup>th</sup> St > Northbound Fairfax Av
- Southbound Fairfax Av > Eastbound 6<sup>th</sup> St > Southbound La Brea Av > Westbound Olympic Bl > Southbound Fairfax Av


# Fairfax Decking Removal – Phase 3

- Work will begin at 9pm on Friday night and continue through 6am on Monday morning. As a contingency, the Design-Builder has requested approval to extend work hours as late as 12 noon on Monday. The extension will only be used in the event of an emergency.
- Following Phase 2 Removal, the third and final phase of work will begin to the west of Fairfax Av
- This work will take place over 4 weekends, beginning on November 18.
- Full closures will be in place at Fairfax Av and San Diego Way
- Eastbound Wilshire will be detoured at La Cienega Bl or San Vicente Bl
- Westbound Wilshire will be detoured at Fairfax Av




Weekend	Dates
Veteran's Day (No work)	November 11 – November 14
10	November 18 – November 21
Thanksgiving (No work)	November 25 – November 28
11	December 2 – December 5
12	December 9 – December 12
13	December 16 – December 19

# Fairfax Decking Removal – Phase 3 Detour Map

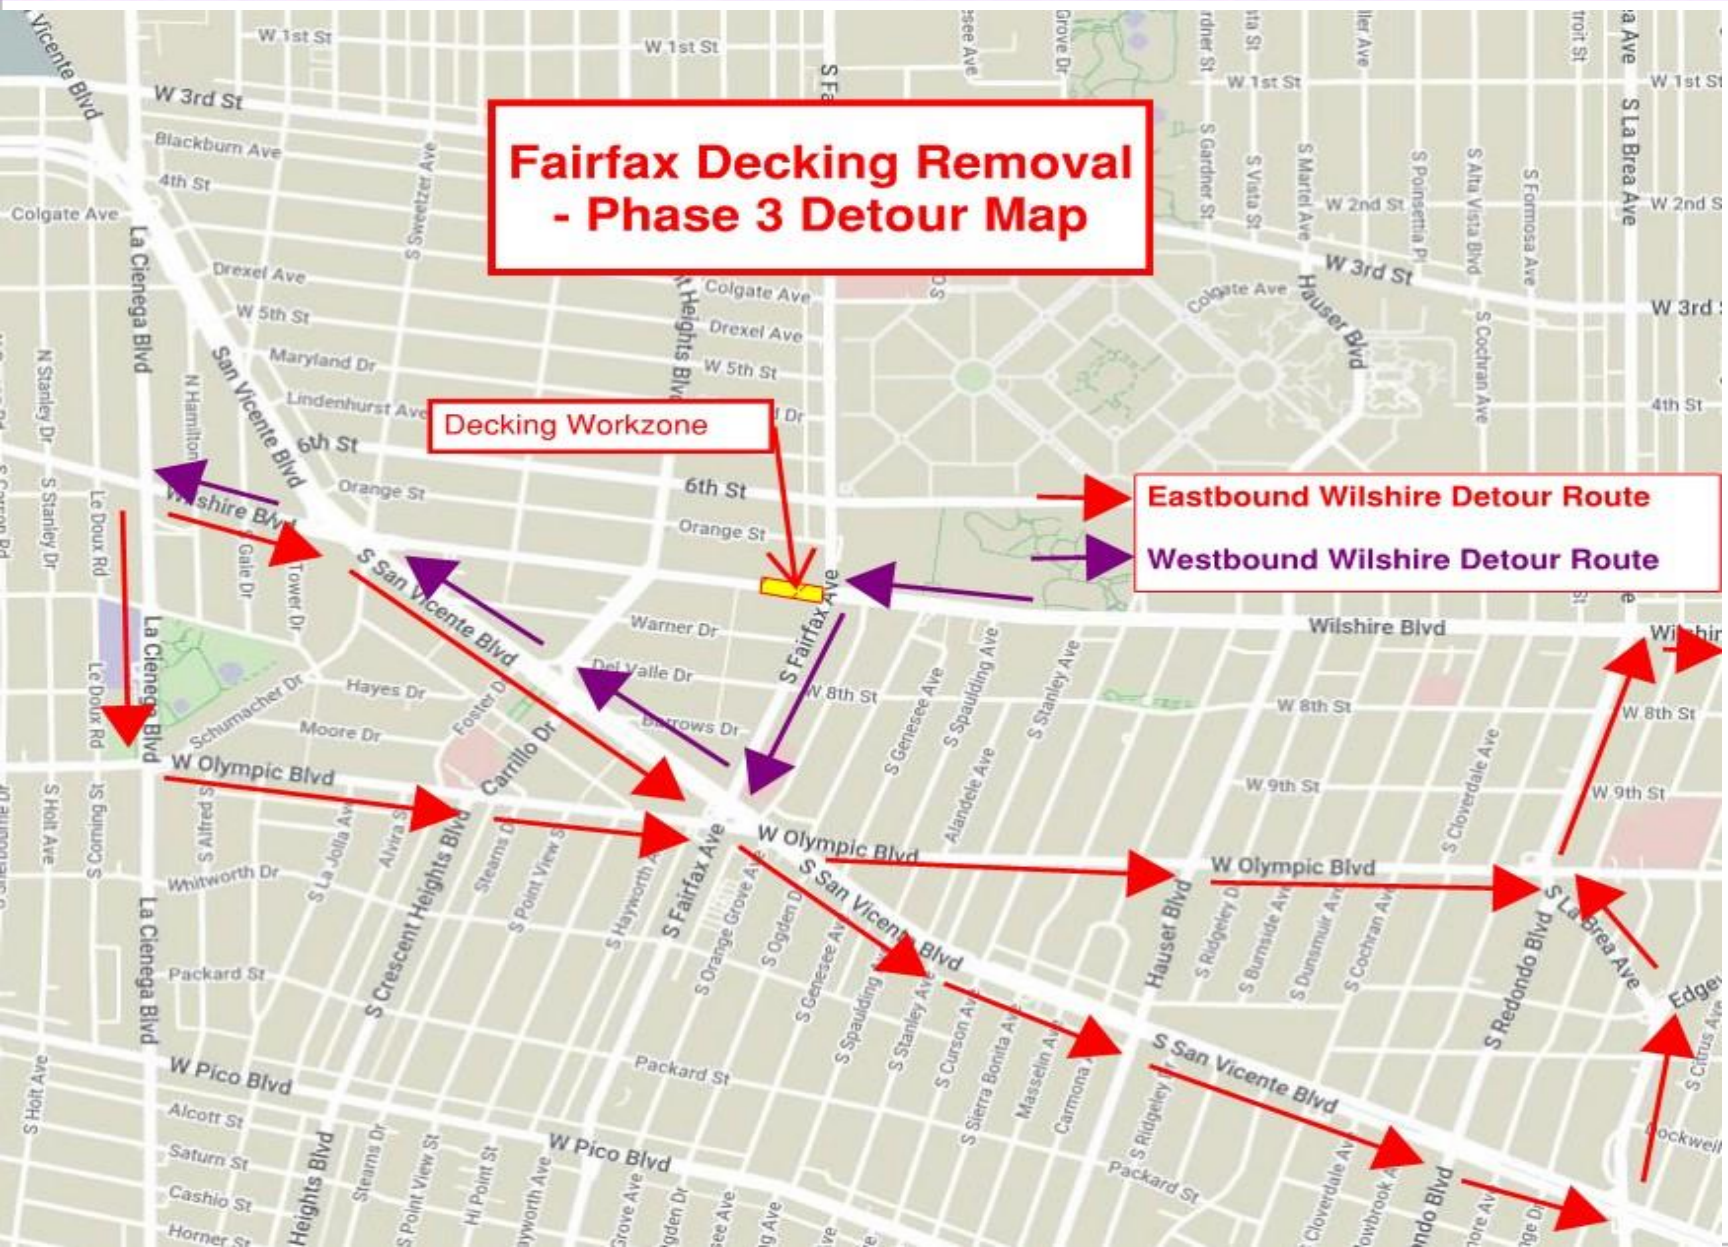

- Eastbound Wilshire > Southbound La Cienega Bl > Eastbound Olympic Bl > Northbound La Brea Av > Eastbound Wilshire
- Eastbound Wilshire > Southbound San Vicente Bl > Northbound La Brea Av > Eastbound Wilshire
- Westbound Wilshire > Southbound Fairfax Av > Northbound San Vicente Bl > Westbound Wilshire

# Fairfax Station – Decking Removal

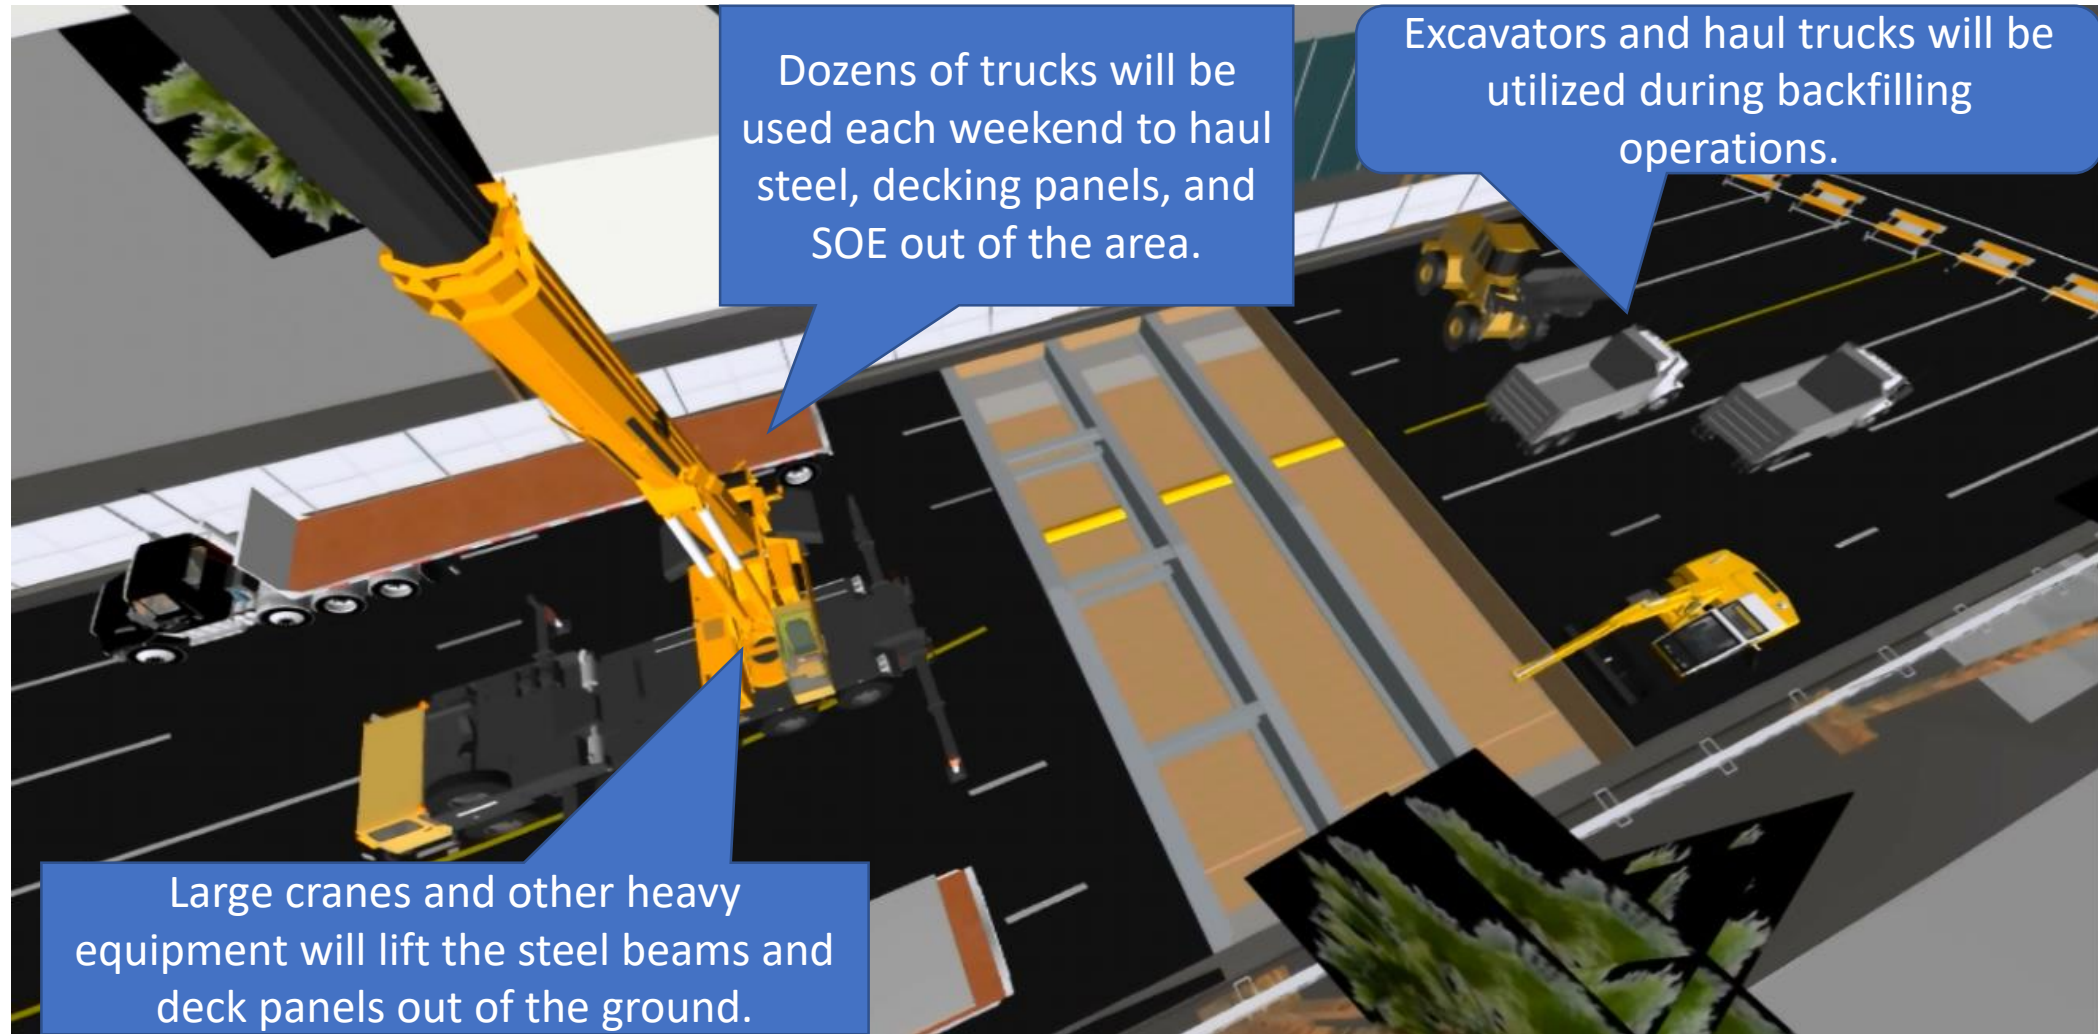


Dozens of trucks will be used each weekend to haul steel, decking panels, and SOE out of the area.


Excavators and haul trucks will be utilized during backfilling operations.

Large cranes and other heavy equipment will lift the steel beams and deck panels out of the ground.

# Fairfax Station – Decking Removal

A 3D architectural rendering of a street construction site. The scene shows a road with a white center line and a yellow curb. A large area of the road is highlighted with a green grid pattern, indicating the area of decking removal. In the background, there are trees and a building. A blue speech bubble is overlaid on the image, pointing to the green grid area.

Following decking removal, steel beams and SOE haul out, and backfilling and utility placement, a new street surface will be placed from curb to curb.

A blue speech bubble pointing to the green grid area on the road.

Work will progress east to west, from one weekend to the next.

# La Brea Station – Decking Removal Equipment

## Aboveground

- Cranes
- Haul trucks, dump trucks
- Concrete pump
- Loaders
- Saw cutter, jackhammer
- Vibrator, roller

## Belowground

- Compact excavators
- Compact bulldozers
- Man lifts, forklifts
- Graders
- Loaders



# Fairfax Station – Decking Removal Schedule

\* Subject to Change

	Friday				Saturday																									
Activities	9pm	10pm	11pm	Midnight	1am	2am	3am	4am	5am	6am	7am	8am	9am	10am	11am	Noon	1pm	2pm	3pm	4pm	5pm	6pm	7pm	8pm	9pm	10pm	11pm	Midnight		
Implement Traffic Control																														
Stage Equipment																														
Deck Panel Removal																														
Deck Beam and Strut Removal																														
Deck Panel Haul Out																														
Deck Beam and Strut Haul Out																														
	Sunday																				Monday									
Activities	1am	2am	3am	4am	5am	6am	7am	8am	9am	10am	11am	Noon	1pm	2pm	3pm	4pm	5pm	6pm	7pm	8pm	9pm	10pm	11pm	Midnight	1am	2am	3am	4am	5am	6am
Haul In																														
Utility Placement																														
Backfilling and Testing																														
Asphalt Placement																														
Asphalt Curing																														
Striping																														
Removal of Traffic Control Materials																														
Open Wilshire																														

Decking removal will begin at 9pm on Friday and continue until Monday at 6am during 10 weekends between September 9, 2022 through December 19, 2022.



# Fairfax Station – Decking Removal Sequence (Part 1)

Activity	Occurs
Design-builder begins to remove deck panels along Wilshire Blvd.	Once road is closed to traffic (9pm)
Crews begin removing steel beams and support for excavation above the station	All day Saturday
Utilities will be relocated as needed. Trucks loaded with backfilling materials will be staged around the deck openings.	Saturday
Testing and quality assurance conclude prior to asphalt placement	All day Sunday

# Fairfax Station – Decking Removal Sequence (Part 2)

Activity	Occurs
Asphalt placement	Begins after backfilling (asphalt requires approximately four hours to cure/cool before it can carry weight)
City agencies test asphalt to ensure that it will be safe for commuters	After curing
The final steps of decking removal includes striping, removing traffic control devices, and opening the road	Sunday night and Monday morning

# Outreach Schedule

Outreach	Occurs
STS and Metro discusses closures with Council District 5.	May 2022
Affected residents and business owners invited to online meetings to discuss decking removal. Meeting announcement appears on Weekly Look Ahead.	One month before work begins
Wilshire/Fairfax decking removal presented during quarterly webinar.	One month before work begins
Door-to-door outreach conducted. A Construction Notice will be widely distributed adjacent to the Wilshire/La Brea intersection.	One month before work begins
A Construction Notice will be re-issued on the Metro website and distributed to the Metro Email List. Computer message signs will be placed at the work area.	One week before work begins
A Construction Notice describing the work will be sent in the Weekly Look Ahead email.	Weekly

## Next Decking Removal Community Meeting

August 2, 2022 at 6:00PM Via Zoom <https://zoom.us/j/96626476708>

Webinar ID: 966 2647 6708

### Call us on the Project Hotline: 213-922-6934

- For project questions, concerns and complaints
- Live during construction work hours
- Monday through Friday, 7am to 5pm
- After 5pm: Leave a voicemail; staff with return call within 24 hours
- Callers can speak with a person via the Hotline after 5pm by pressing 1

### Project Email: [purplelineext@metro.net](mailto:purplelineext@metro.net)

- Receive email project updates and construction notices
- Responses within 24 hours
