



I-405 Sepulveda Pass Improvements Project

30-Day Look Ahead Summary—August 2011

■ Wilshire Segment

DWP and SCE Utility Relocation

- Sepulveda reduced to one lane in each direction, Constitution to Ohio, 9pm to 6am
- Westbound Wilshire reduced to one or two lanes, 9pm to 6am
- Northbound on and off-ramps from Wilshire closed, 9pm to 6am
- Southbound Sepulveda reduced to one lane, Constitution to Ohio, 9am to 3pm

Girder Installations

- Full closure of Santa Monica, August 3-5, 9pm to 6am
- Santa Monica on- and off-ramps closed, August 3-5, 9pm to 6am
- Full closure of Olympic, late August, 9pm to 6am

Freeway Widening, Drainage, Road Work

- Eastbound I-10 to northbound I-405 connector closed, 9pm to 6am
- Westbound I-10 to northbound I-405 connector closed, 11pm to 5am
- Eastbound I-10 to southbound I-405 connector closed, 10pm to 6am

■ Sunset Segment

Sewer Line Relocation

- Sepulveda Bl reduced to 1 lane SB and 2 lanes NB, Constitution to Montana, 24-7

Montana Bridge Widening and Utility Relocation

- Sepulveda reduced to one lane in each direction near Montana, 9pm to 6am
- Montana Av reduced to one lane in each direction or two way traffic maintain with a flagger, 9pm to 6am
- Intermittent closures of the Montana off ramp, 7pm to 6am
- Full closure of Montana Av for one night only on August 9 (tentative), 9pm to 6am
- Open Church Ln at Sunset be for one night only on August 9 (tentative), 9pm to 6am



I-405 Sepulveda Pass Improvements Project

Wall Construction and Utility Relocation from Montana Av to Getty Ramps

- Sepulveda reduced to one lane in each direction, 9am to 4pm and 9pm to 6am

Sunset Bridge Reconstruction and Utility Relocation

- Sunset bridge reduced to one lane in each direction, 10pm to 6am
- Intermittent full closures of Sunset bridge, 10pm to 6am
- SB on-ramp EB Sunset closed, 7pm to 6am
- NB ramps closed nightly, 7pm to 6am
- Full closure of Sepulveda Way near Sunset, 9am to 4pm and 9pm to 6am
- Sepulveda Way closed for WB Sunset access, 9pm to 6am
- Church Ln reduced to one lane in each direction, Sepulveda to Sunset, 9pm to 6am
- Full direction closure of NB 405 on August 22, 12am to 5am
- Full direction closure of SB 405 on August 24, 12am to 5am
- Full closure of Sepulveda on August 22, 9pm to 6am

■ Mulholland Segment

Mulholland Bridge Reconstruction

- Several freeway lane closures, 10 pm to 6 am
- Mulholland Bridge closures for three nights, 10 pm to 6 am

Skirball Bridge Reconstruction

- Directional freeway closures in each direction, in one night, mid-August, midnight to 5 am
- Skirball Bridge closure in mid-August, 10 pm to 6 am
- Skirball Bridge reduced to one lane for two-way traffic, 9 pm to 6 am
- Frequent nighttime closure of Skirball ramps
- Occasional daytime closures of Skirball off-ramps

Sepulveda Bl. near Mountaingate and Skirball Bridge

- Sepulveda reduced to one lane in each direction, every night
- Sepulveda reduced to one lane in each direction, during the day on weekends



I-405 Sepulveda Pass Improvements Project

Community Relations Hotline: 213-922-3665; E-mail: I-405@metro.net; Website: Metro.net/405
Twitter: http://twitter.com/I_405



Thirty-Day Construction Look Ahead Details



July 28, 2011




Wilshire Segment

Location	Activity	Closures/Notes	Work Hours	Projected Date
Wilshire Bl loops	Build MSE wall		D/N	Ongoing
	Pouring and forming abutments		Night	Ongoing
	Replacing on-ramp	NB on-ramp from WB Wilshire first full closure for 90 days	Extended Closure	October
Wilshire UC	Retrofit of superstructure	Temp lane closures on Wilshire		Ongoing
	Abutment pour	Temp lane closures on Wilshire	D/N	Ongoing



Wilshire Segment

Location	Activity	Closures/Notes	Work Hours	Projected Date
Walls 1686, north of Constitution, east of I-405	Build MSE retaining/sound wall	Lane reductions on SB Sepulveda Bl, NB I-405	D/N	Ongoing



Wilshire Segment

Bridge	Activity	Closures/Notes	Work Hours	Projected Date
Santa Monica	Form abutment stems	Temp night closures of ramps, I-405	D/N	Ongoing
	Set NB girders	Full closure of Santa Monica Bl	N	Aug 3-5
Ohio	Abutment forming	Temp closures of Ohio Av, Beloit Av and Cotner Av	D/N	July
	Set NB girders	Full closure of Ohio Av	Night	September
Olympic	Set girders	Full closure of Olympic Bl	Night	August
Constitution	Form abutments	Sidewalk closures at Constitution	D/N	Ongoing




Wilshire Segment

Location	Activity	Closures/Notes	Work Hours	Projected Date
Wall construction on Beloit/Cotner, from Ohio to Santa Monica	Build MSE/CIP walls	Temp night ramp closures, I-405	D/N	Ongoing
Wall construction, Ohio to NB off-ramp to EB Wilshire	Erect, set and backfill MSE panels	Lane reduction on NB I-405	D/N	Ongoing



Wilshire Segment

Location	Activity	Closures/Notes	Work Hours	Projected Date
Beloit Av, Santa Monica to Olympic Bl	Forming and pouring sound wall	Temp lane closures on SB I-405		August
	Drill and set CIDH panels	Temp lane closures on SB I-405	D/N	October

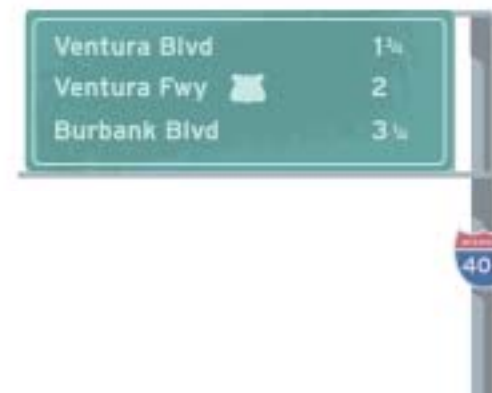

Wilshire Segment

Location	Activity	Closures/Notes	Work Hours	Projected Date
Sepulveda Bl, at Wilshire	DWP and SCE undergrounding of utilities	WB and EB Wilshire lane closures	Night	Ongoing
Pico and Exposition at Sawtelle	Retrofitting superstructure	Future closures on Exposition	D/N	Ongoing
NB on- and off-ramp to EB Wilshire	Form abutments, drill piles	Temporary lane closures NB I-405, on- and off-ramps to EB Wilshire	Night	Ongoing



Wilshire Segment

Location	Activity	Closures/Notes	Work Hours	Projected Date
NB I-405 to EB I-10 connector ramp	Drainage line installation	NB I-405 to EB I-10 connector closure	Night	Ongoing
Wall north of Wilshire, west of I-405	Setting panels for retaining wall	Temp closures on NB I-405 and SB Sepulveda	D/N	Ongoing



Sunset Segment

Location	Activity	Closures/Notes	Work Hours	Projected Date
Sepulveda/ Constitution - Montana	Sewer line relocation	One lane SB and two lanes NB with one lane in each direction for 20 days	D/N	Ongoing
Montana Bridge widening	Deck installation	Full closures of Montana, ramp closures, lane reduction on Sepulveda, as needed. Access via Church Ln	D/N	Ongoing/deck pour one night only 8/9/11
	Storm drain relocation	Full closures of Montana, ramp closures, lane reduction on Sepulveda, as needed	Night	Ongoing

Sunset Segment

Location	Activity	Closures/Notes	Work Hours	Projected Date
Sepulveda/ Montana - Sunset	Utility relocation: AT &T, Verizon, sewer, storm drains, Exxon- Mobil	Maintain one lane in each direction of traffic	D/N	Ongoing
	Chevron line jack and bore	Lane reduction at Montana/Sepulveda and Moraga/Sepulveda to one lane in each direction	D/N	TBD
Walls 1720/1730	Retaining wall (permanent tie backs)/ lateral and sound wall	Maintain one lane in each direction of traffic	Day	Ongoing
	Storm drain, sewer	Most work on hillside	D/N	Ongoing

Sunset Segment

Location	Activity	Closures/Notes	Work Hours	Projected Date
Sunset Bridge re-construction	Deck installation	Fwy lane reductions, ramp closures, fwy directional closures	D/N freeway closures	Ongoing/ deck pour in August
	LADWP power and water vault work, intersection civil improvements	Church Ln full closure from Sunset to Kiel; extended closure Sunset /Church Ln & Sunset /Sepulveda Wy, EB Sunset to SB I-405	D/N Church Ln closure 24 hrs – 7 days a week	Ongoing/ramp and intersection closures in September
NB Sunset Ramps	On-ramp: footing and abutment construction, Wall 1738C	Ramp closures	D/N	Ongoing
	Off-ramp: utility protection, MSE Wall 1738A and SP Wall 1738B construction	Ramp closures	D/N	Ongoing

Sunset Segment

Location	Activity	Closures/Notes	Work Hours	Projected Date
Sepulveda/ Sunset – Church Ln	Wall 1746 construction	Maintain one lane in each direction	D/N	Ongoing
	Utility relocation: Time Warner, Exxon Mobil	Maintain one lane in each direction	D/N	Ongoing/Exxon Mobil completed
Sepulveda Wy/ Sepulveda-Sunset	Gas line and power line relocation	Full closure of Sepulveda Wy, one lane in each direction on Sunset and Sepulveda	D/N	Ongoing
N. Church Ln/ Sepulveda - Sunset	Utility relocation: LADWP - power vault, Chevron	Maintain one lane in each direction; ramp closures	Night	Ongoing
Sepulveda/ Moraga – Getty	MSE Wall 1756, 1766 and 1782: tree removal, clear & grub, sound wall removal	Maintain one lane in each direction; freeway lane reduction, ramp closures	D/N	Ongoing

Sunset Segment

Location	Activity	Closures/Notes	Work Hours	Projected Date
Getty Bridge widening	Demolition and foundation prep-work	Maintain access during hours of operation	D/N	Summer
Sepulveda/ Getty Ramps	LADWP relocation, vault and duct bank	Maintain one lane in each direction; close NB I-405 off-ramp, SB I-405 on-and-off ramps	D/N	Ongoing
SB Getty on-ramp	Construct soil-nail wall 1827 until December	Daily extended lane closures; ramp open 6am-10am, otherwise closed	D/N	Ongoing

Mulholland Segment

Area	Activity	Closures/Notes	Work Hours	Projected Date
Getty Trail Head	Retaining wall construction	Continued construction of one of the retaining walls along the northbound freeway as part of the new NB Getty on-ramp construction	D/N	Ongoing until late 2011
Bel Air Crest	Retaining walls construction	Construction of retaining walls along the northbound I-405 on both sides of the Bel Air Crest undercrossing	D/N	Ongoing
	Bridge/overpass widening	Widening of the freeway overpass above Bel Air Crest Road to accommodate the widening of the I-405 freeway to the east	D/N	Early August



Mulholland Segment

Area	Activity	Closures/Notes	Work Hours	Projected Start Date
Sherman Oaks (east of I-405)	Retaining wall construction	Construction of two retaining walls on east side of freeway in Sherman Oaks to support widening of freeway to the east	D/N	Ongoing
Sherman Oaks (west of I-405)	Area grading and clearing and grubbing	The schedule for the resumption of work to be determined	D/N	TBD
	Retaining wall construction	Nighttime work may entail the closure of two right-hand lanes on the SB I-405, SB Skirball ramps, and the SB Valley Vista on-ramp	D/N	TBD

Mulholland Segment

Area	Activity	Closures/Notes	Work Hours	Projected Date
Valley Vista	Gas line relocation	Relocation of gas lines along Sepulveda Bl to support the eventual widening of Sepulveda Bl underpass in Sherman Oaks	Day	Completed
	Utility relocations	Relocation of utilities to support sound wall construction	Day	TBD
	House demolition	The work zone will be set-up behind temporary fencing	Day	TBD
	Clear and grub	Access to the work zone area will require access from the street and freeway	D/N	TBD
	Sound wall construction	Reconstruction of sound wall to support freeway widening.	D/N	TBD

Mulholland Segment

Area	Activity	Closures/Notes	Work Hours	Projected Date
Skirball Bridge	Bridge reconstruction	North side of the bridge and retaining walls near bridge are undergoing reconstruction. Frequent night time and occasional daytime closures of Skirball ramps.	D/N	On-going until late 2011
	Relocated SB Skirball on-ramp construction	Construction of retaining walls and relocated southbound on-ramp approximately 2,000 feet south of Skirball Bridge	D/N	Ongoing
	Skirball Bridge utility relocation	Several utilities in the Skirball Bridge will be relocated. Initial work requires lane closures on the bridge.	Night	Early August
	Sepulveda Bl utility relocation	Relocation of utilities along Sepulveda Bl between Mountaingate Dr and just north of the Skirball Bridge. Approximately 11-month duration, nighttime work occurring daily and daytime work on weekends.	D/N	Ongoing

Mulholland Segment

Area	Activity	Closures/Notes	Work Hours	Projected Date
Mulholland Bridge	Bridge demolition	Demolition of south half complete		Completed
	Bridge abutment demolition	Bridge abutments to be demolished soon. Anticipated to only require several freeway lanes closures.	Night	August
	Bridge reconstruction	Reconstruction of south half of the bridge will last approximately 11 months.	D/N	July
