


I-405 Sepulveda Pass Improvements Project

QUARTERLY PROJECT STATUS REPORT

JUNE 2015

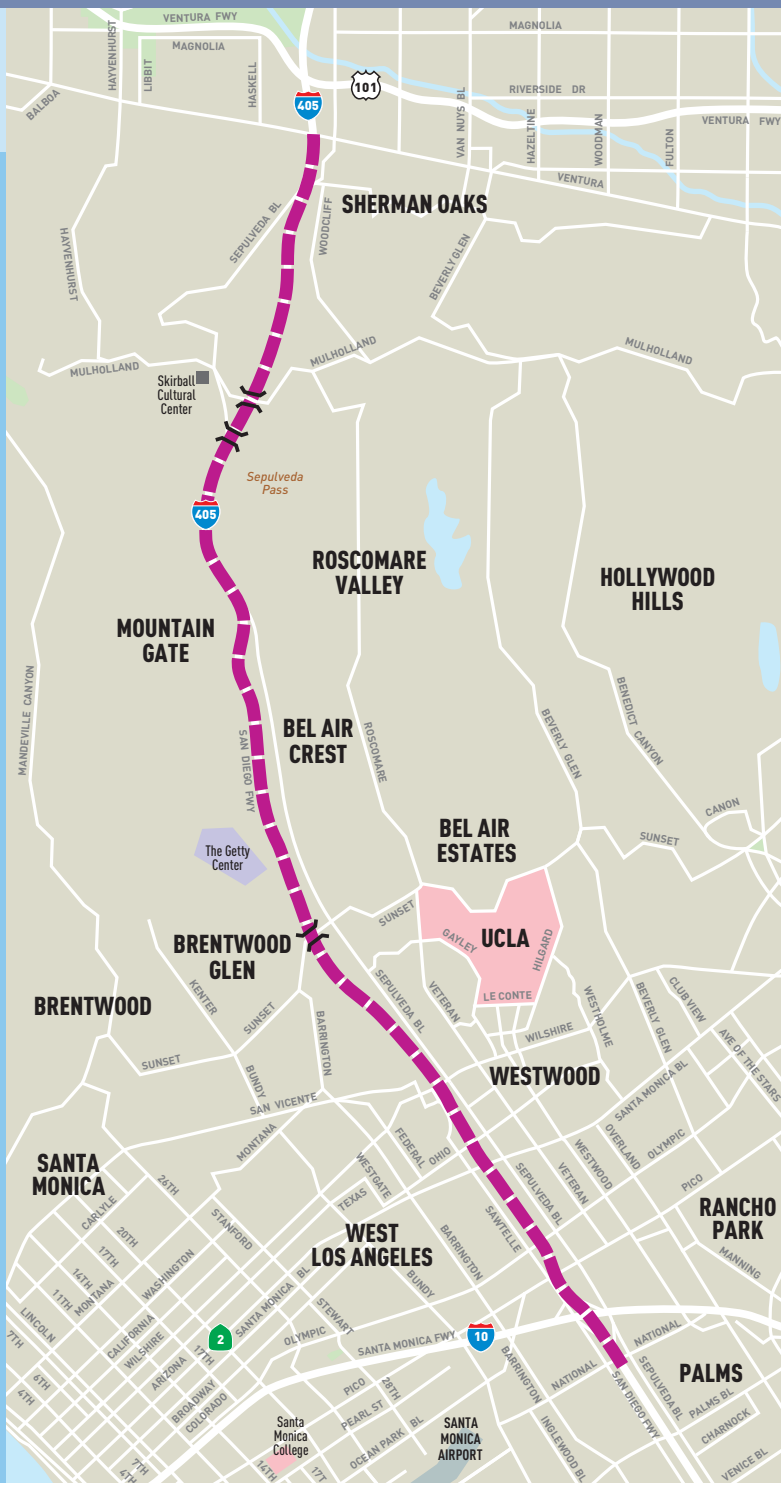

Metro®

Caltrans

11-0062PJ ©2010 LACMTA ©2010 LACMTA

INTERSTATE 405 SEPULVEDA PASS IMPROVEMENTS PROJECT

QUARTERLY PROJECT STATUS REPORT

THE PREPARATION OF THIS DOCUMENT HAS BEEN FINANCED IN PART THROUGH GRANTS FROM THE FEDERAL HIGHWAY ADMINISTRATION (FHWA) AND THE AMERICAN RECOVERY AND REINVESTMENT ACT (ARRA) AND FUNDS FROM THE STATE OF CALIFORNIA.

JUNE 2015

TABLE OF CONTENTS

Page No.

Project Summary…….. 1
Project Overview & Status……..…… 2-4
Management Issues……... 5-6

Project Status

- Project Scope……..…… 7-8
- Schedule
  - Key Milestones Six-Month Lookahead...……..…… 9
  - Project Summary Schedule …….. 10
  - Critical Path Narrative…….. 11
- Project Cost Status……... 12-13
- Financial/Grant Status…….. 14-15
- Staffing…… 16-18
- Real Estate…… 19
- Safety and Security Status…… 20

Contract C0882 Status…..…… 21
Chronology of Events…….. 22-38
Appendices……... 39-42

PROJECT SUMMARY

I-405 SEPULVEDA PASS IMPROVEMENTS PROJECT **As of June 2015**

LOCATION: I-405 Sepulveda Pass Improvements Project

DESIGN/CONSULTANT: Kiewit (D/B)

CONSTRUCTION MANAGEMENT CONSULTANT: Stantec

CONTRACTOR: Kiewit (D/B)

PROJECT PHOTO

Aerial View of Sunset Interchange & Walls 1730 & 1720



WORK COMPLETED PAST MONTH

- Contractor Correcting Non-Conforming work on Barriers and Walls
- Performed SWPPP related activities
- Cleaned Caltrans purchased houses along right-of-way which were used by the Contractor during construction.
- Work on NB Getty On-ramp to remove demarcation cabinet and 2 pull boxes.
- Removed and replaced LED light from mast arm on SB Santa Monica On-ramp.
- Removed demarcation foundation and poured back sidewalk at Skirball Center Drive and Mulholland Drive.
- Hand graded, watered, and compacted the slope under Bridges 7 and 8 at GSA.
- Application for Substantial Completion June 26, 2015.

EXPENDITURE STATUS

($ In Millions)

ACTIVITIES	CURRENT BUDGET	EXPENDED AMOUNT	PERCENT EXPENDED
DESIGN (Preliminary) (PA&ED/PS&E)	$47.0	$47.0	100.0%
RIGHT-OF-WAY (Capital/Support/3rd Party)	$78.4	$71.9	91.7%
CONSTRUCTION (Construction Support/Construction)	$1,013.4	$994.2	98.1%
Reversible Lane	$2.6	$1.5	57.7%
TOTAL	$1,141.4	$1,114.6	97.7%

SCHEDULE ASSESSMENT

MAJOR SCHEDULE ACTIVITIES	PRIOR PLAN	CURRENT PLAN	VARIANCE WEEKS
Environmental			
End Environmental Phase (PA&ED)	Mar-08	Mar-08	Complete
Design			
End Design Support Phase (D/B)	Sep-15	Sep-15	0
Right-of-Way			
ROW Certification	Sep-15	Sep-15	0
Construction			
Opening of SB I-405 Realignment	May-14	May-14	Complete
Substantial Completion	Sep-15	Sep-15	0

AREAS OF CONCERN

Cracks in Retaining Walls/Soil Nail Walls (Case 1 and Case 2)

ROW ACQUISITION (Caltrans)

PARCELS AQUIRED	66
PARCELS NOT AQUIRED (Salvation Army-Litigation Pending)	1
DECERTIFIED PARCELS	12
PAST DUE WITH NO APPARENT SCHEDULE IMPACT	0
ADDITIONAL IMPACTS REQUIRING APPRAISAL MAPS	0
TOTAL REQUIRED PARCELS	79

CRITICAL ACTIVITIES / 3 MONTH LOOK AHEAD

Project Wide Substantial Completion Acceptance - End of September 2015

PROJECT OVERVIEW & STATUS

The I-405 Sepulveda Pass Improvements Project will add a 10-mile HOV lane and improve supporting infrastructure such as ramps, bridges, and soundwalls on the San Diego Freeway (I-405); while widening lanes from the Santa Monica Freeway (I-10) to Ventura Freeway (U.S. 101). This project will reduce existing and forecasted traffic congestion on the I-405 and enhance traffic operations by adding freeway capacity in an area that experiences heavy congestion. In addition to these modifications, the project will improve both existing and future mobility and enhance safety throughout the corridor. Project benefits include a decrease in commuter time, reduce air pollution, and promote ridesharing. The I-405 Sepulveda Pass Improvements Project features include:

- *Add a 10-mile HOV lane on the northbound I-405 between the I-10 and US-101 freeways*
- *Remove and replace the Skirball Center, Sunset Blvd. and Mulholland Dr. Bridges*
- *Realign 20 on and off ramps*
- *Widen 20 existing overpasses and structures*
- *Construct approximately 18 miles of retaining walls and soundwalls*

Interstate 405 (I-405), also known as the San Diego Freeway, is a north/south route classified as an interstate/interregional loop freeway. It is part of the National Highway System (NHS), originating at the I-5 in Orange County in the City of Irvine and terminating at the I-5 in Los Angeles County, in the City of Los Angeles near the community of Mission Hills.

The design-build contract Notice to Proceed (NTP) was issued on June 2, 2009 with a Substantial Completion Deadline of May 31, 2013. Currently, the substantial completion is expected to occur on September 30, 2015 Kiewit submitted its Application for Substantial Completion on June 26, 2015.

Project Close out

Tree planting mitigation for City Trees

Metro and the City have reached agreement on method of payment to have the City complete "City Trees" this Fall. The number of trees to be planted adjacent to city streets in close proximity to I-405 is 331. This work is anticipated to be complete by end of year 2015.

Note: Of the total of 435 trees, 104 Native Trees were added to Caltrans numbers to be planted in Santa Monica Mountains Conservancy.

Tree Planting mitigation for Caltrans Trees

Metro and Caltrans are looking at various options to plant over 3800 trees adjacent to the I-405 project. Some, if not all, may end up being planted on the Santa Monica Mountains Conservancy. This work is anticipated to be completed by end of year 2015.

Final Landscaping related to Habitat Mitigation and Monitoring Plan (HMMP)

Three (3) locations (out of 13) are remaining to be completed pending permits from Army Corps and Water Quality Board.

PROJECT OVERVIEW & STATUS (Cont'd)

Completion of Getty's North Canyon Work

This work is complete for the project with some work to be completed by Getty or Caltrans at a later date under a separate Project.

Arbitration/Claims Process

It is the Project understanding that Metro has agreed to an Arbitration process as defined below:

1. Selection of Arbitration judge and construction lawyers
2. Exchange lists of Claims – Metro Affirmative Claims and Kiewit Claims
3. Resolve as many discrete Kiewit claims as possible, prior to Arbitration and during the first 6 months of Arbitration
4. Phase I Arbitration hearing on discrete Kiewit/Metro claims (12 months)
5. Phase II Arbitration hearing " Delay and Disruption" (12 months following Phase I)

Claims

The following are the general areas and process for resolution of Claims:

1) Known Claims that Kiewit has been working on with Metro, including previous DRB Decisions
2) New Claims that Kiewit has recently submitted
3) The above claim areas will continue to be resolved outside of the Arbitration process. If these claims are not resolved by the 6th month of Arbitration, they can or will be rolled into the Arbitration process by Kiewit.
4) Phase I Arbitration: resolve all discrete claims on the Project, except Claim 86
5) Phase II Arbitration: Claim 86 on delay and disruption

Cost Forecasting

Project recognizes three (3) key areas of cost increase:

1) Labor from Caltrans, Metro, Consultant, and City – This is being caused by the schedule delay and keeping staff onboard longer than anticipated. In addition, Caltrans has been charging significant amount of hours for some time which has little to do with delay, but their interpretation of what is needed to perform Independent Quality Assurance.
2) Claims – The Contractor has always had Potential Impact letters and has reserved its right to claim areas of the work. Kiewit continues to submit claims and Metro is responding to the letters. Metros forecast cost-to-complete includes Kiewit's latest submitted claims.
3) Right-of-Way (ROW) capital billings by Caltrans are reported to Metro after the fact. This was initially reported going over budget according to Caltrans billing documentation. Metro and Caltrans are in the process of reconciling these cost

PROJECT OVERVIEW & STATUS (Cont'd)

.

issues and it appears that there was double counting of these costs, plus Caltrans was anticipating unknowns that do not appear to be real. A credit back to the construction funds is a real possibility and we are currently waiting for Caltrans to finalize ROW costs to determine availability of these funds

Forecasting costs for labor is real and we expect the cost of the project to increase with little control over these costs as they are associated with an impact. ROW is being verified by Metro and the control of this is in Caltrans authority to administer; Metro can only verify that these costs are appropriate. The costs of Claims depend on Kiewit requesting a hearing and the outcome of those hearings. The swing on these issues is significant ($44.9M) and we expect over the next several months a significant dollar amount of claims to be resolved.

Cost Recovery

I-405 Team has put together a list of issues that are considered improvements, excessive mitigations, or just requests from Caltrans, City, and County Agencies that contributed to the LOP Budget increase. Some of these are well documented, some are not. Examples include the Getty work and ramp improvements (Caltrans), widening of Sepulveda and slide repairs at Sepulveda and Homedale (City), and turn pocket SB Sepulveda at Wilshire (County).

MANAGEMENT ISSUES

Concern No. 1: Project Cost and Schedule Reassessment

Status/Action LOP increase for September 2015 Board is $115M and the reasoning and amounts are listed in the Board Report and summarized below:

Current Forecast		
Project Close Out		
Provisional Sum Authorizations and Change Orders	$ 8.9M	
Legal Cost for Dispute Resolution Board	$ 7.78M	
3rd Party/Master Co-Operative Agreement and Others	$ 15.22M	
Professional Services (Metro/Caltrans/Consultants)	$ 29.80M	
Claims (at 50% Risk Level)	$ 44.86M	
Sub-Total		$106.56M
Less Contingency	($ 16.56M)	
Sub-Total (net)		$ 90.00 M
Arbitration		
Legal and Expert Costs	$ 20.00M	
Staff Support	$ 5.00M	
Sub- Total		$ 25.00 M
Net Requested LOP Increase (September 2015)		$115.00 M
Unknown Arbitration Judgment		$ TBD

Concern No. 2: Landscaping

Status/Action See City and Caltrans Trees in Project Overview above

The Project has determined the need for 435 additional trees within the City ROW and 3800 additional trees within the Caltrans ROW as mitigation for all the trees removed by the Contractor. Regardless, the Project footprint cannot take the above mentioned number of trees and Metro has been working with both City and Caltrans staff to address this, to no avail.

The Project, City, and Caltrans have been meeting on this issue continuously and options appear to be as follows:

1) Establish responsibility for planting – Kiewit or Metro
2) Determine who should do the work: City or Metro/Caltrans, since Kiewit is not going to do the work.
3) Mitigation bank
4) We have determined trees will be planted outside the project limits.
5) Finalizing pricing of this effort is being studied to help narrow down options. Metro is working on letter to City Department of Public Works BSS to identify what Metro/Caltrans will do for tree planting and Maintenance. The following conflict will be

MANAGEMENT ISSUES (Cont'd)

highlighted: 1 year of maintenance according to the Project Contract and several additional years as being requested by City BSS.

Concern No. 3: Commercial Issues

Status/Action Metro continues with the effort of resolving commercial issues with Kiewit.


Concern No. 4: Caltrans Staff and Real Estate Cost

Status/Action Caltrans ROW has determined that $18.6M can be allocated to Construction. Caltrans ROW has reserved $10M for Environmental Mitigation. Recent cost analysis has shown a cost overrun for Caltrans staff budget cost. Caltrans staff costs have been brought up to Caltrans Executive Management in the past and Caltrans has informed Metro on every occasion that staff charges are appropriate. These overruns are ongoing issues and project is looking for viable solutions to resolve these issues. Project is also re-assessing related potential cost increases.

Concern No. 5: Potential Increases to Staffing Costs

Status/Action Metro has monitored our Support costs and Consultant costs with delay and Claims resolution driving the costs- We have incorporated all of these costs in our LOP Budget increase for September 2015 Board Report.

PROJECT SCOPE

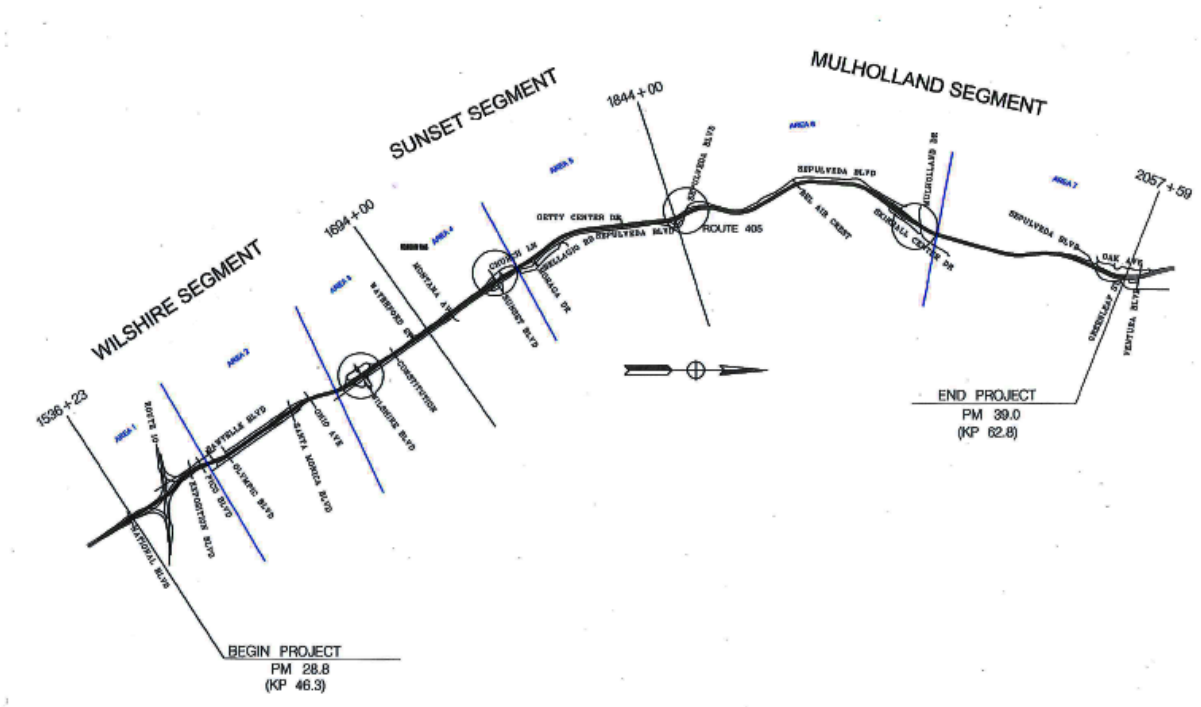

The I-405 Sepulveda Pass Improvements Project is a Design-Build contract to add a 10-mile High Occupancy Vehicle (HOV) lane on the northbound San Diego Freeway (I-405) between the Santa Monica (I-10) and Ventura (US 101) Freeways. The purpose of the project is to reduce congestion by adding the HOV lane and closing the HOV gap, which will provide a continuous HOV lane from the Orange County Line to the I-405/US-101 interchange. The scope entails an 11-foot half median, one 12-foot HOV lane, a 1-foot HOV buffer, five 12-foot mixed-flow lanes (six 12-foot mixed-flow lanes between Mulholland Bridge and Valley Vista), and a 10-foot outside shoulder.

Most of the freeway widening required for this project occurs along the east side of I-405 along Sepulveda Blvd. between Montana Ave. and Moraga Dr. and between Getty Center Drive and the northbound Getty Center off-ramp. Sepulveda Blvd. is going to be slightly realigned at the relocated southbound I-405 Skirball Center Drive on/off-ramps in order to add a dual-left-turn lane to the on-ramp.

Some freeway widening also occurs along the west side of the freeway between Olympic Blvd. and Waterford Street, and between Bel Air Crest to just north of Ventura Blvd. This entails NB and SB lanes and shoulder standardization.

In order to reduce accidents associated with traffic on the ramps, project scope includes several interchange improvements as detailed below:

PROJECT SCOPE

- Wilshire Blvd. interchange in both directions
  The northbound on-ramp from eastbound Wilshire Blvd. is grade-separated from the northbound off-ramp to westbound Wilshire Blvd. and from Sepulveda Blvd. The southbound off-ramp to eastbound Wilshire Blvd. is grade-separated from the southbound off-ramp to westbound Wilshire Blvd.

- Northbound I-405 Sunset Blvd. interchange
  The northbound I-405 off-ramp to eastbound Sunset Blvd. is widened to include one more lane. Two exclusive 12-foot lanes on the reconstructed Sunset Blvd. overcrossing and two 12-foot lanes on the on-ramp are provided for the northbound I-405 on-ramp from eastbound Sunset Blvd. In the eastbound direction three 12-foot lanes and in the westbound direction three 11-foot lanes are provided which solves the existing reduction from three lanes to two lanes in the eastbound direction. In both directions, 4-foot shoulders and 5-foot sidewalks as well as a 13-foot median are provided on the Sunset Blvd. overcrossing.

- The irregular northbound I-405 on/off-hook ramps at the Getty Center interchange are reconfigured to a standard diamond interchange to increase stopping sight distances in order to improve safety.

- The southbound I-405 Skirball Center Drive interchange is relocated to form a “T” intersection with Sepulveda Blvd. This eliminates the existing intersection at Skirball Off-Ramp and Skirball Center Drive.

- The southbound Valley Vista On and Off Ramps are realigned due to freeway widening and freeway mainline realignment between SB Valley Vista On/Off Ramps. The realignment will improve the stopping sight distance for the SB Valley Vista Off-Ramp. A third lane will be added to the SB Valley Vista On-Ramp to increase the ramp capacity.

- A second NB lane will be added on Skirball Center Drive between the Skirball Bridge and NB Skirball ramps.

- A NB auxiliary lane and bike lanes will be added on Sepulveda Blvd. on each direction, between the new SB Skirball ramps and Skirball Bridge.

A total of 12 soundwalls and 54 retaining walls within the project limits are constructed at embankments where right-of-way is constrained.

A total of 12 undercrossings within the project limits are widened. Three overcrossings at Sunset Boulevard, Skirball Center Drive, and Mulholland Drive are replaced.


KEY MILESTONE SCHEDULE SIX-MONTH LOOKAHEAD

	Milestone Date	Apr-15	May-15	Jun-15	Jul-15	Aug-15	Sep-15
Wall 2041 - Rework Grading for Case 1/2 Issue	4/10/15A	○					
Wall 2004 - Rework Substandard Barrier Completed	4/21/15A	○					
Wall 1915 - Rework Substandard Barrier Completed	4/24/15A	○					
Removed Temporary Project Signs	4/25/15A	○					
Complete Project Wide Paving Profilograph/Grind on mainline and ramps.	4/27/15A	○					
Complete Fiber Optic splices for Verizon Wireless relocation at Wilshire	4/28/15A	○					
Final Landscaping completed for HMMP changes	5/1/15A		○				
Striping Touch-up Project Wide	5/20/15A		○				
Straightened Traffic Signal Head at NB Getty On-ramp	5/22/15A		○				
Application for Substantial Completion	6/26/15A			○			
Soil and Compaction Testing for Case 1/2 Issue at seven Walls Completed	6/30/15A			○			
Slope Grading Rework and Jutemesh Install at Bridges 7 & 8 Completed	6/30/15A			○			
Punchlist Inspection & Work	7/1/15				○		
Punchlist Inspection & Work	8/1/15					○	
Punchlist Inspection & Work	9/1/15						○
Substantial Completion Accceptance	9/30/15						○

Metro Metro Milestone ○ Design/Build △ Third Parties Approval

CT Caltrans Milestone * New Date FHWA FHWA Federal Highway Administration Approval

PROJECT SUMMARY SCHEDULE

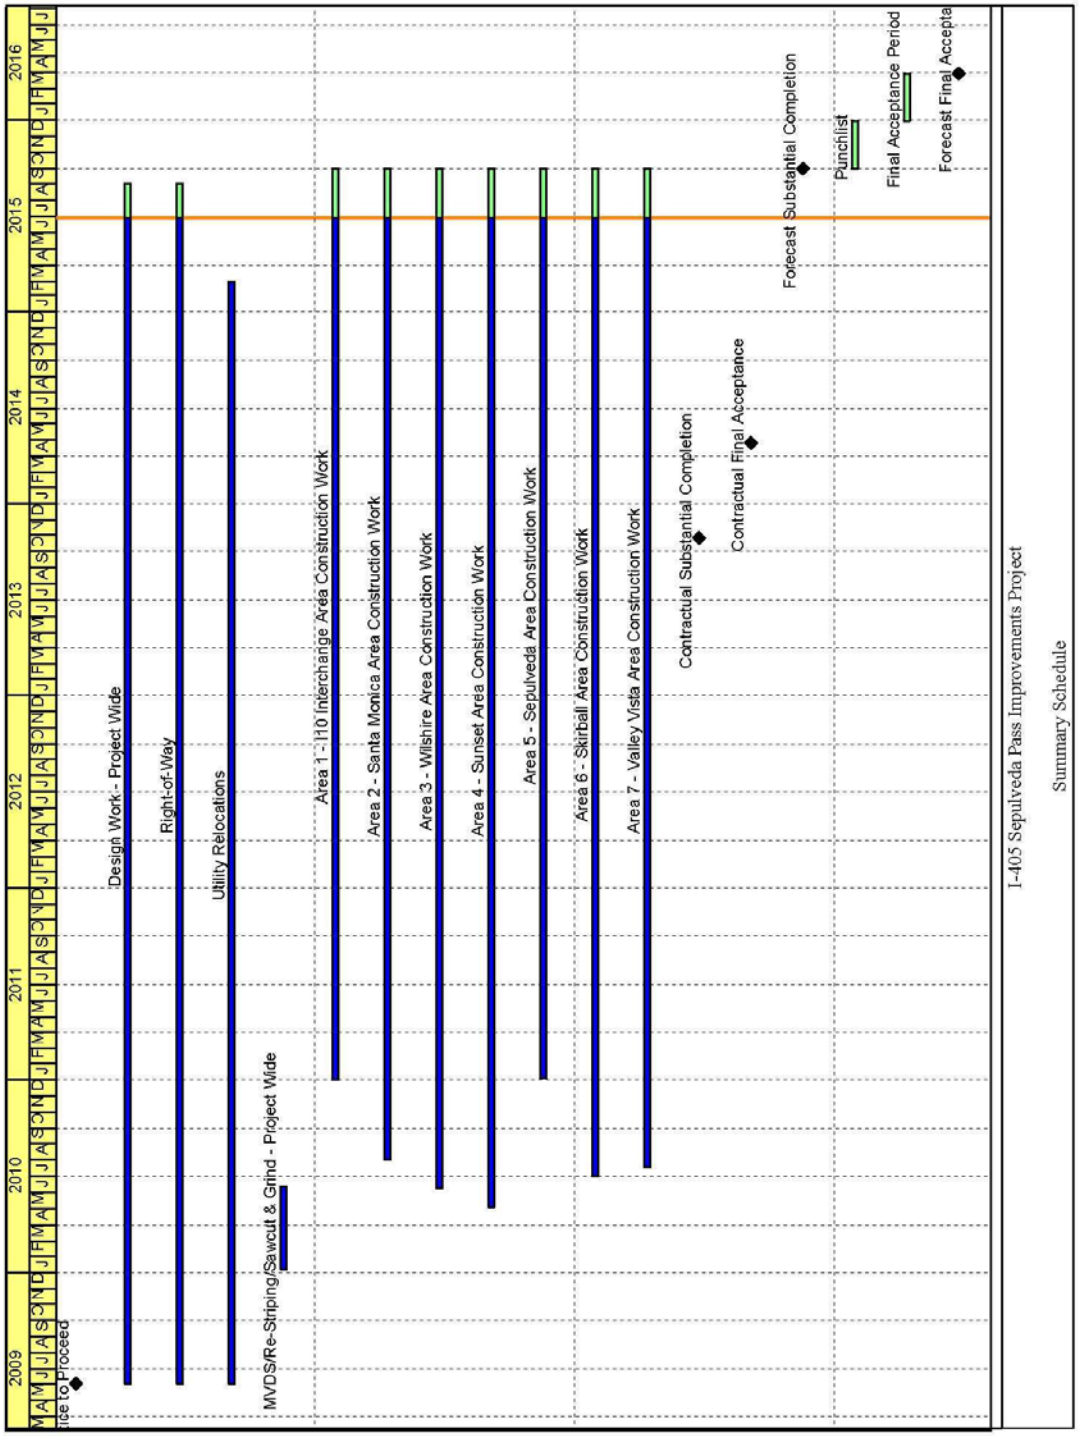

CRITICAL PATH NARRATIVE

Based on the current project update, the critical path runs through irrigation and landscaping.

PROJECT COST STATUS

METRO CONSTRUCTION MANAGEMENT DIVISION / CALTRANS
COMBINED COST REPORT BY PHASE
PERIOD ENDING: JUNE 2015
DOLLARS IN THOUSANDS

PHASE #	PHASE CODE	DESCRIPTION	ORIGINAL BUDGET	CURRENT BUDGET		COMMITMENTS		EXPENDITURES		CURRENT FORECAST		BUDGET / FORECAST VARIANCE
				PERIOD	TO DATE	PERIOD	TO DATE	PERIOD	TO DATE	PERIOD	TO DATE	
0	PA&ED	PROJECT APPROVAL & ENVIRO DOCS	22,000	-	21,457	-	21,078	-	21,078	-	21,457	-
1	PSE	PLANS, SPECS, & ENGINEERING	63,100	-	25,560	39	26,159	39	26,131	-	25,632	72
2	RS	RIGHT-OF-WAY SUPPORT	14,000	-	9,543	110	9,302	110	9,302	-	8,076	(1,467)
3	CS	CONSTRUCTION SUPPORT	28,000	-	67,735	1,501	123,538	1,524	119,462	-	85,519	17,784
4	C	CONSTRUCTION	823,900	-	915,319	-	886,798	3	874,721	-	937,324	22,005
9	RC	RIGHT-OF-WAY CAPITAL	83,000	-	99,186	10	67,751	151	62,507	-	60,792	(38,394)
		SUBTOTAL PROJECT	**1,034,000**	**-**	**1,138,800**	**1,661**	**1,134,627**	**1,827**	**1,113,201**	**-**	**1,138,800**	**-**
4	C	CONSTRUCTION OF CITY OF L.A.'S REVERSIBLE LANES PROJECT	-	-	2,600	-	1,466	-	1,466	-	2,600	-
4	C	CONSTRUCTION OF CALTRANS DRAINAGE SYSTEM REPAIRS	-	-	-	-	-	-	-	-	-	-
		TOTAL PROJECT	**1,034,000**	**-**	**1,141,400**	**1,661**	**1,136,093**	**1,827**	**1,114,667**	**-**	**1,141,400**	**-**

NOTE: EXPENDITURES ARE CUMULATIVE THROUGH MAY 31, 2015.
KIEWIT EXPENDITURES ARE ONLY THROUGH JANUARY 31, 2015 DUE TO INVOICING LAG.
CALTRANS EXPENDITURES ARE ONLY THROUGH MAY 22, 2015.

PROJECT COST ANALYSIS

Original and Current Budgets

The Original Budget reflects the Metro Board adopted Life-of-Project (LOP) Budget which was approved in April 2009 in the amount of $1,034 million. An additional $6.0 million was approved by the Metro Board in February 2011 to add the City of LA's Reversible Lanes Project Scope funded by the City of Los Angeles, along with $8.0 million approved by the Metro Board to add Caltrans drainage system repairs to be funded by Caltrans. The Metro Board approved a decrease in the amount of $3.4 M for the Reversible Lanes and an increase of $26.1M for betterments. This brings the total Current Budget to $1,070.7 million. In June and July 2013, the Metro Board approved increases of $70.7 million which brings the Current Budget to $1,141.4 million. The Project Cost Report has been updated to reflect this increase.

Current Budget and Current Forecast

The Current Budget is $1,141.4 million. Trends 1 through 391 have been approved and are included in the Current Forecast of $1,141.4 million. Trends are being prepared for all Professional Services (including Metro, Caltrans and Stantec staff) and will be included in next month's report. Project Budget Change Requests (PBCR) 1 through 9 have been issued and included in the Current Budget.

Commitments

The Commitments increased by $1.7 million this period primarily for Legal Services purchase orders, Kiewit Contract Modifications and Metro/Caltrans staff charges. Total Commitments are $1,136.1 million.

PROJECT COST ANALYSIS (Cont'd)

Expenditures

Expenditures are cumulative through May 2015. The period expenditures were $1.8 million. Expenditures within the construction support phase included Metro and Caltrans project staff and miscellaneous consultant contract services. Costs in the right-of-way categories were for 3rd party Metro staff costs and for third party expenditures. Caltrans right-of-way expenditures for the period included staff charges for right-of-way support and purchase orders for right-of-way capital. No Kiewit invoices were processed by Metro Accounting this period. The $1,114.7 million in Project Expenditures to date represents 97.7% of the Current Budget.

FINANCIAL/GRANT STATUS – ORIGINAL SCOPE ACTIVITIES

JUNE 2015 **STATUS OF FUNDS BY SOURCE**

SOURCE	(A) APPROVED BUDGET	(B) TOTAL FUNDS ANTICIPATED	(C) TOTAL FUNDS AVAILABLE	(D) COMMITMENTS $	(D/B) %	(E) EXPENDITURES $	(E/B) %	(F) BILLED TO FUNDING SOURCE * $	(F/B) %
FEDERAL SAFETEA-LU	$117.000	$117.000	$117.000	$117.000	100%	$117.000	100%	$72.266	62%
FEDERAL ARRA	$189.900	$189.900	$189.900	$189.900	100%	$189.900	100%	$189.900	100%
STATE CMIA	$640.100	$640.100	$640.100	$640.100	100%	$640.100	100%	$630.661	99%
STATE TCRP	$90.000	$90.000	$90.000	$90.000	100%	$90.000	100%	$48.737	54%
STATE RSTP	$10.100	$10.100	$10.100	$10.100	100%	$10.100	100%	$10.100	100%
PROPOSITION C 25%	$13.000	$88.000	$88.000	$87.527	99%	$66.101	75%	$2.125	2%
FURTHER COST/REVENUE RECOVERY	$0.000	$3.700	$0.000	$3.700	100%	$0.000	0%	$0.000	0%
SUB TOTAL FUNDS	$1,060.100	$1,138.800	$1,135.100	$1,138.327	100%	$1,113.201	98%	$953.789	84%
CITY OF LA **	$2.600	$2.600	$0.000	$1.466		$1.466		$0.000	
TOTAL FUNDS	$1,062.700	$1,141.400	$1,135.100	$1,139.793		$1,114.667		$953.789	

NOTE: EXPENDITURES ARE CUMULATIVE THROUGH MAY 2015
TOTAL FUNDS ANTICIPATED BASED ON JUNE 2013 PROJECT COST AND FUNDING PLAN AND JULY 2013 BOARD REPORT.
* BILLING AMOUNT IS LESS THAN EXPENDITURES AMOUNT DUE TO SYSTEM LAG IN SUBMITTING INVOICES TO CALTRANS.
** CONSTRUCTION OF CITY OF LA REVERSIBLE LANES PROJECT.

STATUS OF FUNDS ANTICIPATED

FEDERAL SAFETEA-LU: $117M is available for drawdown for specific phases of the Project as agreed upon in the Cooperative Agreement between Caltrans and Metro.

FEDERAL ARRA: $189.9M is available for drawdown for specific phases of the Project as agreed upon in the Cooperative Agreement between Caltrans and Metro with consultation with FHWA.

STATE CMIA: State Proposition 1B Bond sales provided $254.7M to the project. Funds are available for drawdown. The remaining balance of $359.3M has been allocated and are available for drawdown. In December 2012, the California Transportation Commission and Metro Board approved the reprogramming of $26.1M in CMIA funding to the I-405 Project. Funds are available for drawdown.

STATE TCRP: $42M is available for drawdown for specific phases of the Project as agreed upon in the Cooperative Agreement between Caltrans and Metro. The remaining balance of $48M has been made available by the CTC and is available for drawdown.


STATE RSTP: $10.1M is available for drawdown for specific phases of the Project as agreed upon in the Cooperative Agreement between Caltrans and Metro.

PROPOSITION C 25%: The Metro Board initially approved the allocation of $13M to the Project. In June 2013, the Metro Board approved an additional allocation of $75M.

CALTRANS: Metro Board authorized staff in July 2012 to execute a Memorandum of Understanding between Caltrans Maintenance and Metro for a total amount of $8M for the cleaning and the reconstruction of Caltrans drainage. In March 2013, Caltrans informed Metro that the work and funding have been cancelled.

STAFFING STATUS


Total Project Staffing - FTEs

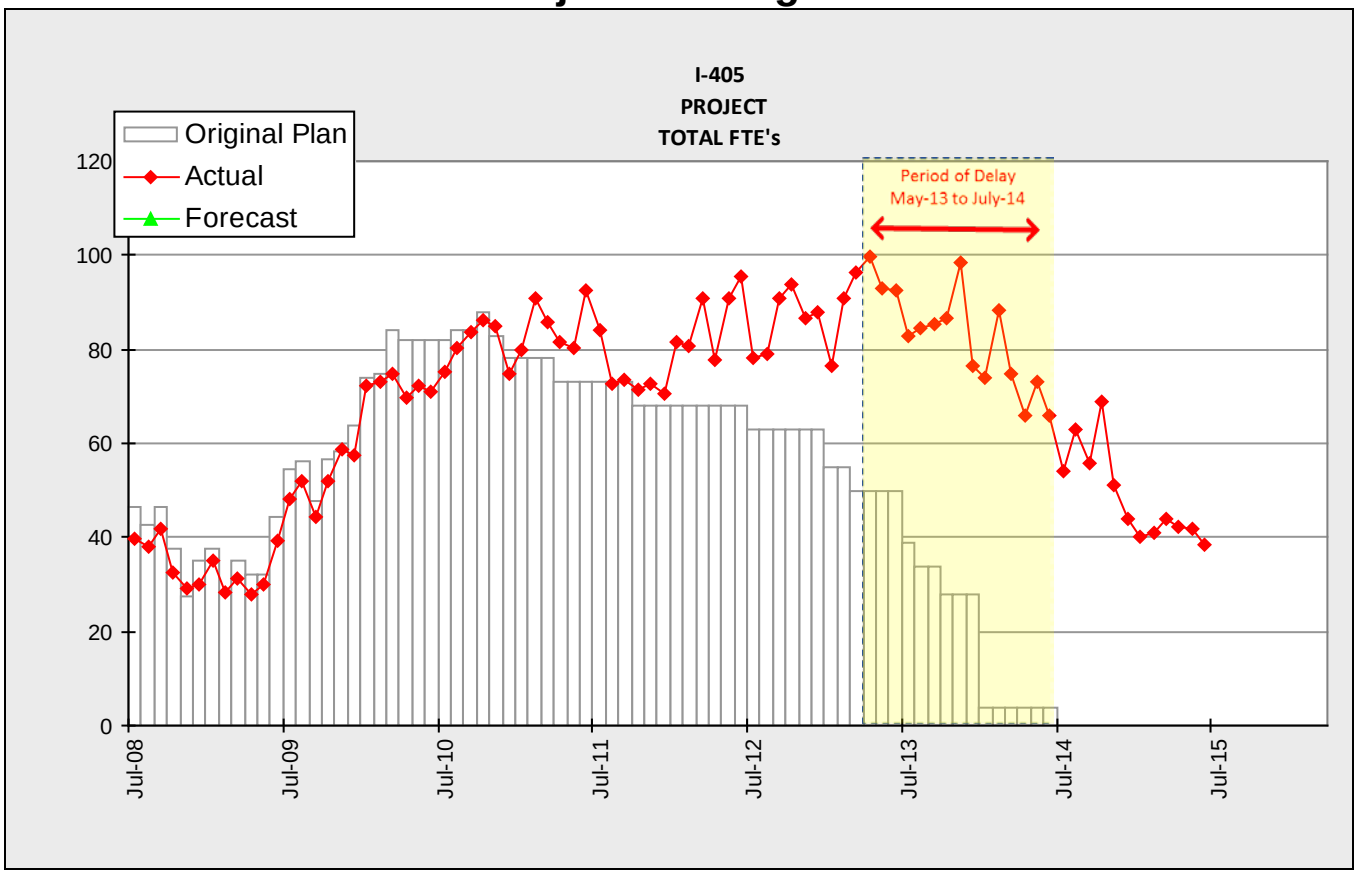


Total Project Staffing


Due to the project delay, project staffing has been reforecasted through the end of project as shown in the staffing status charts.

STAFFING STATUS (Cont'd)

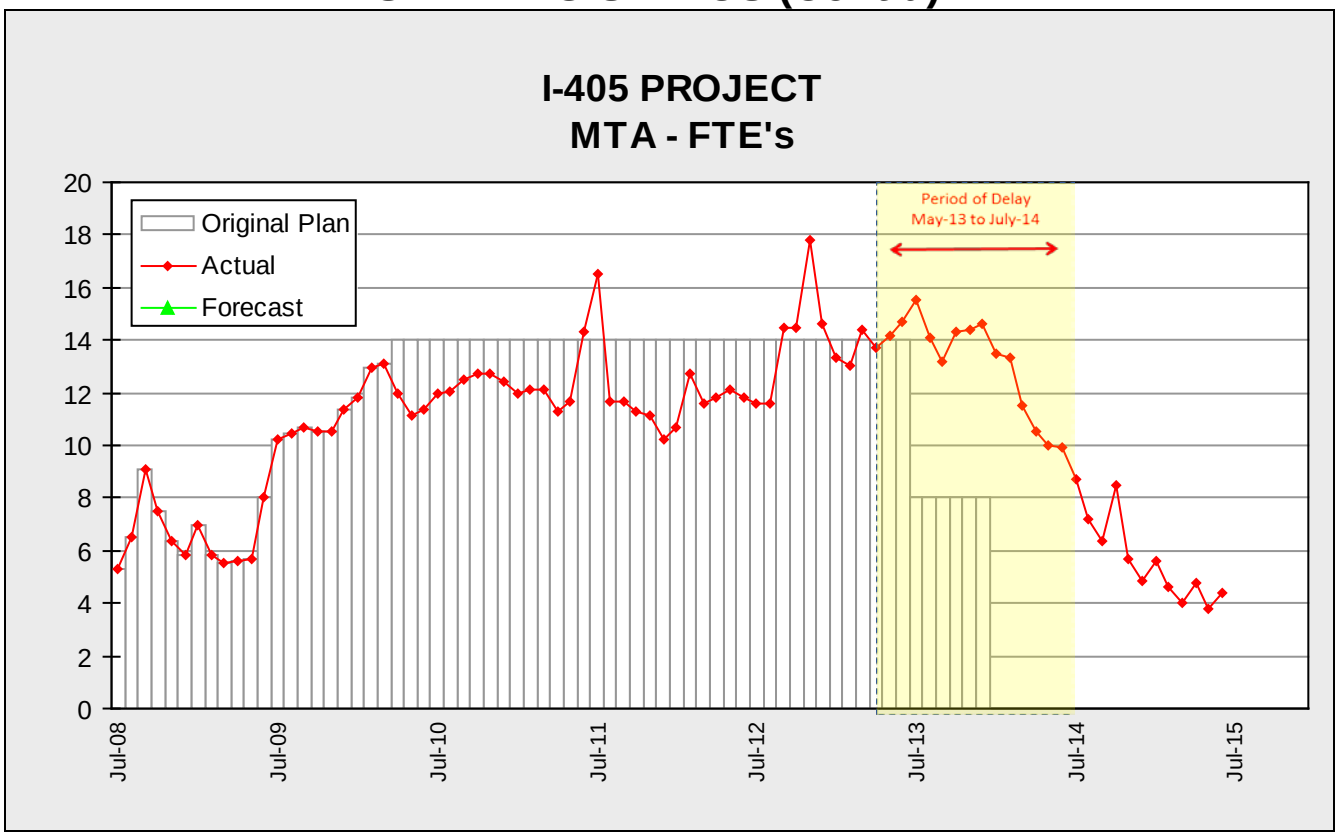

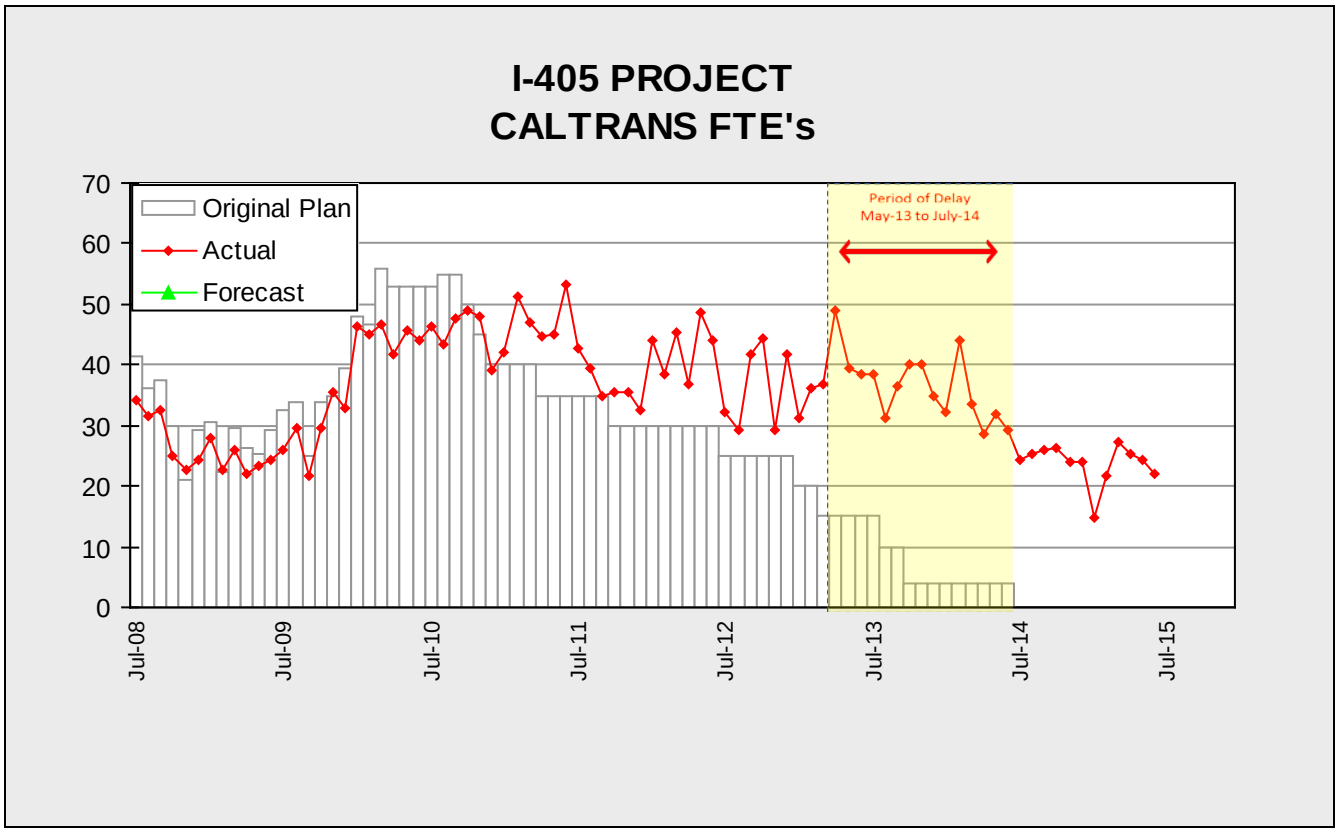

STAFFING STATUS (Cont'd)

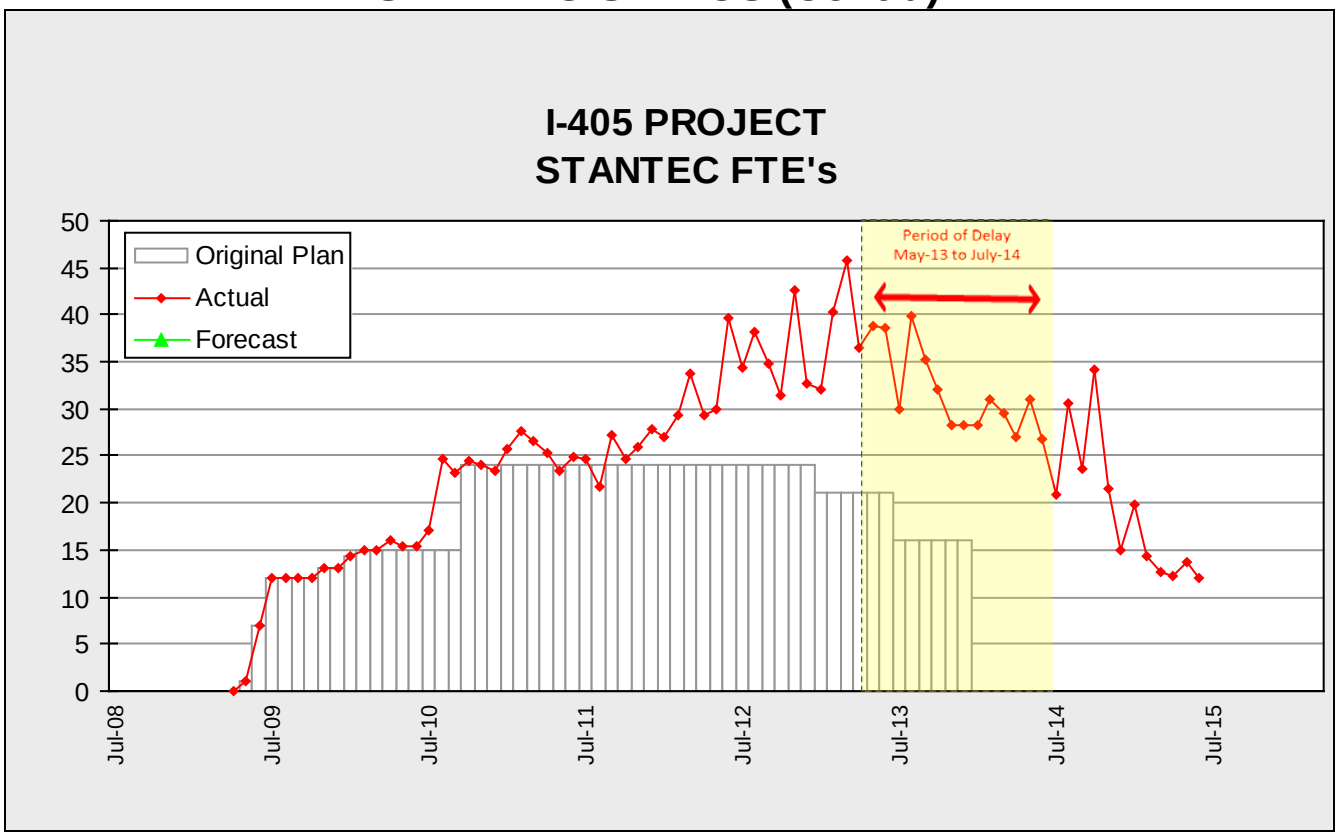

REAL ESTATE STATUS

The Real Estate acquisition process is proceeding and the Project is working on obtaining and releasing the parcels to the Contractor.

- Parcel 79612 (MWD) – Right-of-Entry (ROE) is in place for the SB Skirball Ramps. All work is complete. Caltrans is in the process of finalizing and acquiring the Permanent ROW requirements.
- ROW at the Getty – ROE has been provided. Caltrans is in the process of acquiring the rights pending a final meeting with the Getty.
- Parcel 79619 (LACMTA) – Construction has been completed. Caltrans HQ is currently reviewing the deeds.
- Parcel 80387 (Leo Baeck Temple) – The work has been completed under a temporary easement. Caltrans is in process of acquiring the permanent rights. Leo Baeck is currently reviewing the final language in the deeds.
- Parcel 79559 (GSA) – A temporary construction easement was acquired to do the work at the GSA. Currently the GSA is reviewing the final deeds for final conveyance of the property.

SAFETY AND SECURITY STATUS

- There were no injuries on the Project during the quarter April to June 2015.
- Monitoring of construction activities concluded on June 30, 2015.
- Due to reductions in administrative staff the Contractor has fallen behind in reporting monthly work hours. An up to date work hour report will be submitted next quarter.
- December Contractor Work Hours (Design & Construction): 44,633
- Contractor – Project to Date Work Hours (Design & Construction through 12/31/2014): 8,761,454
- Total Project to Date Work Hours (Contractor & the IPO Staff through 12/31/2014): 9,579,266
- Project to Date Recordable Injury Rate: 0.7 (Thirty-four Recordable Injuries) (each rate is per 200,000 work hours).
- Project to Date Total Time Away Injury Rate: 0.3 (Fifteen Time Away From Work Injuries).
- Project to Date Total Days Away Rate: 28.3 (1,356 Days Away From Work)
- Metro Construction Safety is providing Safety and Security Contract Compliance oversight during both day and night shifts. During weather events when work is suspended, compliance visits are focused on security issues.

CONTRACT STATUS

I-405 Sepulveda Pass Improvements Project
Design/Build Contractor: Kiewit

Contract No.: C0882

Status as of: June 26, 2015

Progress/Work Completed:
Major work started/completed this period:
· Kiewit submitted Application for Substantial Completion.
· Landscaping work.
· Punchlist work begins.
· Non-standard barrier and wall correction begin.

Areas of Concern:
· Cracks in retaining walls / soil nail walls (Case 1/ Case 2).

Major Activities (In Progress):
· Punchlist work
· Corrective actions for non-standard items.
· Soil sampling and compaction testing at Case 1/2 Walls.
· Maintenance during construction.

Major Activities Next Period:
· Project wide punchlist activities completion.
· Substantial completion.

	Original Baseline	Time Extension	Current Contract	Forecast Completion	Variance Cur-Fcast
Commencement	08/31/09	0	08/31/09	08/31/09	0
Completion	05/31/13	149	10/27/13	09/30/15	-703
Punchlist Complete	08/29/13	149	01/25/14	12/29/15	-703
Final Acceptance	11/27/13	149	04/25/14	03/28/16	-703

Schedule Summary:

Notice of Award	04/29/09
Notice to Proceed	06/02/09
Original Contract Duration (CD)	1640
Approved Time Extensions (CD)	149
Current Contract Duration (CD)	1789
Forecast Contract Duration	2492
Forecast Final Acceptance	03/28/16
Elapsed Time from NTP (CD)	2216
Contract Elapsed Time Percent	88.9%

Cost Summary: **$ In 000's**

1. Award Value:	720,922
2. Executed Modifications:	144,740
3. Approved Change Orders:	45,920
4. Current Contract Value (1 + 2 + 3):	911,582
5. Incurred Cost:	874,971
6. Percent Incurred Cost:	96.2%

CHRONOLOGY OF EVENTS

May 18, 2007	The Draft Environmental Impact Report (EIR)/Environmental Impact Statement (EIS) is issued.
May 22, 2007 to October 1, 2007	Public review of draft EIS.
February 29, 2008	The Final Environmental Impact Report (EIR)/Environmental Impact Statement (EIS) is issued.
March 10, 2008	The Final Environmental Impact Report (EIR)/Environmental Impact Statement (EIS) errata with U. S. General Services Administration (GSA) comments is issued.
March 14, 2008 to April 14, 2008	Public review of Final EIS.
April 25, 2008	Record of Decision (ROD) approved.
October 10, 2008	LACMTA issued Invitation For Bid (IFB) for the project.
February 20, 2009	Project bids opened.
April 23, 2009	LACMTA Board authorized the Chief Executive Officer to award Design-Build Contract C0882 to Kiewit Pacific Co.
April 23, 2009	LACMTA Board approved establishing a budget of $1.034 billion for project 405523.
April 23, 2009	LACMTA awarded Contract C0882 to Kiewit Pacific in the amount $694,156,000 to include Schedules A, C, and H (Option 4).
April 29, 2009	LACMTA issued a revised NOA to Kiewit Pacific in the amount $720,922,000 to include Schedules A, C, E (Option 1), F (Option 2), G (Option 3), and H (Option 4).
June 2, 2009	LACMTA issued Notice to Proceed to Kiewit Pacific for the Design-Build Contract C0882.
August 31, 2009	Contract Commencement Date.
September 24, 2009	Kiewit Pacific submitted the Project Baseline Schedule.
October 14, 2009	Project Design Quality Management Plan approved.

CHRONOLOGY OF EVENTS (Cont'd)

December 14, 2009	Project Quality Management System approved.
January 20, 2010	Project Baseline Schedule was approved.
January 27, 2010	Roadway Restriping commenced.
March 12, 2010	Major Project Permits were obtained; Permit 401 – Water Quality Control Board, Permit 404 – U.S. Army Corps of Engineers, and Permit 1600 – California Department of Fish & Game.
May 31, 2010	The Project completed one year without a Recordable Injury.
July 23, 2010	Sunset Bridge major demolition of the south side top deck and center column.
August 2, 2010	Commenced construction on Bridge 4a/b.
August 16, 2010	Commenced ExxonMobil 16" utility relocation at Bridge 16.
August 20, 2010	Operating Engineers Local 12 initiate labor action by striking.
August 24, 2010	Completed ductbank work on Sepulveda for DWP utility undergrounding.
August 24, 2010	Commenced construction of Walls 1720/1730.
August 24, 2010	ITS Backbone is cut.
September 7, 2010	DWP started pulling wires for utility undergrounding on Sepulveda.
September 9, 2010	Operating Engineers Local 12 Labor action is settled and strike ends.
September 13, 2010	Completed the excavation of Roadway at 1685/1691.
September 15, 2010	Completed the removal of Wall 1665.
September 18, 2010	Completed installation of Temporary walkway at Skirball Bridge.
September 28, 2010	Pioneer access to Sunset on-ramp, Bridge 15 Abutment 1.

CHRONOLOGY OF EVENTS (Cont'd)

October 12, 2010	Began excavation of Sunset Bridge 16 Abutment 1 Footing.
October 12, 2010	Began demolition of Skirball Bridge 21.
October 15, 2010	Completed demolition Skirball Bridge 21.
October 15, 2010	Began driving piles at Santa Monica Bridge 4.
October 15, 2010	Installed Beams at Sunset Bridge 16, Bent #2.
October 15, 2010	Began driving piles on Santa Monica Bridge 4.
October 19, 2010	Completed demolition of Sunset Bridge 16, Abutment 4.
October 21, 2010	Installed beams at Sunset Bridge 15 On Ramp, Abutment 1.
October 22, 2010	Began Demolition of Sunset Bridge 16, Abutment 1.
October 22, 2010	Installed Piles at Wall 1720.
October 25, 2010	Began Excavation at Walls 1685/1691.
October 28, 2010	Began the relocation of overhead power lines at Ohio Ave Bridge 5.
October 28, 2010	Clear and grub area at Wall 1746.
November 12, 2010	Completed demolition of soundwall, barrier rail, and overhang at Bridge 13.
November 15, 2010	Completed installation of SOE at Abutment 1 NB at Bridge 4 Santa Monica.
November 15, 2010	Completed demolition of existing ExxonMobil16" Oil Pipeline.
November 17, 2010	Completed excavation of CIP at Wall 1640.
November 18, 2010	Began excavation at Wall 1635.
November 29, 2010	Began Excavation at Bridge 13.
November 30, 2010	Began relocation of SCE underground vault.

CHRONOLOGY OF EVENTS (Cont'd)

December 7, 2010	Began driving piles at Bridge 13 - Montana Avenue UC.
December 14, 2010	Completed Pile driving at Abutment 1 Bridge 16 Sunset OC.
December 15, 2010	Completed the installation of new power poles and raised the utility wires at Bridge 5 - Ohio Avenue.
December 16, 2010	Completed piles at abutments 1 and 2 for Bridge 13 Montana Ave UC.
December 17, 2010	Began installation of SOE beams at Bridge 15 Sunset on-ramp.
January 3, 2011	Began Construction of Piers and Columns at Bridge 16.
January 11, 2011	Began Construction Activities at Bridge 5.
January 13, 2011	Began Construction Activities at Bridge 12.
January 17, 2011	Began Installation of Footings and Pile Caps at Bridge 16.
February 1, 2011	Began Construction Activities at Bridge 21 – Skirball Center Drive.
February 14, 2011	Began Field Work relocating Storm Drain at Veterans Administration (VA).
February 21, 2011	Began Field Work relocating Chevron Oil Pipeline at Bridge 23 – Sepulveda UC.
February 23, 2011	Began Construction Activities at Bridge 15 – Sunset On-Ramp.
February 25, 2011	Completed Drilling and Placing Beams at NB Abutments 1 & 2 at Bridge 12 – Constitution UC.
February 28, 2011	Completed Pouring Columns at Bent 3, Bridge 16 – Sunset OC.
March 2, 2011	Began Field Work relocating LADWP 4" Waterline at Valley Vista.
March 2, 2011	Completed Driving 14" Square Piles at Bridge 3 Abutment 1.
March 15, 2011	Began Field Work relocating So Cal Gas Line at Wall 1746.

CHRONOLOGY OF EVENTS (Cont'd)

March 18, 2011	Completed Setting Soldier Beams at Bridge 15 Bent 2 & 3 Mainline.
March 23, 2011	Began Field Work Encasing Sewer Lines 401-403 at Walls 1720, 1730 and 1746.
March 31, 2011	Completed Setting and Backfilling Wall Panels at Wall 1942B.
April 4, 2011	Began Installation of Bent 2 & Bent 3 Columns at Bridge 21 Skirball Center Drive OC.
April 5, 2011	Began Installation of Storm Drain at Walls 1720 and 1730.
April 10, 2011	Completed Installation of Girders at Bridge 13 Montana Ave UC.
April 22, 2011	Completed Bridge 9 Wilshire Blvd. UC demolition for widening.
April 25, 2011	Began Work Relocating Shell Oil Line at Bridge 23 Sepulveda UC.
May 2, 2011	Began Relocation of Area 2 Sewer Lines # 201-203.
May 6, 2011	Completed Setting Girders at Southside of Bridge 16 Sunset OC.
May 11, 2011	Began Construction Work on Bridge 3 Olympic Blvd.
May 25, 2011	Completed Tie Back Installation at Walls 1720 and 1730.
June 3, 2011	Completed Girder Installation on the North Side of Bridge 21 Skirball OC.
June 13, 2011	Began Installation of Precast Deck Panels on Bridge 16 Sunset OC.
June 24, 2011	Began Demolition of Existing Walls 1720 and 1730 along Sepulveda Blvd.
June 30, 2011	Completed Installation of Precast Deck Panels on Bridge 16 Sunset OC.

CHRONOLOGY OF EVENTS (Cont'd)

July 6, 2011	Began Relocation of LADWP Overhead Power Lines at Mulholland Bridge.
July 13, 2011	Completed installation of Void Slab Deck at Bridge 12 Constitution UC.
July 14, 2011	Completed Pouring Diaphragms 1, 2, and 3 at Bridge 21 Skirball OC.
July 16, 2011	Began Demolition of South Side of Bridge 22 Mulholland OC.
July 17, 2011	Completed Demolition of South Side of Bridge 22 Mulholland OC.
July 20, 2011	Completed Installation of Pre-cast Girders at Bridge 4SB Santa Monica UC.
July 26, 2011	Began Driving Piling at Bridge 8 NB from EB Wilshire, Bent 8.
August 1, 2011	Began installation of forms and rebar for Top Deck at Bridge 21, Skirball Center Drive.
August 3, 2011	Began work on the Interchange Ramp from Westbound I-10 to Northbound I-405.
August 6, 2011	Began work installing Top Deck at Bridge 4 Santa Monica Blvd.
August 24, 2011	Completed pouring the Top Deck at Bridge 13, Montana Ave.
August 26, 2011	Completed installation of Footing & Pile Cap/Abutment-Wingwalls/Bridge Bearing Bridge 3 Olympic Blvd.
August 31, 2011	Completed pouring the Top Deck at South Side of Bridge 16, Sunset Blvd.
September 15, 2011	Completed installation of Top Deck and Diaphragm on Bridge 16, Sunset Blvd.
September 16, 2011	Completed pouring the Top Deck at Bridge 21, Skirball Center Drive.
September 23, 2011	Began construction of LADWP Power Utilities undergrounding ductbank between Stations 1740 and 1760.

CHRONOLOGY OF EVENTS (Cont'd)

September 27, 2011	Completed pouring curb and gutter on west side of Bridge 16, Sunset Blvd.
September 29, 2011	Completed pouring Lateral Retaining Walls #6, #7, and #8 at Retaining Wall 1720.
October 14, 2011	Completed pouring footing for Bent 2 at Bridge 22, Mulholland Drive.
October 17, 2011	Began installation of Bent 2 Forms at Bridge 22, Mulholland Drive.
October 18, 2011	Began construction activities at Bridge 18, Bel Air Crest.
October 22, 2011	New Bridge 16, Sunset Blvd. South Side opened to vehicle traffic.
October 27, 2011	Completed pouring Abutment 1 at Bridge 22, Mulholland Drive.
November 1, 2011	Began demolition of Bridge 16 Sunset Blvd. north side.
November 7, 2011	Began installation of CIDH Piles for I-10 Connector.
November 9, 2011	Completed demolition of Bridge 16 Sunset Blvd. north side.
November 22, 2011	Received the VA License to Enter agreement.
November 22, 2011	Completed pouring Bridge 22 Mulholland OC Bent 2 Columns.
November 22, 2011	Completed pouring Bridge 5 Ohio NB Abutments 1 & 2.
December 1, 2011	MSE Wall 1897 along NB Sepulveda Blvd. south of Skirball Center Drive ruptures. Kiewit stops work on all MSE Walls throughout the project and begins investigation into MSE Wall deficiencies.
December 1, 2011	Began 2nd pouring of Bridge 22 Mulholland Abutment 1.
December 8, 2011	Completed subgrade for NM Connector.
December 17, 2011	Began installation of Precast Girders at Bridge 5A Ohio Ave.
December 19, 2011	Began installation of falsework beams for Bridge 15 Sunset on-ramp.

CHRONOLOGY OF EVENTS (Cont'd)

December 19, 2011	Began driving piles for Bridge 16 Sunset Blvd. Bent 3.
January 4, 2012	Began De-construction of MSE Wall 1738A.
January 9, 2012	Began De-construction of MSE Wall 1665.
January 16, 2012	Completed demolition of the I-405 median barrier at Mulholland Bridge and began erection of Falsework.
January 19, 2012	Began pouring footings for Soundwalls at Retaining Walls 1720 and 1730.
January 20, 2012	Completed pouring column # 1 @ Sunset Blvd. Bridge.
January 25, 2012	Began De-construction of MSE Wall 1634.
January 27, 2012	Kiewit stopped work on all Soil Nail Walls due to developing cracks, pending investigation.
January 31, 2012	Poured columns at Bel Air Crest Bridge.
February 13, 2012	Construction activities are started in Area 5 at Bridge 18 Getty Center UC and Bridge 19 Sepulveda UC.
February 15, 2012	De-construction of MSE Wall 1738A at Sunset NB Off-Ramp is completed.
February 18, 2012	Piers and Columns are poured for Bridge 16 Sunset Blvd.
February 18, 2012	LADWP completes installation of new underground cabling in ductbank along Sepulveda Blvd and Wilshire Ave. Final paving of Sepulveda trench is completed.
February 28, 2012	Kiewit submits notification to LACMTA that all remaining MSE Walls, with the exceptions of completed MSE Walls 1619 and 1942B will be de-constructed.
March 2, 2012	Full NB Freeway Closure at Mulholland Bridge to install Falsework Girders.
March 6, 2012	Caltrans identifies a potential Safety Concern during Mulholland Bridge Falsework Girder Installation on the SB Side and orders girders to be removed. Caltrans issues Stop Work Order pending review of Girder Installation Process.

CHRONOLOGY OF EVENTS (Cont'd)

March 8, 2012	Caltrans completes review of Girder Installation Process and authorizes resumption of installation of Falsework Girders at Mulholland Bridge. SB Side Falsework Girders are installed.
March 22, 2012	Concrete Girders are installed at Bridge 5B Ohio UC SB side.
April 7, 2012	Kiewit completes installation of Mulholland Bridge (South Side) Sheet Decking and begins installation of structural rebar.
April 10, 2012	Kiewit resumes construction of MSE Walls. Construction of Wall 1672 new leveling pad is started.
April 14, 2012	Kiewit begins installation of top deck and diaphragm structural rebar at Bridge 4Santa Monica UC.
April 20, 2012	Kiewit pours concrete top deck, curb, and gutter at Bridge 9 Wilshire UC.
May 1, 2012	Begin installation of Concrete girders at Bridge 16 Sunset OC North Side.
May 4, 2012	Kiewit resumes construction of MSE Walls using an approved new Wall Panel Vendor and Construction Plan. Construction begins at MSE Wall 1672 along Sepulveda Blvd. north of Wilshire Blvd.
May 4, 2012	Completion of installation of Concrete Girders at Bridge 16 Sunset OC North Side.
May 18, 2012	Construction of MSE Wall 1808 along Sepulveda Blvd. north of Getty Center Drive is started using new Wall Panels and Construction Plan.
May 24, 2012	Structural construction is started within the GSA Property. Construction of Bridge 7 Bent 3 is started.
May 31, 2012	Construction of MSE Wall 1686 along Sepulveda Blvd. north of Constitution Drive is started using new Wall Panels and Construction Plan.

CHRONOLOGY OF EVENTS (Cont'd)

June 2, 2012	NW1 Ramp from WB I-10 to NB I-405 is opened for traffic.
June 6, 2012	GSA Microwave Security System is installed.
June 7, 2012	Bridge 7 NB I-405 to EB Wilshire Off-ramp Columns for Bents 3 and 4 are constructed on GSA Property.
June 22, 2012	90-Day Shutdown of Bridges 10 & 11 NB I-405 to WB Wilshire and WB Wilshire to NB I-405 commenced.
June 27, 2012	Demolition of existing Bridges 10 & 11 is completed.
July 15, 2012	Bridge 21 Skirball Center Drive, North side, is opened to traffic.
July 20, 2012	Bridge 22 Mulholland Drive, Top Deck is poured.
July 21, 2012	Bridges 10 & 11 Pre-cast Girders are installed.
July 30, 2012	Bridge 21 Skirball Center Drive, South Side, Demolition is started.
August 3, 2012	Bridge 21 Skirball Center Drive, South Side, Demolition is Completed.
August 10, 2012	Bridges 10 & 11 Top Deck is Poured.
August 23, 2012	Bridge 16 Sunset Blvd. Top Deck is Poured.
August 31, 2012	Bridges 10 & 11 are Opened for Traffic.
September 4, 2012	Bridge 7 Falsework installation begins.
September 24, 2012	Bridge 16 is fully opened for traffic.
September 24, 2012	Bridge 22 South Side is opened for traffic.
September 28, 2012	Began demolition of the north side of Mulholland Bridge 22.
September 30, 2012	Complete demolition of the north side of Mulholland Bridge 22.
October 1, 2012	Began construction activities for Bridge 17, Church Lane UC.

CHRONOLOGY OF EVENTS (Cont'd)

October 1, 2012	Began construction activities for Bridge 22, Mulholland OC north side.
October 15, 2012	MSE Wall 1897 reconstruction is completed.
October 19, 2012	Bridge 15 Sunset NB On-ramp, top deck is poured.
October 23, 2012	RW 1720 punch list work begins.
November 4, 2012	Re-aligned Sepulveda Blvd. to the east at Bronwood Apartments.
November 6, 2012	Begin construction activities for Bridge 14 Sunset NB Off-ramp.
November 8, 2012	Bridges 6A and 6B SB Off-ramp to EB Wilshire abutments poured.
November 28, 2012	Completed re-striping and realignment of Sepulveda Blvd. to the east at walls 1720 & 1730.
November 29, 2012	Completed pouring Top Deck at Bridge 1 I-10 Connector.
December 4, 2012	Completed installation of Pre-Cast Girders at Bridge 2 Exposition.
December 6, 2012	Sepulveda Blvd. is restriped and realigned from Montana Avenue to Bridge 14 NB Sunset Off-Ramp.
December 20, 2012	Completed pouring Top Deck at Bridge 18 Getty Center Drive NB and SB.
December 21, 2012	Completed girder installation at Bridge 6A and 6B SB Wilshire Off-Ramp.
January 4, 2013	False work for Bridge 7 is completed allowing construction of CIP Box Girder to progress from abutment to abutment.
January 4, 2013	Completed installation of 10' diameter CIDH Piles for Bridge 14 Construction of foundation piles is started.
January 15, 2013	Completed pouring outside stems for Bridge 8.

CHRONOLOGY OF EVENTS (Cont'd)

January 23, 2013	Completed installation of top deck metal decking for Bridge 6A.
February 3, 2013	Opened new SB 405 On-ramp from Skirball Center Drive.
February 11, 2013	Began installation of Falsework for Mulholland Bridge north side.
February 21, 2013	Opened new SB 405 On-ramp from EB Wilshire Blvd.
February 22, 2013	Opened new NB 405 On-ramp from Cotner Ave. at Olympic Blvd.
March 8, 2013	Began 14-day closure of SB I-405 to WB Wilshire Off-ramp to allow construction of new Off-ramp.
March 16, 2013	Completed construction of new SB I-405 to WB Wilshire Off-ramp and re-opened the Off-ramp 6 days early.
March, 22, 2013	Began forming bottom deck of north side of Bridge 22, Mulholland OC.
March 25, 2013	Opened new Bridge 1, I-10 EB to I-405 NB, and began demolition of existing Bridge 2 Span 4 to Abutment 9.
April 6, 2013	Completed paving on NB side of I-10 to I-405 Interchange Area.
April 9, 2013	Completed Bridge 22, Mulholland Dr. OC, Falsework installation.
April 18, 2013	Completed Bridge 7, NB 405 to EB Wilshire Off-ramp, Top Deck installation.
May 3, 2013	Completed NB I-405 paving activities in the Santa Monica Area.
May 23, 2013	Change Order 105.00 is issued extending the Substantial Completion Deadline by 149 days to October 27, 2013.
May 24, 2013	General Purpose Lane opened in Segment 1 from the I-10 to the Santa Monica Area.
May 30, 2013	Began removal of Falsework at Bridge 7 NB I-405 to EB Wilshire Off-ramp.

CHRONOLOGY OF EVENTS (Cont'd)

June 11, 2013	Additional NB General Purpose Lane is opened to traffic from Santa Monica Blvd. to Wilshire Blvd.
June 20, 2013	Completed work on Bridge 7, NB 405 to EB Wilshire Off-ramp.
June 21, 2013	Completed installation of girders on Bridge 21, Skirball Center Drive OC.
June 22, 2013	Bridge 15, Sunset Blvd. to NB 405 On-ramp, opened to traffic.
June 26, 2013	Bridge 7, NB 405 to EB Wilshire Off-ramp, opened to traffic.
June 29, 2013	Bridge 22, Mulholland OC, completed pouring Top Deck.
July 3, 2013	Bridge 7, NB 405 to EB Wilshire Off-ramp, demolition of existing bridge is completed.
July 18, 2013	Bridge 22, Mulholland OC, Falsework removal is started.
July 30, 2013	Area 2, Santa Monica Area, Median paving is completed.
August 2, 2013	Bridge 14 Sunset NB Off-ramp, 120-Day Closure Window begins.
August 4, 2013	Bridge 14 Sunset NB Off-ramp, Demolition of existing bridge is completed.
August 15, 2013	Bridge 17 Sepulveda UC, Top Deck concrete is poured.
August 22, 2013	Bridge 8 EB Wilshire to NB 405 On-ramp, 90-Day Closure Window begins.
August 22, 2013	Bridge 8 EB Wilshire to NB 405 On-ramp, Demolition of existing bridge is completed.
Sept. 12, 2013	Bridge 14 Sunset Off-ramp, steel girder installation over Sepulveda Blvd. is started.
Sept. 14, 2013	SB I-405 to Valley Vista Off-ramp to EB Wilshire, new Off-ramp is opened to traffic.
Sept. 23, 2013	Bridge 6A and 6B SB I-405 Off-ramp to EB Wilshire, new Off-ramp is opened to traffic.

CHRONOLOGY OF EVENTS (Cont'd)

Sept. 24, 2013	Bridge 14 Sunset Off-ramp, steel girder installation over Sepulveda Blvd. is completed.
Sept. 30, 2013	SB I-405 to Skirball Center Drive Off-ramp, new Off-ramp is opened to traffic.
October 7, 2013	Bridge 8 EB Wilshire Blvd. to NB I-405 On-ramp, top deck and barrier concrete pour completed.
October 8, 2013	Bridge 2 Exposition Avenue UC, top deck concrete pour completed.
October 25, 2013	Bridge 23 Sepulveda Blvd. UC, top deck concrete pour completed.
October 26, 2013	Bridge 21Skirball Center Dr. OC, top deck concrete pour completed.
October 30, 2013	Bridge 8 EB Wilshire Blvd. to NB On-ramp falsework removed.
November 2, 2013	SB I-405 On-ramp from EB Wilshire Blvd. is opened to full capacity traffic.
November 17, 2013	Bridge 8 EB Wilshire Blvd. to NB I-405 On-ramp is opened to traffic. 90-day closure window is ended.
November 23, 2013	Bridge 14 I-405 NB Off-ramp to Sunset Blvd. Falsework is removed.
November 24, 2013	Bridge 21 Skirball Center Drive OC falsework is removed.
November 25, 2013	Bridge 14 I-405 Off-ramp to Sunset Blvd. is opened to traffic. 120-day closure window is ended.
December 14, 2013	Bridge 17 Church Lane UC, Top Deck Concrete is poured.
December 17, 2013	RW 1720 & 1730, Shotcrete installation is completed.
December 18, 2013	Bridge 22, Mulholland OC, Bridge is opened to full traffic capacity.
December 23, 2013	Bridge 2, Exposition UC, Bridgework is completed.

CHRONOLOGY OF EVENTS (Cont'd)

January 7, 2014	RW 1730, artwork installation is started.
January 21, 2014	Bridge 21 Skirball Center drive, approach slabs completed.
January 23, 2014	Bridge17 Church Lane, approach slabs completed.
January 24, 2014	Bridge 19 Sepulveda Blvd., bridge work completed.
February 4, 2014	Bridge 23, Sepulveda Blvd., bridge work completed.
February 14, 2014	80-hour lane reduction begins.
February 18, 2014	80-hour lane reduction ends.
February 18, 2014	Area 5-7 median barrier installation and AC grind and overlay, planned during 80-hour lane reduction, completed.
March 4, 2014	Getty Center North Canyon Road Construction begins with drainage system installation.
March 5, 2014	Walls 1720 and 1730 Artwork stenciling completed.
March 12, 2014	Area 6 Skirball Center NB I-405 traffic switched to new median lane.
March 15, 2014	Area 4 Sepulveda Blvd. SB paving replacement from Montana Avenue tor Church Lane begins.
March 21, 2014	Bridge 21, Skirball Center Dr., additional lane, total of 2 SB lanes and 1 NB Lane, opened to traffic.
April 11, 2014	Bridge 9, NB I10 to Wilshire Blvd. HOV Lane opened to traffic.
April 28, 2014	NB I-405 I-10 to Wilshire Blvd. HOV Lane opened to traffic.
May 23, 2014	NB I-405 HOV Lane fully opened to traffic.
May 31, 2014	SB I-405 General Purpose Lanes from Getty Center to Wilshire Area, paving and permanent delineation completed.
June 1 , 2014	Area 4 Sunset, Mainline K-rail removal completed.
June 1, 2014	Area 5 Sepulveda, Mainline Pavement grind and overlay and K-rail removal completed.

CHRONOLOGY OF EVENTS (Cont'd)

June 25, 2014	Area 7, Valley Vista, cul-de-sac paving completed.
July 3, 2014	SB I-405 final lane configuration completion.
July 10, 2014	Wall 1746 slope paving completed.
July 11, 2014	Walls 1720 and 1730 slope paving stain completed.
July 16, 2014	Area 2 LABSL lighting final inspection completed.
August 12, 2014	Slope stabilization behind Wall 2011 begins.
August 18, 2014	GSA anti-climb fence installation begins.
August 30, 2014	SB Sepulveda from Skirball Center Drive to Mountaingate Drive paving and striping completed.
September 12, 2014	GSA Anti-Climb Fence installation completed.
September 28, 2014	Right-turn lanes at SB Skirball Center Drive On and Off Ramps completed.
October 11, 2014	Segment 1 landscaping work completed.
October 18, 2014	Area 4 and Area 7 preliminary punchlist work begins.
October 23, 2014	Area 6 preliminary punchlist work begins.
October 24, 2014	Area 5 preliminary punchlist work begins.
November 10, 2014	.Segment 3 landscape punchlist work begins.
November 14, 2014	Area 1 landscape punchlist completed.
November 14, 2014	Segment 2 landscape punchlist work completed.
November 20, 2014	Area 6 Mulholland West Area punchlist work begins.
December 6, 2014	Area 4 Sunset/Sunset cul-de-sac ADA ramps completed.
December 10, 2014	Area 2 Ohio and Cotner ADA ramps completed.
December 20, 2014	Area 3 ADA ramps completed.

CHRONOLOGY OF EVENTS (Cont'd)

January 12, 2015	Retaining Wall 2011 slope stabilization work begins.
February 2, 2015	Retaining Wall 2011 slope stabilization work completed.
March 13, 2015	Retaining Wall 2004 substandard barrier repair work begins.
June 26, 2015	Kiewit files Application for Substantial Completion.

APPENDICES

COST AND BUDGET TERMINOLOGY

APPROVED BUDGET: The Approved Project Budget as established by Metro Board of Directors at the time it authorizes Construction Project Management Division to commence full design and construction of the project (Project Adoption).

CURRENT BUDGET: The Original Budget plus all budget amendments approved by formal Metro action. Also referred to as Approved Budget.

CURRENT FORECAST: Evaluation of costs to go combined with actual expenditures.

COMMITMENTS: The total of actual contract awards, executed change orders or amendments, approved work orders of Master Cooperative Agreements, offers accepted for purchase of real estate, and other Metro actions which have been spent or result in the obligation of specific expenditures at a future time.

EXPENDITURES: The total dollar amount of funds expended by Metro for contractor or consultant invoices, third party invoices, staff salaries, real estate and other expenses that is reported in Metro's Financial Information System (FIS).

PROJECT APPROVAL & ENVIRONMENTAL DOCUMENTS: Costs for agency staff and consulting contracts leading to project approval and environmental clearances.

PLANS, SPECS. & ENGINEERING: Agency staff and consulting contract costs between the initial project approval and environmental clearances but prior to start of construction.

RIGHT-OF-WAY SUPPORT: Costs for agency staff involved in real estate appraisal and parcel purchase activities and agency staff costs involved in utility relocations and third party agreements. Includes real estate appraisal costs.

CONSTRUCTION SUPPORT: Agency staff and consulting contract costs occurring during the construction phase of the project.

CONSTRUCTION: Costs for highway construction, bridge and on/off ramp construction and modifications, retaining wall and sound wall construction. Includes final design costs by Design/Build Contractor.

RIGHT-OF-WAY CAPITAL: Costs for real estate parcel purchases and utility relocations costs after approval of utility company agreements. Includes costs for Master Cooperative Agreements after approval by agencies.

APPENDIX

LIST OF ACRONYMS

ARRA	American Recovery & Reinvestment Act
AWIS	Automated Work Zone Information Systems
CADD	Computer Aided Drafting and Design
CALTRANS	California Department of Transportation
CCTV	Closed Circuit Television
CD	Calendar Day
CDFG	California Department of Fish and Game
CEQA	California Environmental Quality Act
CM	Construction Manager
CMAC	Congestion Mitigation Air Quality
CMIA	Cash Management Improvement Act
CMS	Changeable Message Signs
CN	Change Notice
CO	Change Order
COE	Corps of Engineers
COLA	City Of Los Angeles
CPM	Critical Path Method
CPUC	California Public Utilities Commission
CR	Camera Ready
CTC	California Transportation Commission
D-B	Design-Build
D-B-B	Design-Bid-Build
DD	Design Development
DEIR	Draft Environmental Impact Report
DR	Deficiency Report
DWP	Department of Water and Power
EIR	Environmental Impact Report
EIS	Environmental Impact Statement
FD	Final Design
FEIR	Final Environmental Impact Report
FHWA	Federal Highway Administration
FIS	Financial Information System
FOCT	Fiber Optics Cable Transmission System
FTE	Full Time Equivalent
GDSR	Geotechnical Design Summary Report
GSA	General Services Administration
GSRD	Gross Solids Removal Devices
HAR	Highway Advisory Radio
HOV	High Occupancy Vehicle
IFB	Invitation for Bid
IPO	Integrated Project Office
ITS	Intelligent Transportation Systems

APPENDIX

LIST OF ACRONYMS (Continued)

LA	Los Angeles
LABOE	Los Angeles Bureau of Engineering
LACFCD	Los Angeles County Flood Control District
LADOT	Los Angeles Department of Transportation
LADPW	Los Angeles Department of Public Works
LADWP	Los Angeles Department of Water and Power
LARTMC	Los Angeles Regional Transportation Management Center
LFAT	Local Field Acceptance Test
LNTP	Limited Notice To Proceed
LONP	Letter Of No Prejudice
LOP	Life of Project
MCA	Master Cooperative Agreement
METRO	Los Angeles County Metropolitan Transportation Authority
MIS	Major Investment Study
MOT	Maintenance of Traffic
MPSR	Monthly Project Status Report
MSE	Mechanically Stabilized Earth
MVDS	Microwave Vehicle Detection System
MVP	Maintenance Vehicle Pullouts
MWD	Metropolitan Water District
N/A	Not Applicable
NCR	Non-Conformance Report
NEPA	National Environmental Quality Act
NHS	National Highway System
NOA	Notice of Award
NTE	Not to Exceed
NTP	Notice To Proceed
NTSC	National Television System Committee
P6	Primavera Project Planner® (scheduling software)
PC	Project Control
PE	Preliminary Engineering
PIP	Project Implementation Plan
PM	Project Manager
PMA	Project Management Assistance
PMP	Project Management Plan
P&P	Policies & Procedures
PR	Project Report
PS&E	Plans, Specs & Engineering
PSR	Project Study Report
QA	Quality Assurance
QAR	Quality Assurance Report

APPENDIX

LIST OF ACRONYMS (Continued)

QC	Quality Control
QPSR	Quarterly Project Status Report
RFC	Request For Change or Released for Construction (based on context)
RFP	Request For Proposal
RMS	Ramp Metering Systems
ROM	Rough Order of Magnitude
ROW	Right-Of-Way
SIT	System Integration Testing
RSTP	Regional Surface Transportation Program
RWQCB	Regional Water Quality Control Board
SAFETEA-LU	Safe, Accountable, Flexible, Efficient Transportation Equity Act: A Legacy for Users
SCE	Southern California Edison
SONET	Synchronous Optical Network
SOV	Schedule Of Value
SOW	Statement Of Work
SP	Special Provision
TBD	To Be Determined
TCRP	Traffic Congestion Relief Program
TMS/CS	Traffic Monitoring Stations/Count Stations
TPM	Transportation Management Plan
VE	Value Engineering
WBS	Work Breakdown Structure
WP	Work Package
