


I-405 Sepulveda Pass Widening Project

Community Advisory Committee Meeting

February 25, 2010



Project Approach

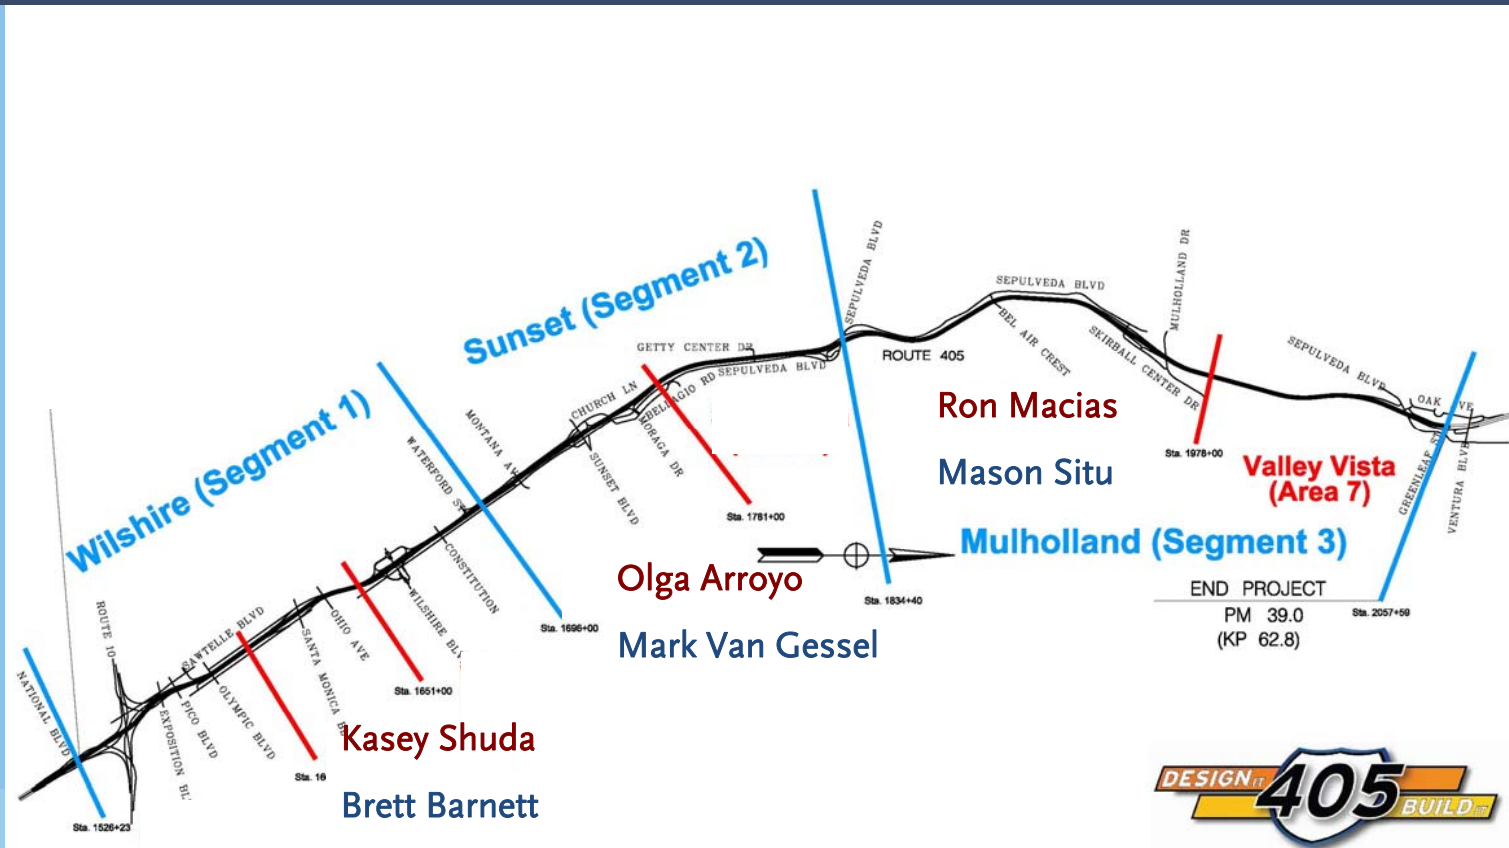

Three-Month Look Ahead Mainline

Activity	Closures/Notes	Work Hours	Projected Date
Striping (reconfigure lanes) <i>except S/B between 101 and The Getty Center</i>	<ul style="list-style-type: none"> • Full segmented freeway closures • Traffic detours • Lane reductions 	Night	Through mid-March
Saw cut and grinding	<ul style="list-style-type: none"> • Lane reductions • Traffic detours 	Night	February 16 – early April
K rail placement (in sections)	<ul style="list-style-type: none"> • Lane reductions • Ramp closures 	Night	March 1

Wilshire and Sunset ramps will not be closed at the same time.



Full Freeway Closure Schedule

Activity	Segment	Projected Date *	Anticipated Duration	Description
K-rail Placement - Northbound I-405 Partial Freeway Closures	I-10 to Santa Monica Blvd.	3/2010	TBA	Partial Freeway Closure
Freeway Restriping - Southbound I-405 Full Freeway Closures	Santa Monica Blvd. to National Blvd.	3/3/2010	Three Nights	Full Freeway Closure: Detour in Place
Freeway Restriping - Southbound I-405 Full Freeway Closures	Sunset Blvd. to Santa Monica Blvd.	3/6/2010	Two Nights	Full Freeway Closure: Detour in Place
Freeway Restriping - Southbound I-405 Partial Freeway Closures	Skirball Center Dr. to Wilshire Blvd	3/9/2010	Two Nights	HOV, #1, #2
Freeway Restriping - Southbound I-405 Full Freeway Closures	Valley Vista Blvd. to Bel Air Crest Rd.	3/11/2010	Two Nights	Full Freeway Closure: Detour in Place

* Weather permitting



Five-Week Look Ahead

Wilshire Segment (National to Waterford)

Activity	Closures/Notes	Work Hours	Projected Date
Development of Wilshire Yard		Day	Through mid-March
Move in to Wilshire yard		Day	Mid-March
Clear Wilshire on/off ramps (west side)		Day	Mid-March
Build MSE walls S/B I-405 at Wilshire	Possible night work for dirt hauling	Day	Mid-March
VA Sewer Relocation	Lane closures on Bonsall Road (VA property)	Day	Late March through mid-June




Five-Week Look Ahead

Wilshire Segment (Continued)

Activity	Closures/Notes	Work Hours	Projected Date
Development of Wilshire Yard		Day	Through mid-March
Move in to Wilshire yard		Day	Mid-March
Clear Wilshire on/off ramps (west side)		Day	Mid-March




Wilshire Segment Map

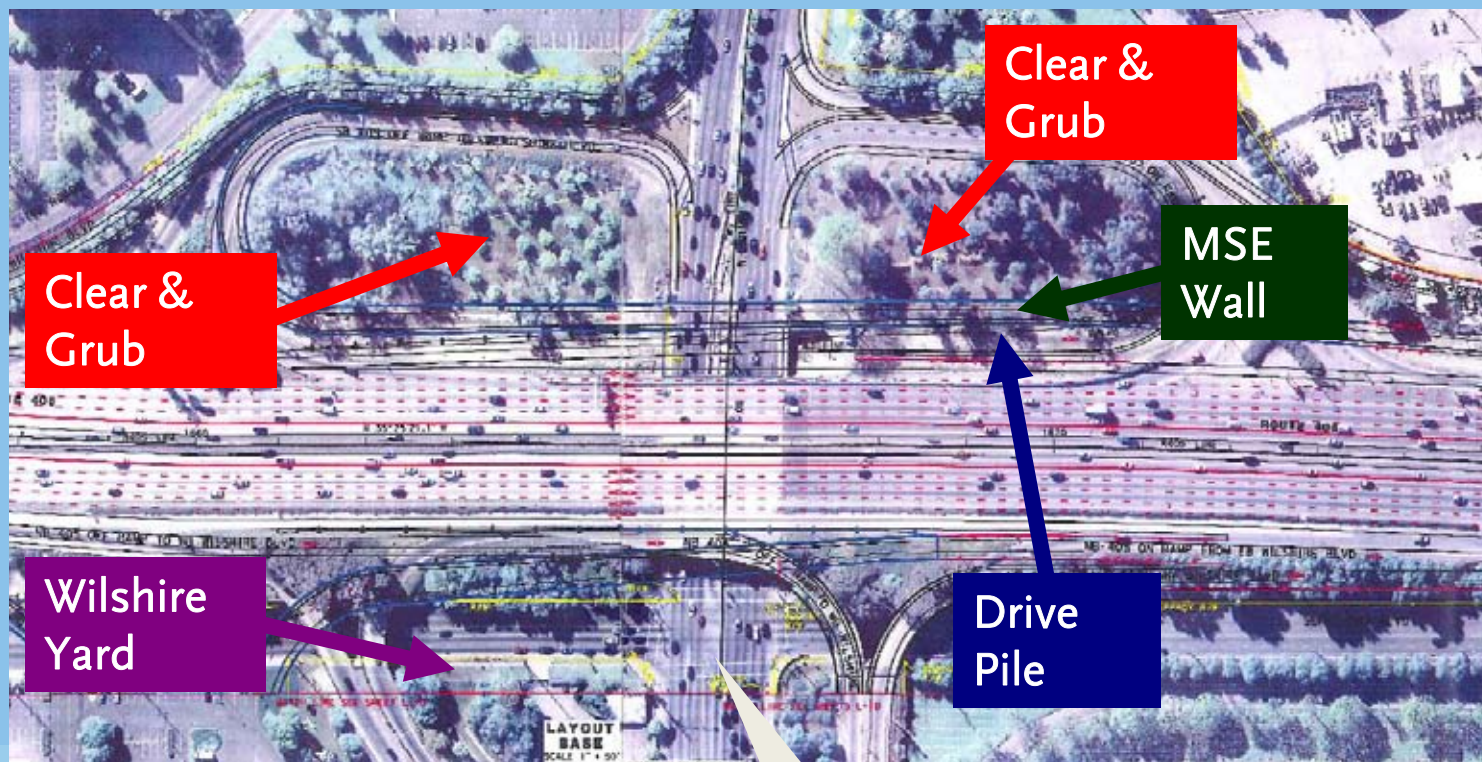

Wilshire
Blvd.



Wilshire Yard Layout

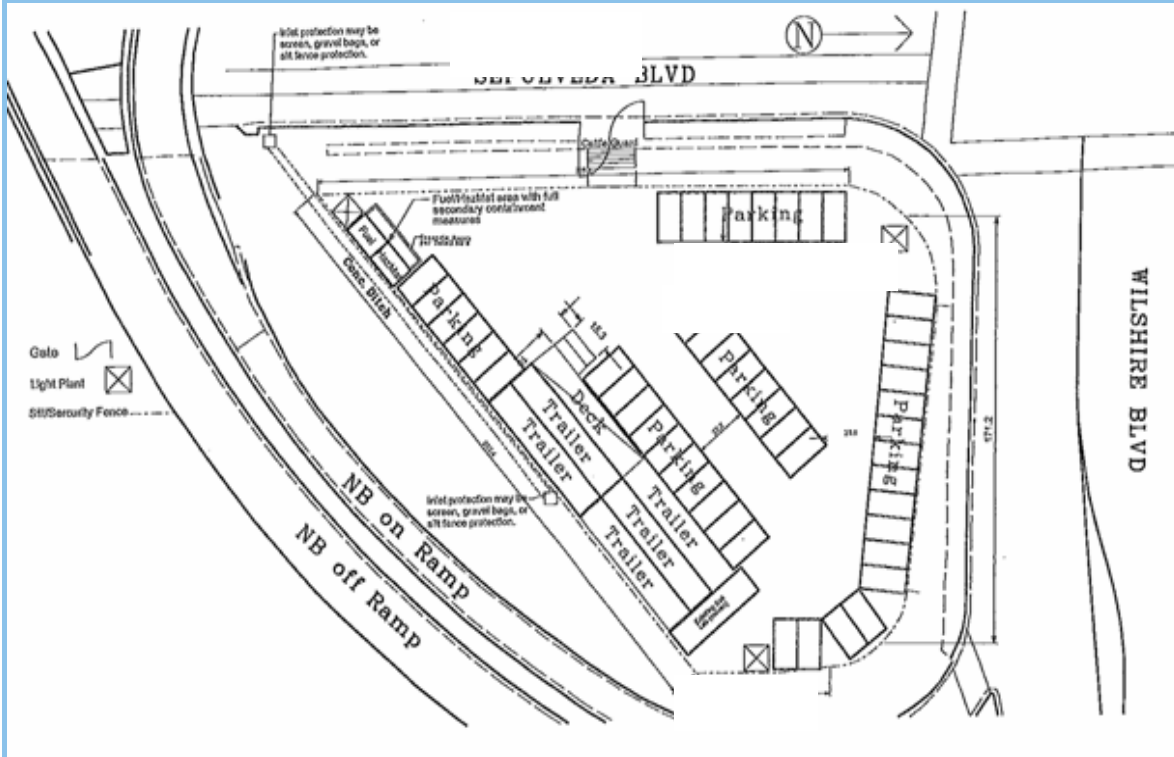

- Caltrans owned property
- Clear vegetation
- Fence area
- Pave space
- Set up field offices

Five-Week Look Ahead

Sunset Segment (Waterford to Sepulveda)

Location	Activity	Closures/Notes	Work Hours	Projected Date
Between Montana and Sunset	Undergrounding utilities	Lane reduction during off-peak hours. Closure of Sepulveda Intersection at Homedale, Bronwood and Alleyway.	Day/Night	March
	Clear hillside (shrubs) Phase I	Lane reduction	Day	Early March
	Build access		Day	Late March
	Clear hillside (trees) Phase II	Lane reduction	Day	May
	Begin retaining and sound walls		Day/Night	May



Five-Week Look Ahead

Sunset Segment (Continued)

Location	Activity	Closures/Notes	Work Hours	Projected Date
Sunset bridge*	Clear on/off ramps	Lane closures	Day/Night	March
	Realign traffic	Traffic reconfiguration (two lanes in each direction) Lane closures	Night	March
	Begin Sunset bridge demolition *	Traffic delays Lane reduction	Day/Night	Late March
	Yard Development		Day	March

* Construction Alternatives



Five-Week Look Ahead

Mulholland Segment (Sepulveda to 101 Highway)

Area	Activity	Closures/Notes	Work Hours	Projected Date
Getty Trail Head	Clear and grub, crusher pad setup	No residents within impacted perimeter.	Day	March
Mission Land Fill	Site office set up	Traffic in/out from site office. Will re-stripe Sepulveda Blvd. to provide NB left-turn pocket into the site.	Day	March



Pre-Construction Surveys

- Survey purpose
- Criteria
- Security of information

*To schedule an appointment contact
Morgner Construction at 818-461-8100*



Landscape

- Overview
- Trees selected



Jacaranda Mimosaifolia



Stomemia

Landscape (Continued)



- Removal of the Washingtonia Palm Tree
- Phoenix Dactylifera

The End

Metro Community Relations

Project Hotline: (213) 922-3665

I405@metro.net

www.metro.net/405

Twitter: http://twitter.com/I_405

Nixle: nixle.com

